ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
0	**FiberTel Network U**	**203.5 hrs**	**0 hrs**	**203.5 hrs**	**0 hrs**	**203.5 hrs**	**0%**
1	**1 Initiate**	**16.5 hrs**	**0 hrs**	**16.5 hrs**	**0 hrs**	**16.5 hrs**	**0%**
2	1.1 Sponsor mee	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
3	1.2 Develop Proj	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%
4	1.3 Review and A	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%
5	**1.4 Kickoff meet**	**4 hrs**	**0 hrs**	**4 hrs**	**0 hrs**	**4 hrs**	**0%**
6	1.4.1 Sit dowr	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
7	1.4.2 Site visit	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
8	1.5 Develop a Pr	2.5 hrs	0 hrs	2.5 hrs	0 hrs	2.5 hrs	0%
9	**2 Plan Project**	**42.5 hrs**	**0 hrs**	**42.5 hrs**	**0 hrs**	**42.5 hrs**	**0%**
10	**2.1 Design**	**12.5 hrs**	**0 hrs**	**12.5 hrs**	**0 hrs**	**12.5 hrs**	**0%**
11	2.1.1 Measure	1 hr	0 hrs	1 hr	0 hrs	1 hr	0%
12	2.1.2 Check cc	1.5 hrs	0 hrs	1.5 hrs	0 hrs	1.5 hrs	0%
13	2.1.3 Design C	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%
14	2.1.4 Calculat	1 hr	0 hrs	1 hr	0 hrs	1 hr	0%
15	2.1.5 Obtain c	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
16	2.1.6 Design F	1 hr	0 hrs	1 hr	0 hrs	1 hr	0%
17	2.1.7 Designat	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
18	**2.2 Procuremen**	**15 hrs**	**0 hrs**	**15 hrs**	**0 hrs**	**15 hrs**	**0%**
19	2.2.1 Contact	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
20	2.2.2 Obtain c	8 hrs	0 hrs	8 hrs	0 hrs	8 hrs	0%
21	**2.2.3 Procure**	**2.5 hrs**	**0 hrs**	**2.5 hrs**	**0 hrs**	**2.5 hrs**	**0%**
22	2.2.3.1 Proc	0.5 hrs	0 hrs	0.5 hrs	0 hrs	0.5 hrs	0%

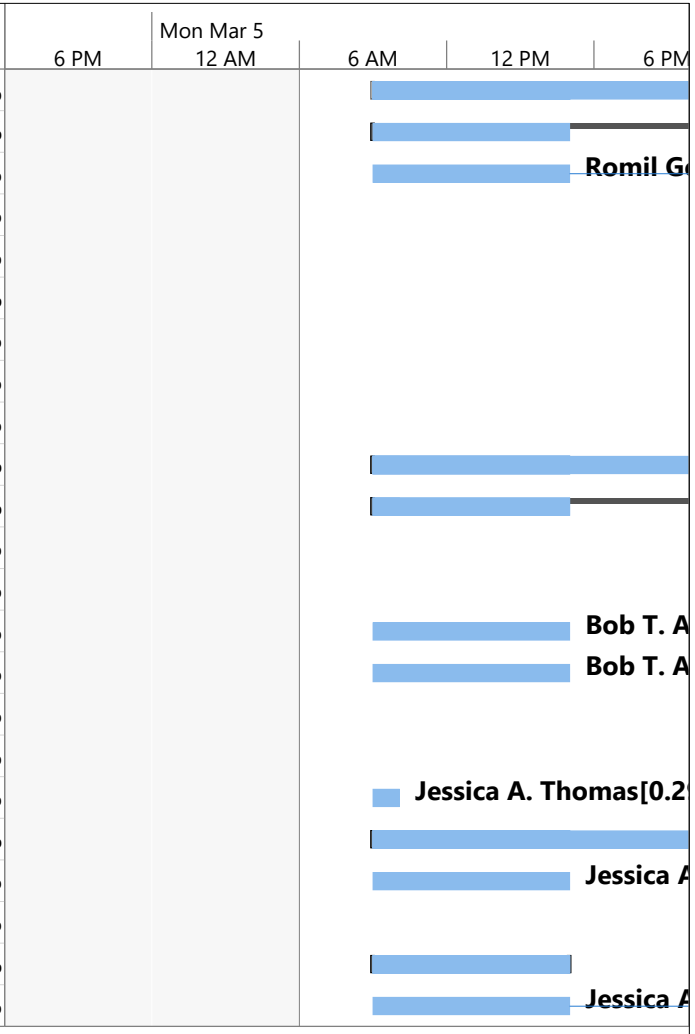

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		

ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
23	2.2.3.2 Proc	0.5 hrs	0 hrs	0.5 hrs	0 hrs	0.5 hrs	0%
24	2.2.3.3 Proc	0.5 hrs	0 hrs	0.5 hrs	0 hrs	0.5 hrs	0%
25	2.2.3.4 Proc	0.5 hrs	0 hrs	0.5 hrs	0 hrs	0.5 hrs	0%
26	2.2.3.5 Proc	0.5 hrs	0 hrs	0.5 hrs	0 hrs	0.5 hrs	0%
27	2.2.4 Procure	1.5 hrs	0 hrs	1.5 hrs	0 hrs	1.5 hrs	0%
28	2.2.5 Procure	1 hr	0 hrs	1 hr	0 hrs	1 hr	0%
29	**2.3 Receive Mat**	**15 hrs**	**0 hrs**	**15 hrs**	**0 hrs**	**15 hrs**	**0%**
30	2.3.1 Receive	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
31	2.3.2 Receive	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
32	2.3.3 Receive	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%
33	2.3.4 Check qu	2.5 hrs	0 hrs	2.5 hrs	0 hrs	2.5 hrs	0%
34	2.3.5 Check qu	2.5 hrs	0 hrs	2.5 hrs	0 hrs	2.5 hrs	0%
35	**3 Execute Project**	**89.5 hrs**	**0 hrs**	**89.5 hrs**	**0 hrs**	**89.5 hrs**	**0%**
36	3.1 Clean the wo	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
37	3.2 Remove unn	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
38	**3.3 Furniture Ins**	**16 hrs**	**0 hrs**	**16 hrs**	**0 hrs**	**16 hrs**	**0%**
39	3.3.1 Install Ca	8 hrs	0 hrs	8 hrs	0 hrs	8 hrs	0%
40	3.3.2 Install Fu	8 hrs	0 hrs	8 hrs	0 hrs	8 hrs	0%
41	**3.4 Equipment I**	**27.5 hrs**	**0 hrs**	**27.5 hrs**	**0 hrs**	**27.5 hrs**	**0%**
42	3.4.1 Install 10	10 hrs	0 hrs	10 hrs	0 hrs	10 hrs	0%
43	3.4.2 Install re	5 hrs	0 hrs	5 hrs	0 hrs	5 hrs	0%
44	3.4.3 Install 10	5 hrs	0 hrs	5 hrs	0 hrs	5 hrs	0%
45	3.4.4 Install sp	1.5 hrs	0 hrs	1.5 hrs	0 hrs	1.5 hrs	0%

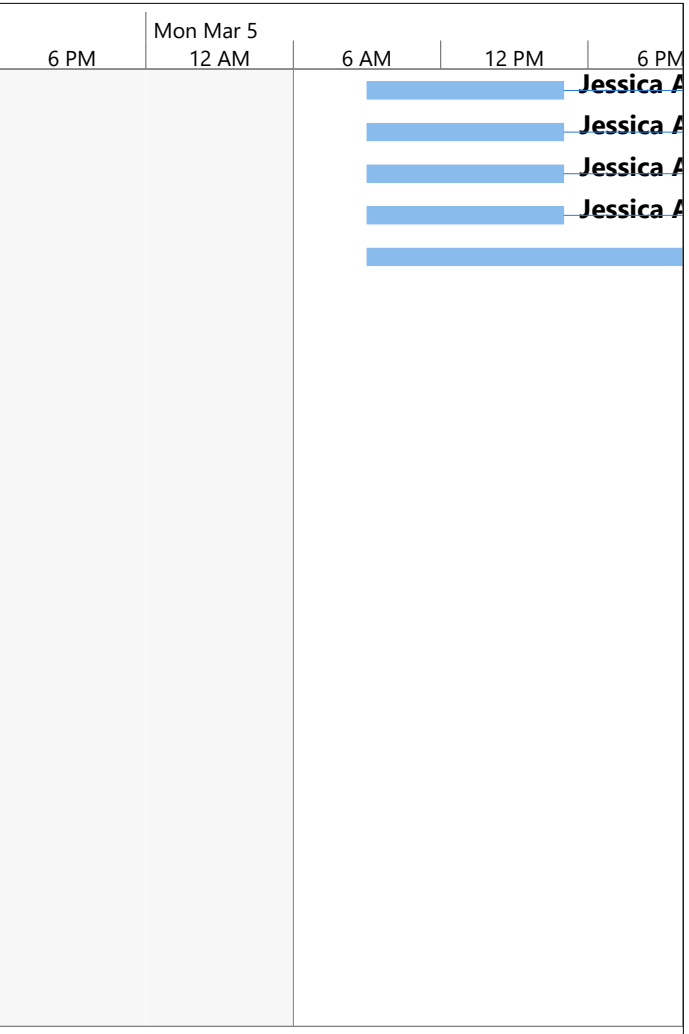

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
46	3.4.5 Install C	1 hr	0 hrs	1 hr	0 hrs	1 hr	0%
47	3.4.6 Install 2	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%
48	3.4.7 Install Li	1 hr	0 hrs	1 hr	0 hrs	1 hr	0%
49	**3.5 Connect Inst**	**12 hrs**	**0 hrs**	**12 hrs**	**0 hrs**	**12 hrs**	**0%**
50	3.5.1 Connect	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
51	3.5.2 Connect	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
52	3.5.3 Connect	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
53	3.5.4 Connect	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
54	3.5.5 Connect	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
55	3.5.6 Connect	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
56	**3.6 Configure an**	**29 hrs**	**0 hrs**	**29 hrs**	**0 hrs**	**29 hrs**	**0%**
57	3.6.1 Configur	15 hrs	0 hrs	15 hrs	0 hrs	15 hrs	0%
58	3.6.2 Configur	6 hrs	0 hrs	6 hrs	0 hrs	6 hrs	0%
59	3.6.3 Configur	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
60	3.6.4 Test cab	5 hrs	0 hrs	5 hrs	0 hrs	5 hrs	0%
61	**4 Close Out Projec**	**55 hrs**	**0 hrs**	**55 hrs**	**0 hrs**	**55 hrs**	**0%**
62	4.1 Develop fina	40 hrs	0 hrs	40 hrs	0 hrs	40 hrs	0%
63	**4.2 Gain sponso**	**5 hrs**	**0 hrs**	**5 hrs**	**0 hrs**	**5 hrs**	**0%**
64	4.2.1 Visit site	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
65	4.2.2 Review c	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
66	**4.3 Analyze proj**	**6 hrs**	**0 hrs**	**6 hrs**	**0 hrs**	**6 hrs**	**0%**
67	4.3.1 Conduct	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%
68	4.3.2 Conduct	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%



Project: FiberTel Network Upgr
Date: Mon 11/13/17



ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
69	4.4 Reassign res	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%



Project: FiberTel Network Upgr
Date: Mon 11/13/17



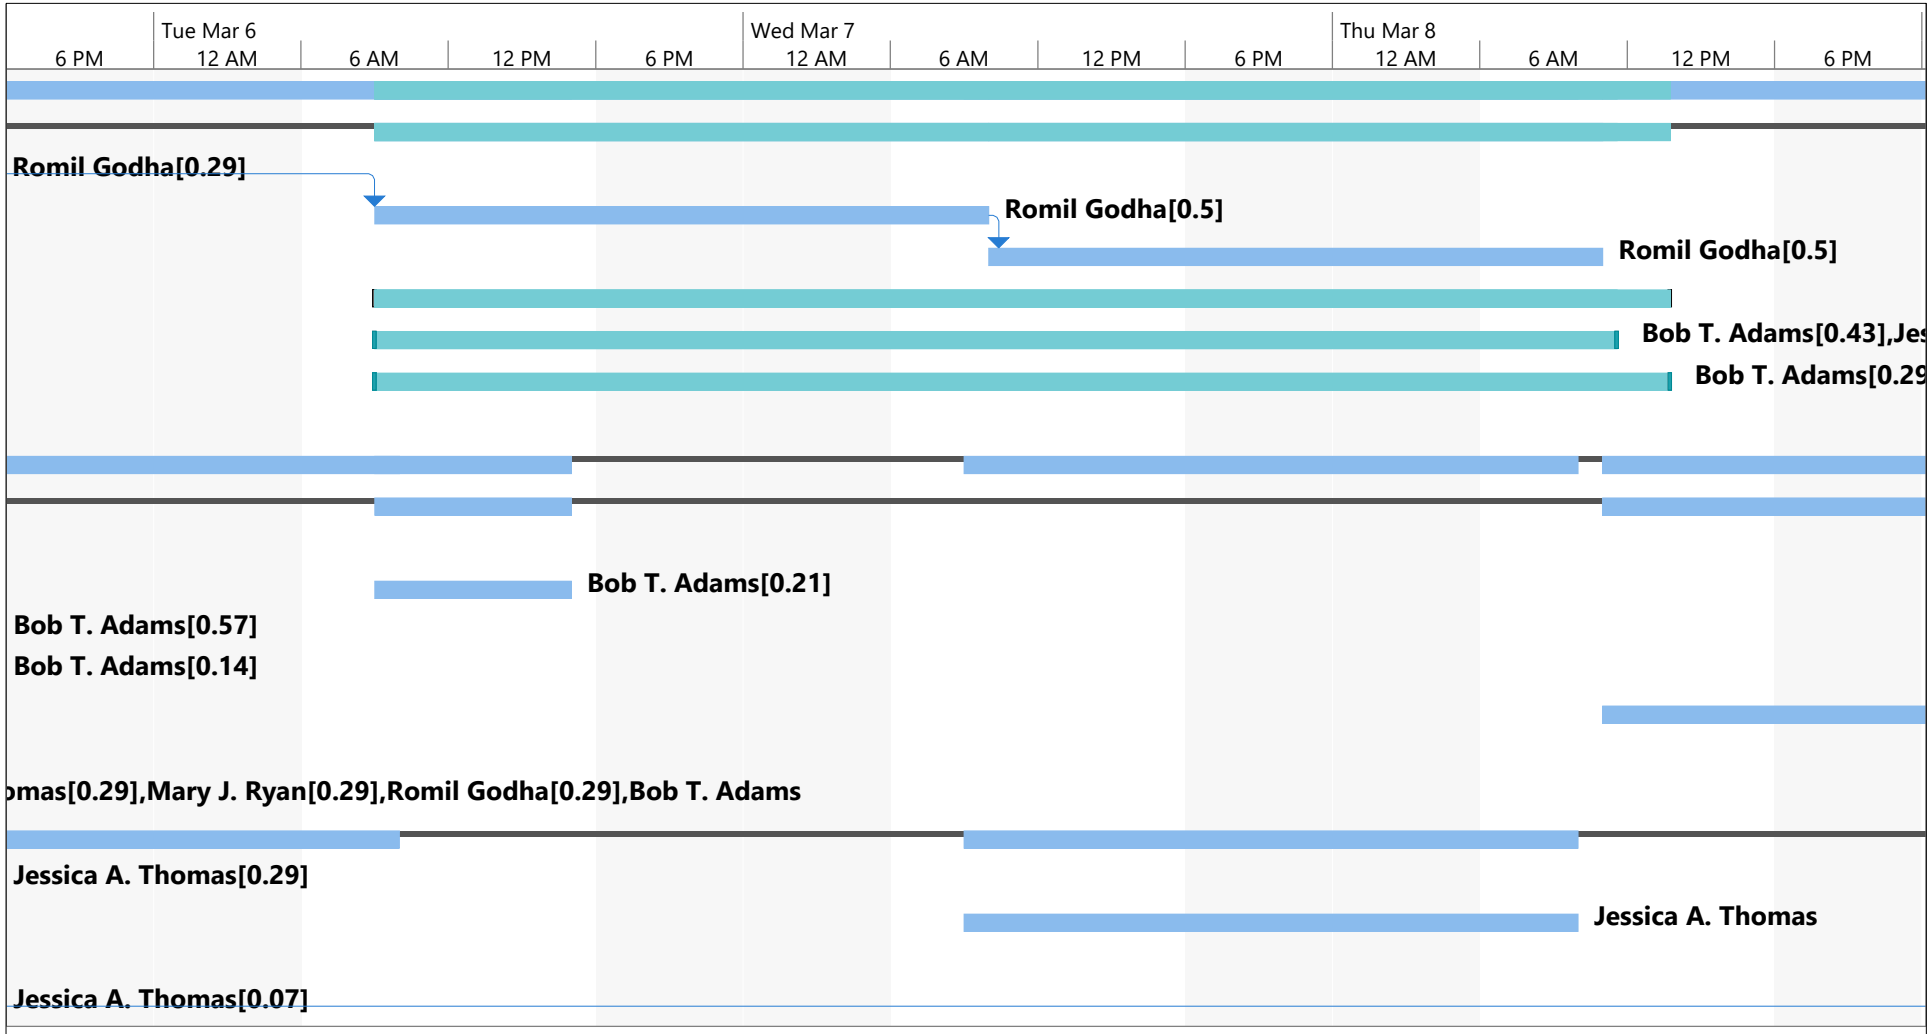

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

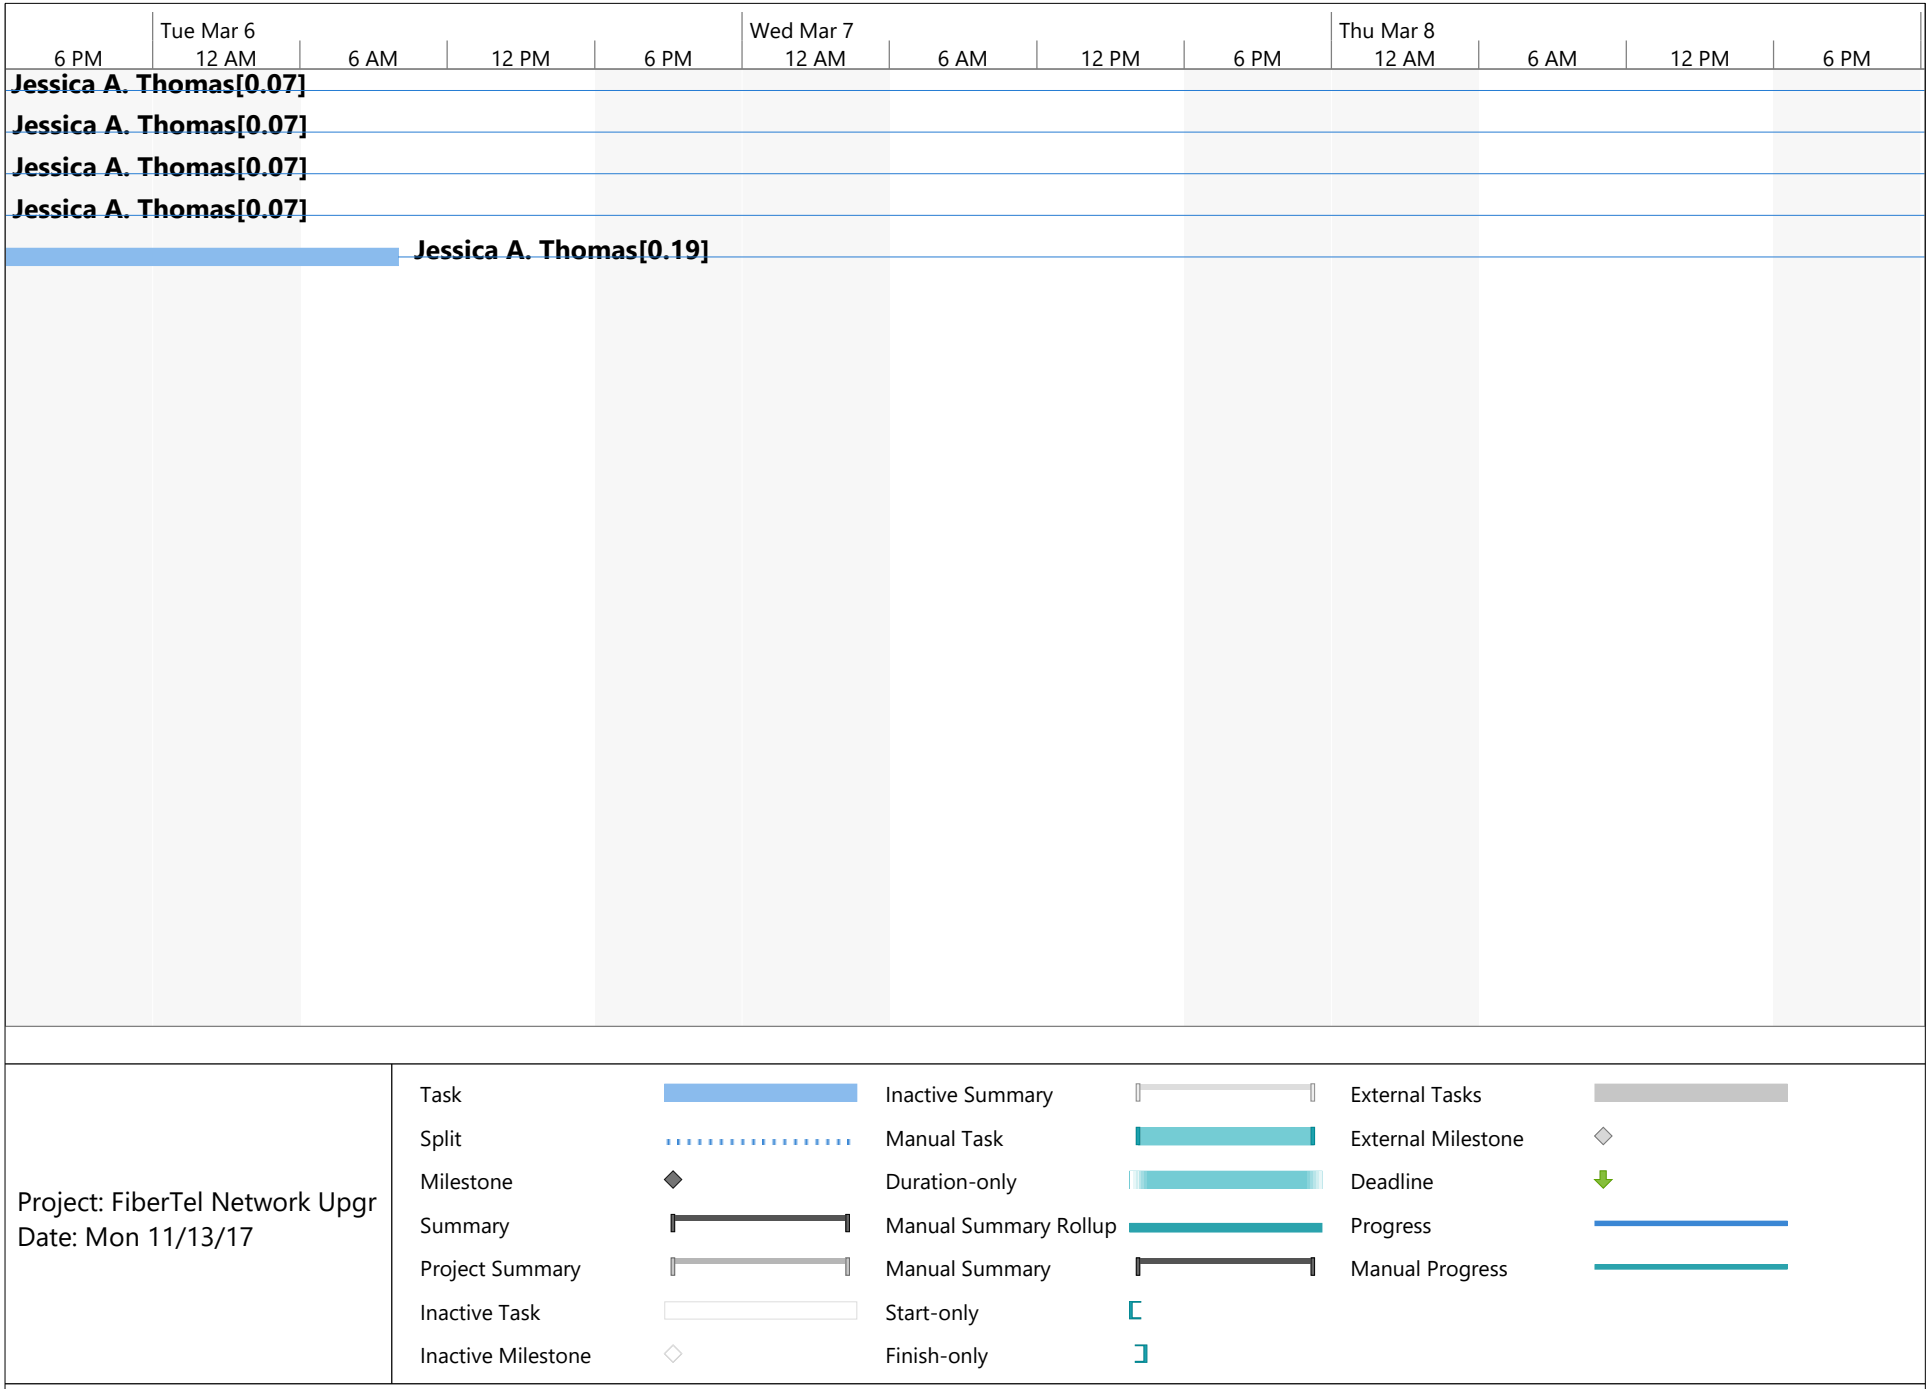

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

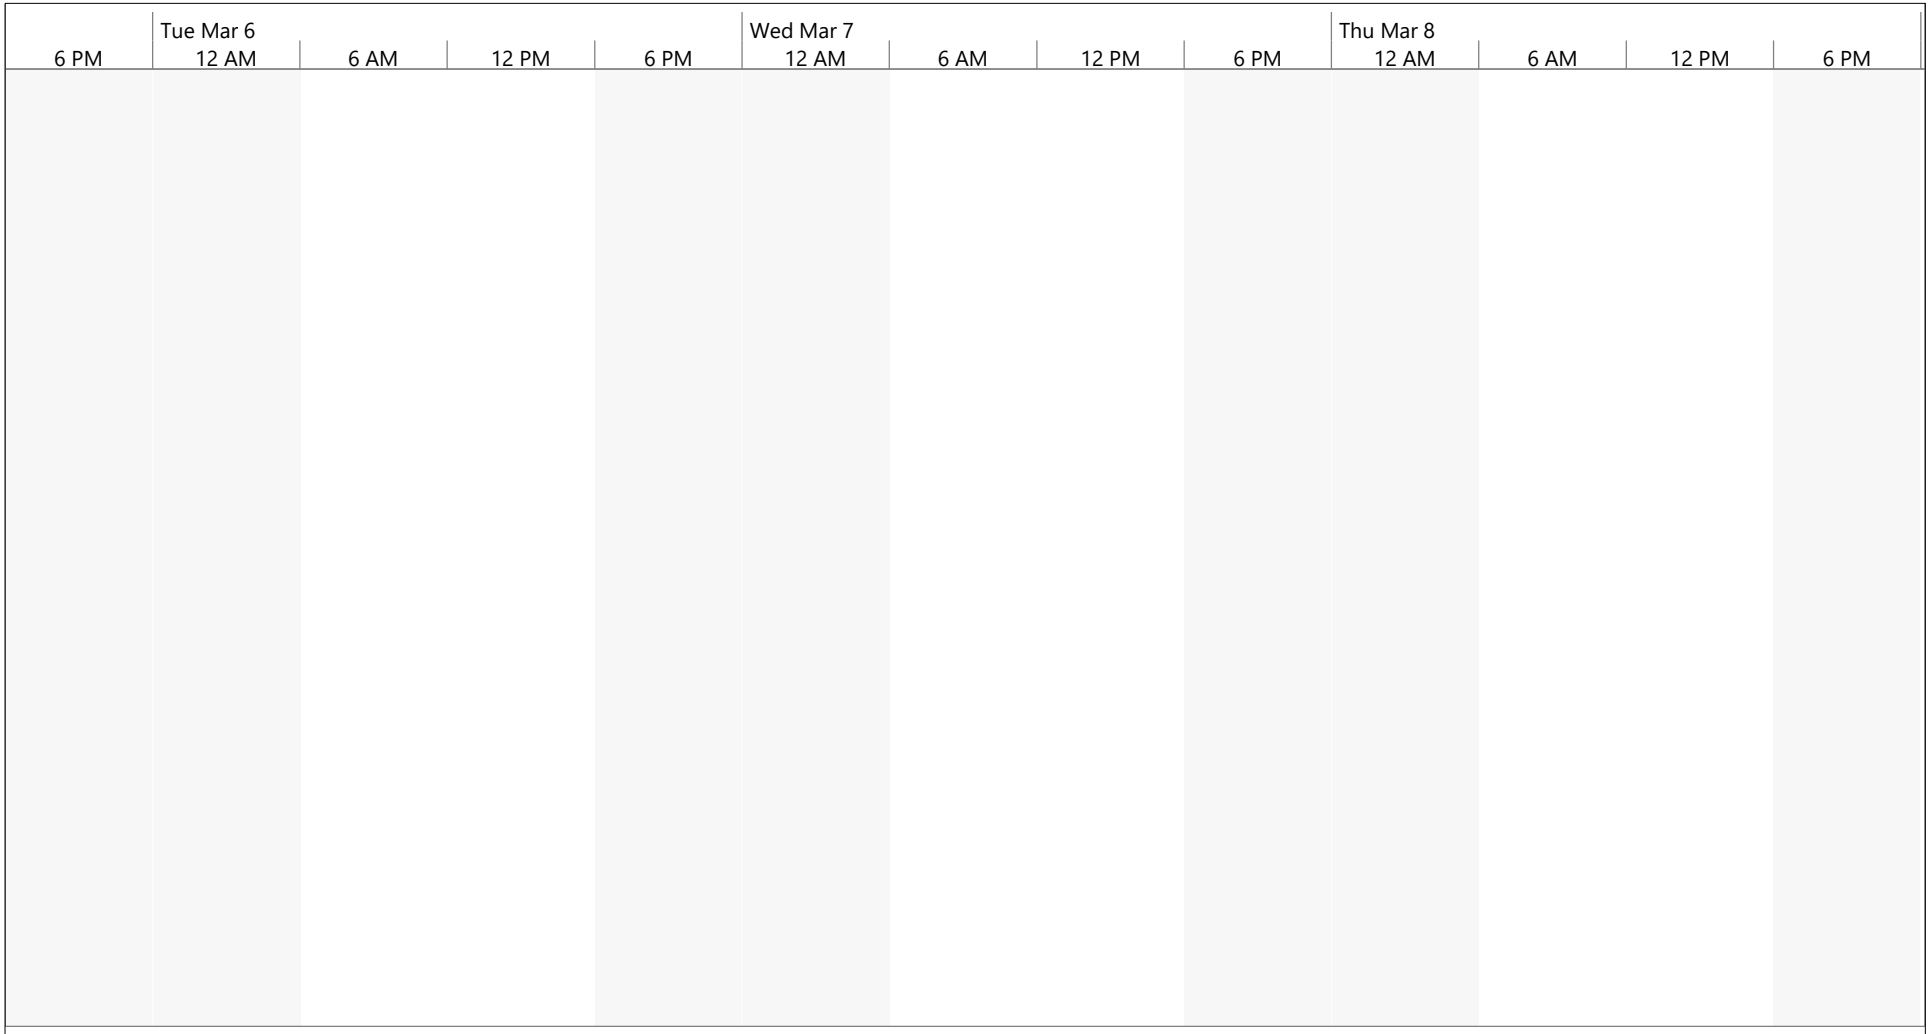

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	



Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

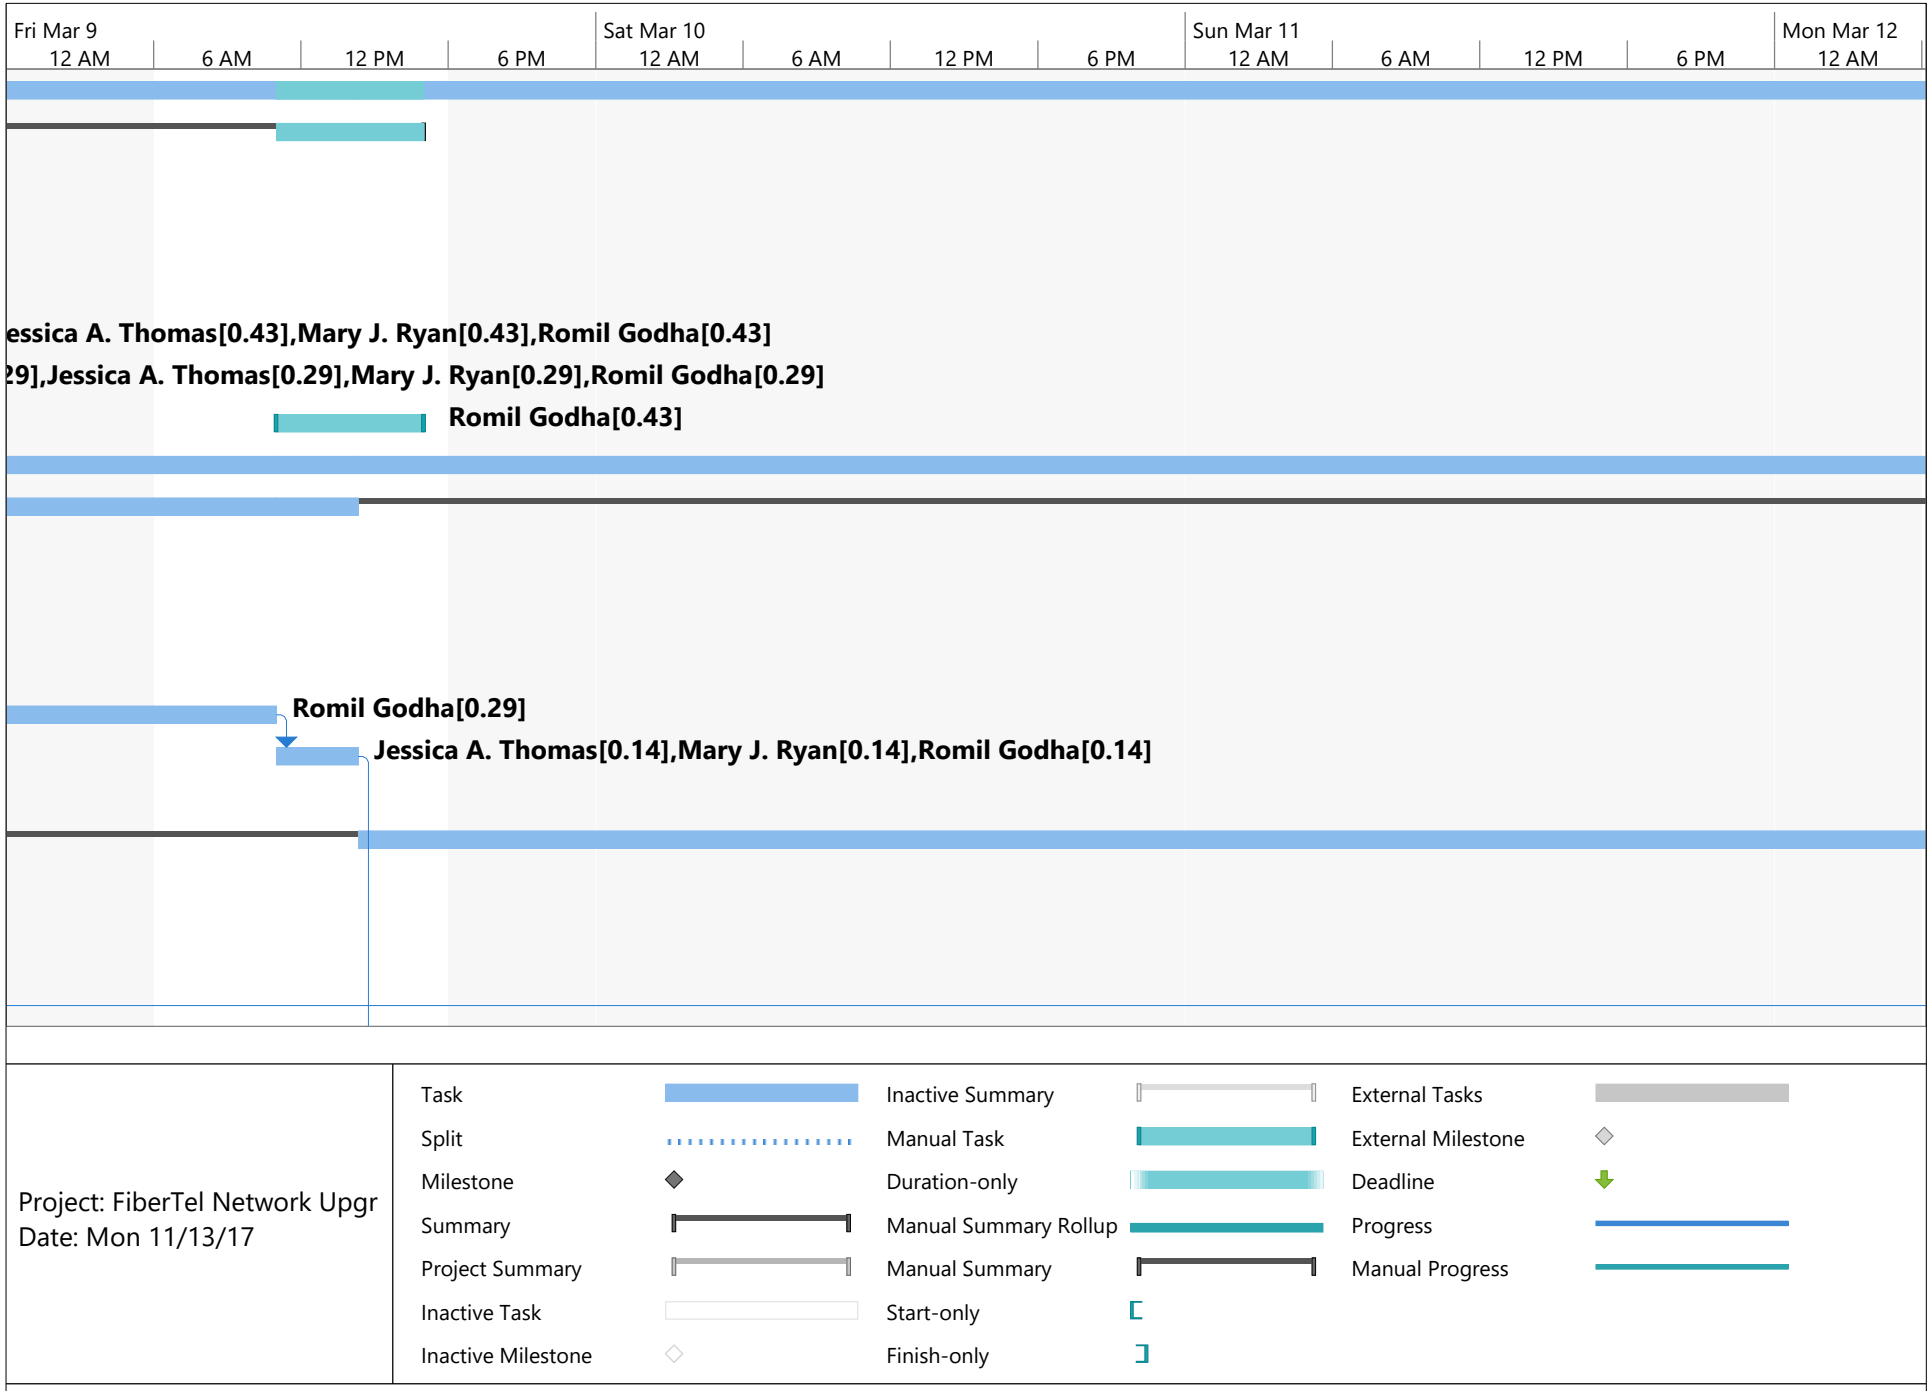

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

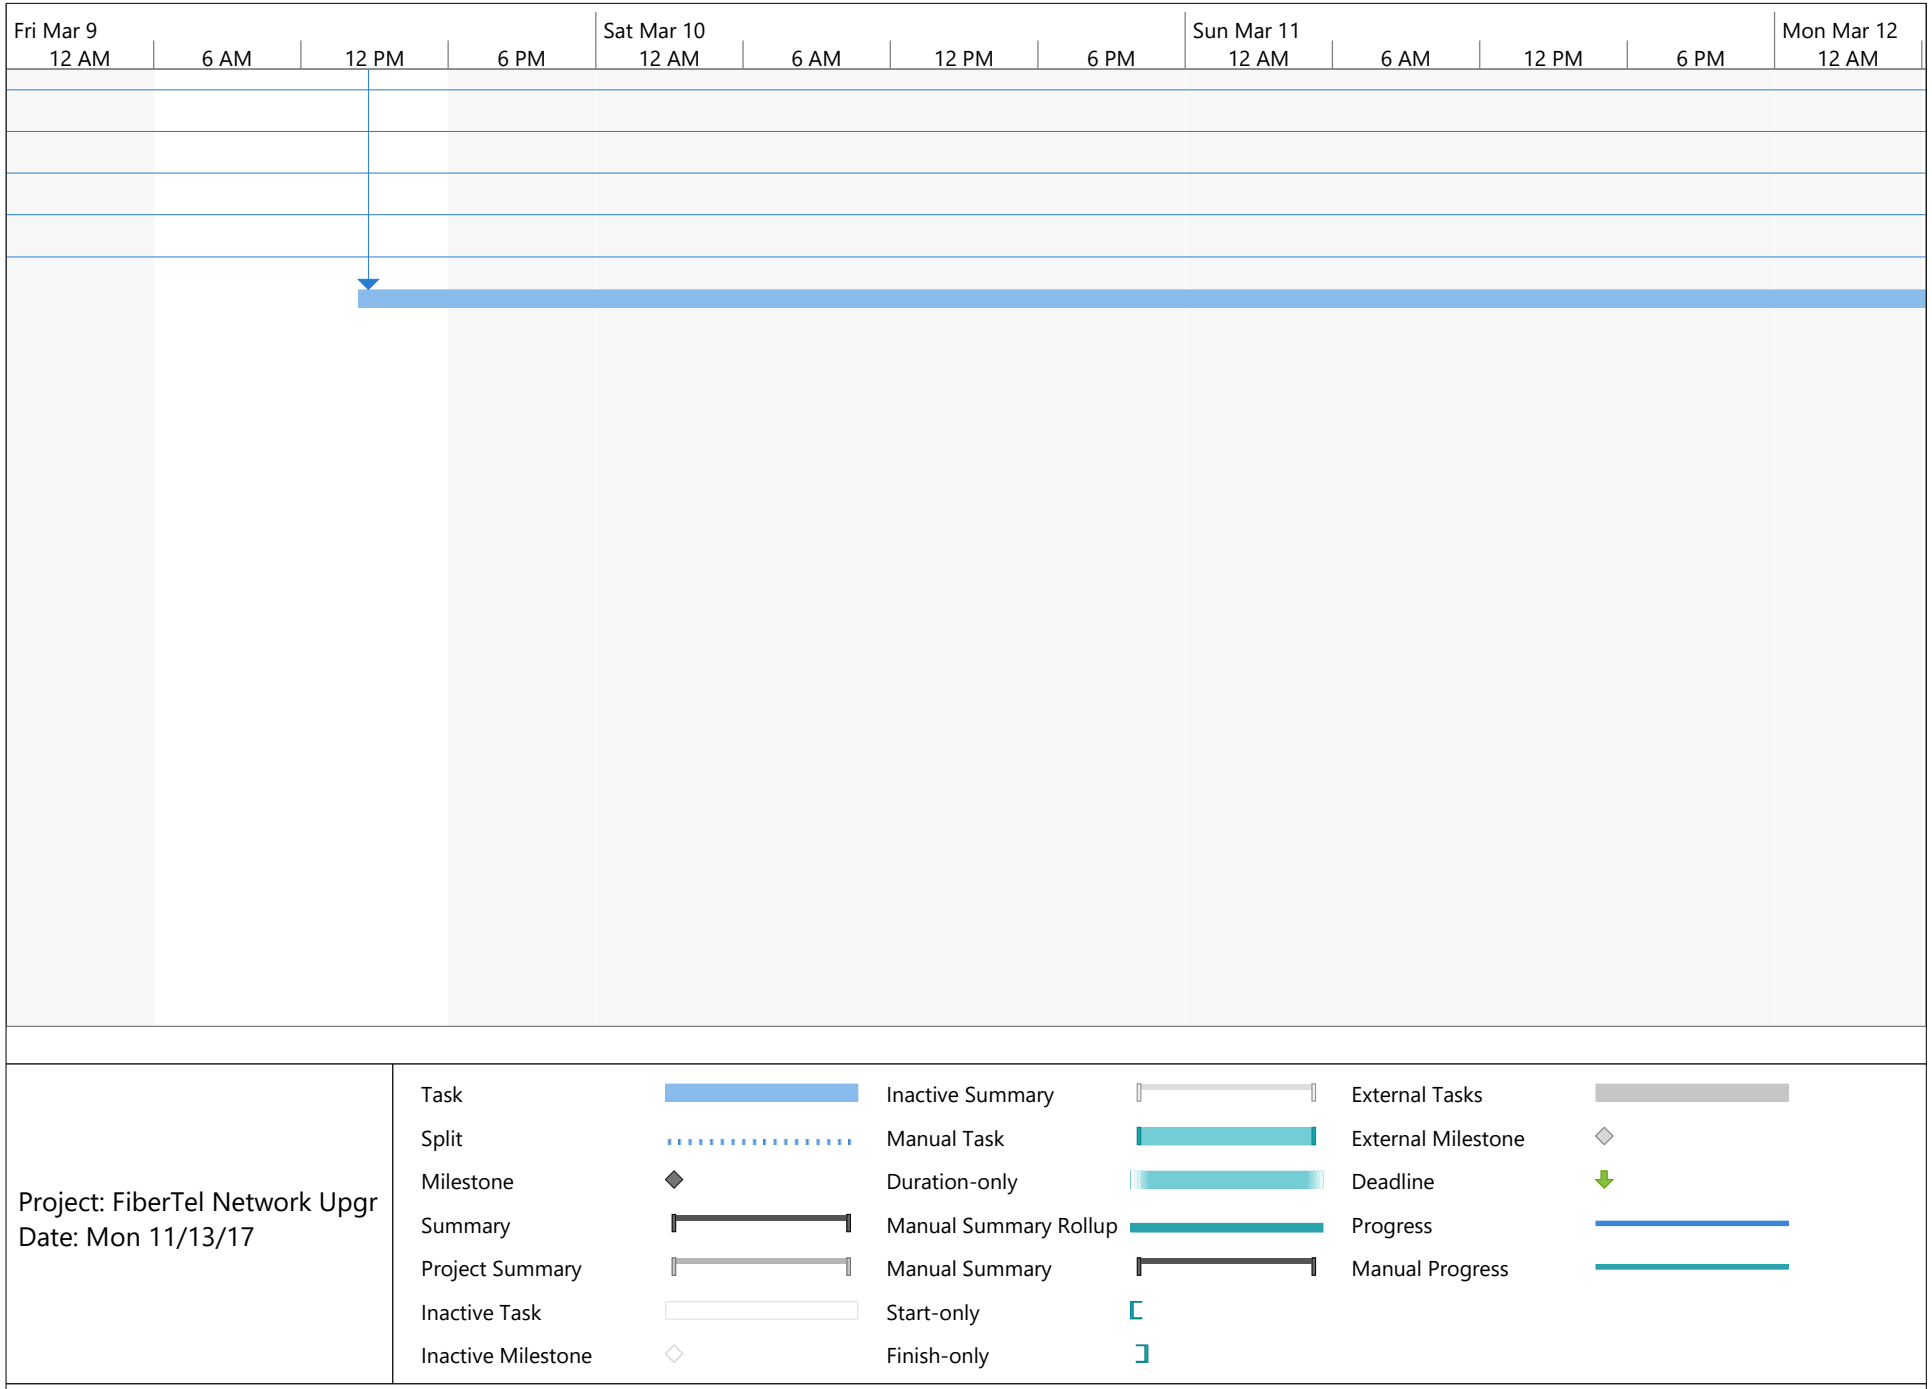

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

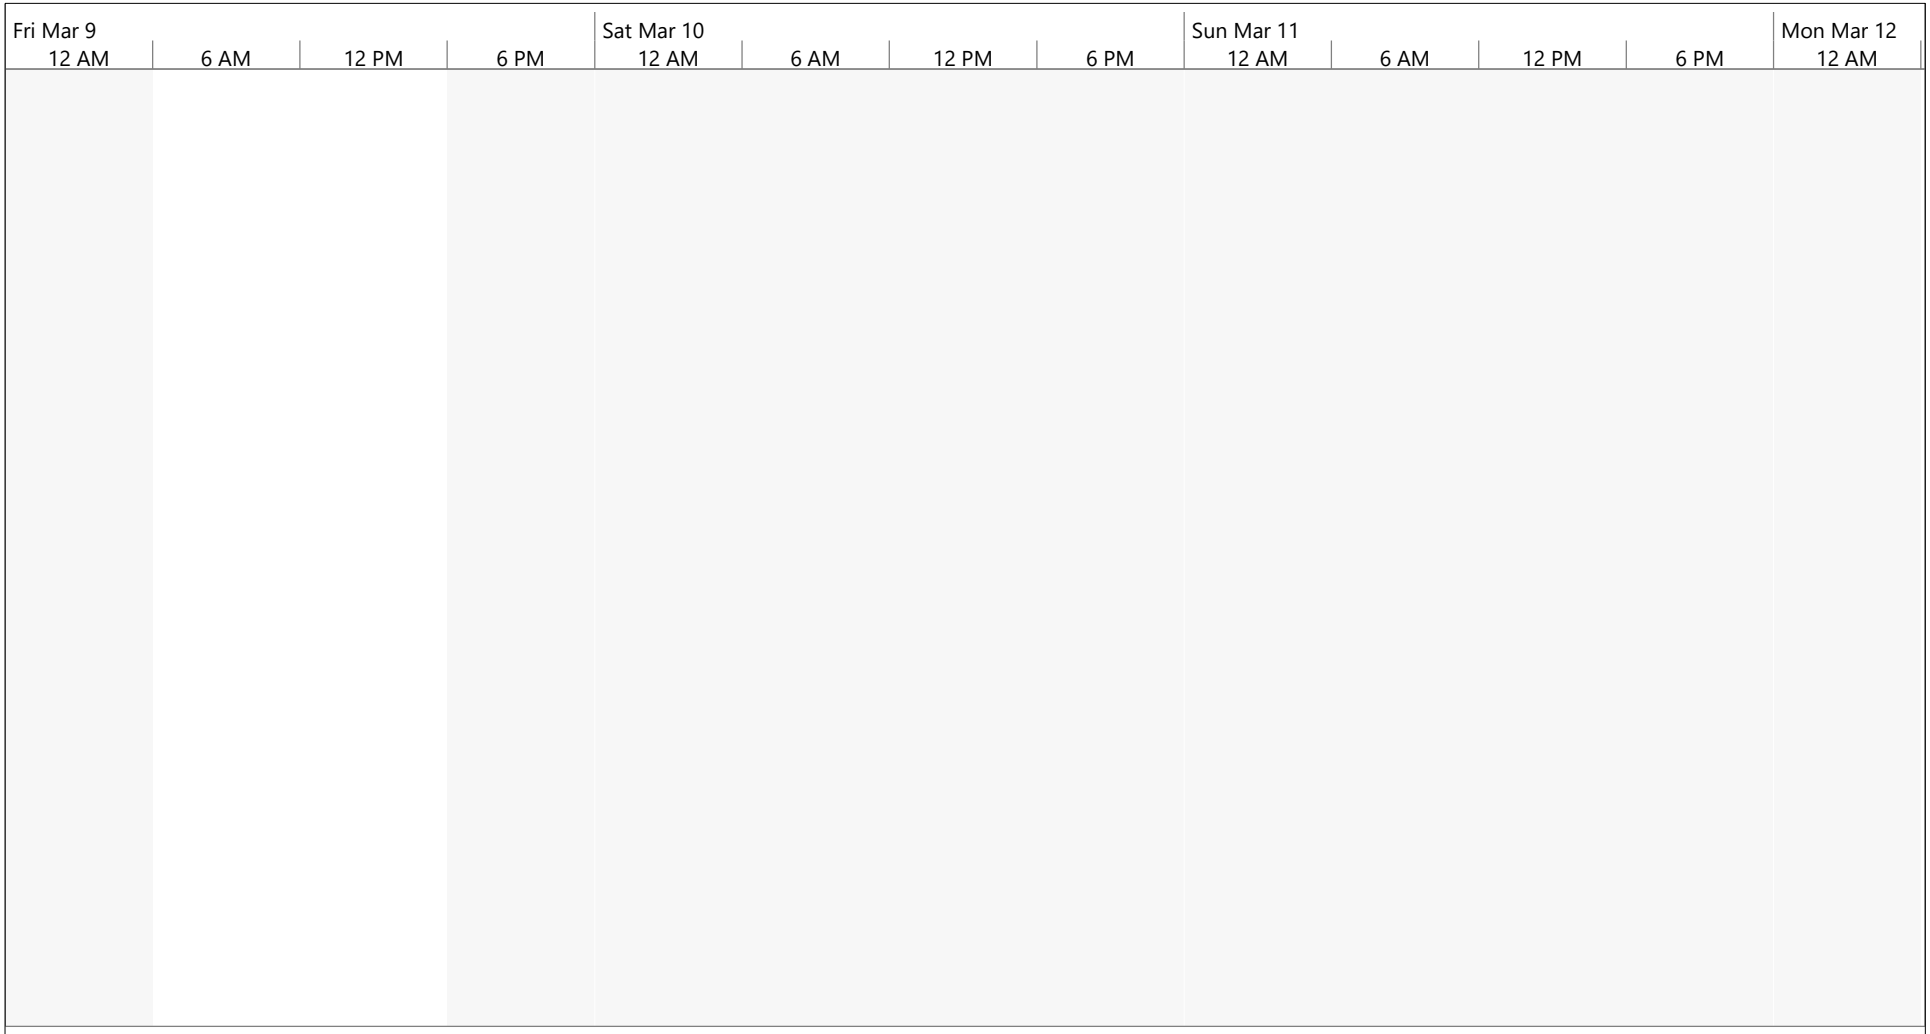

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

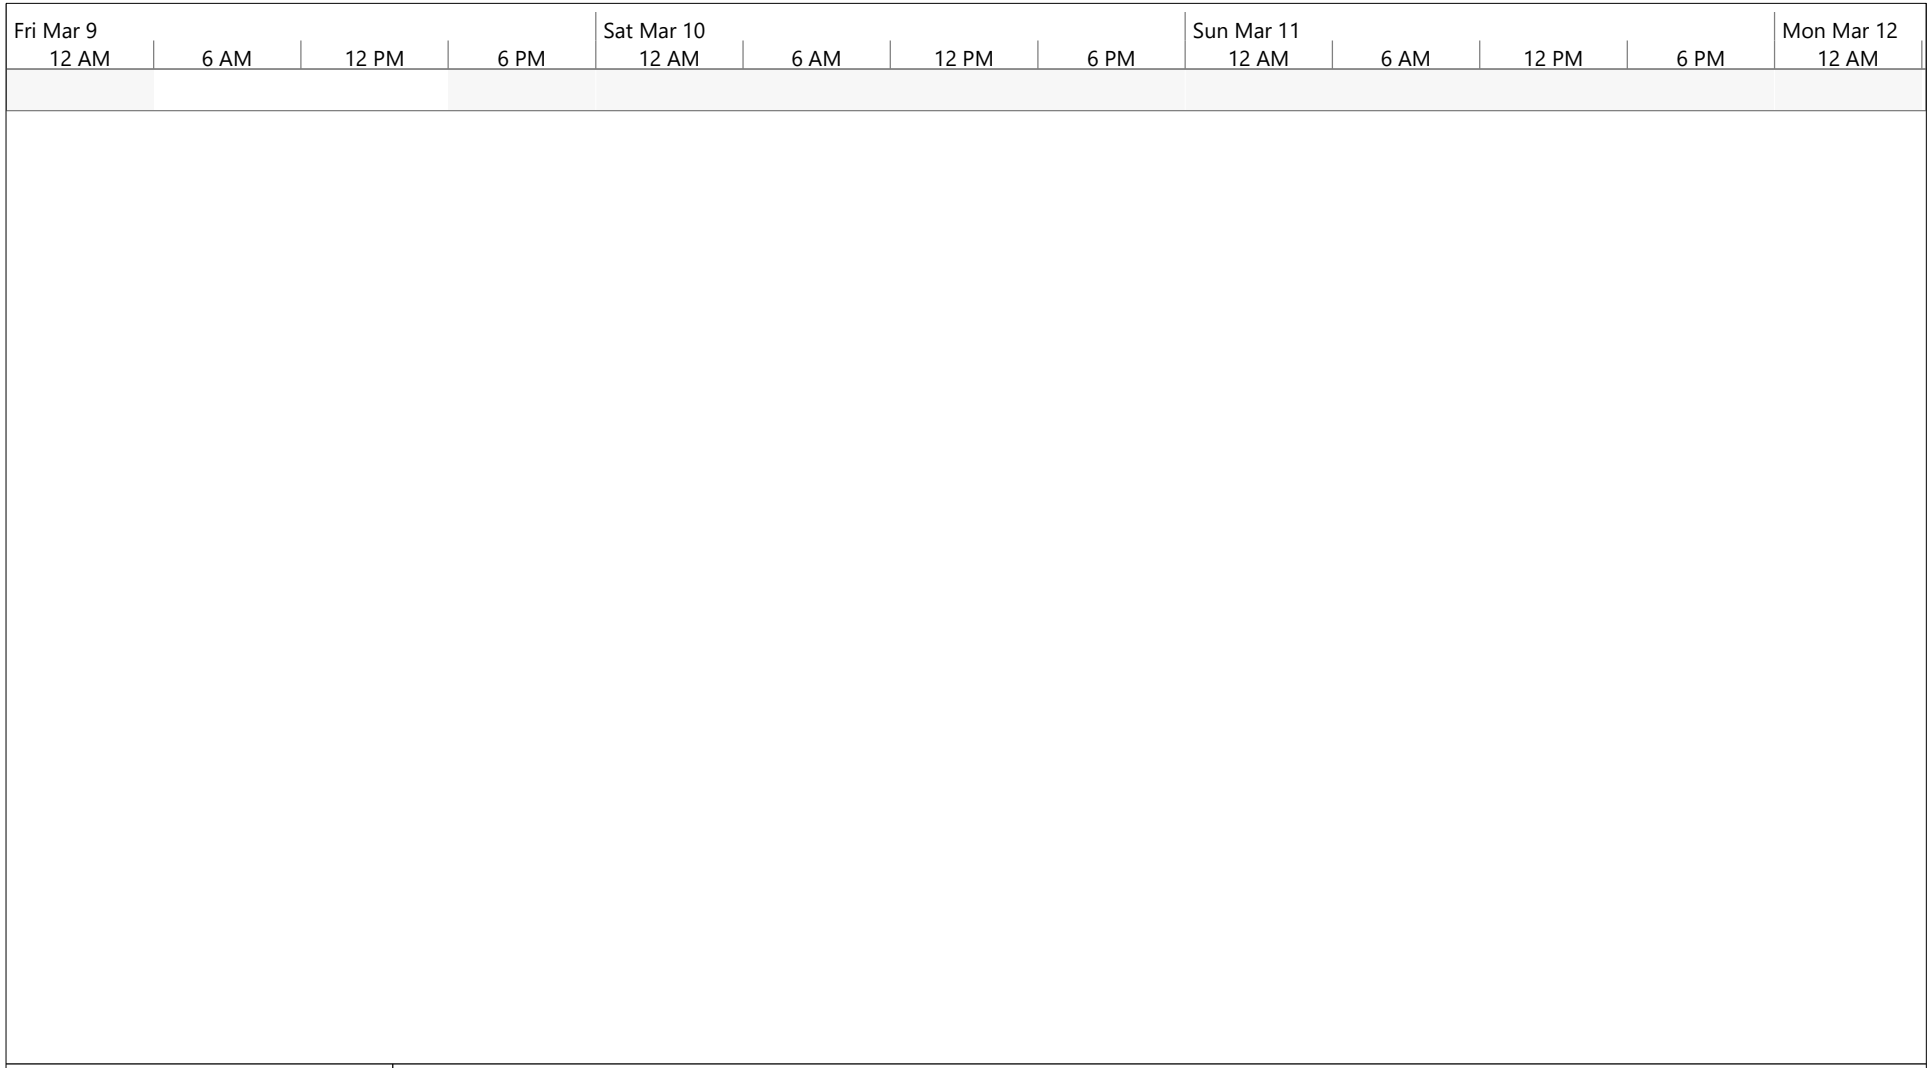

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

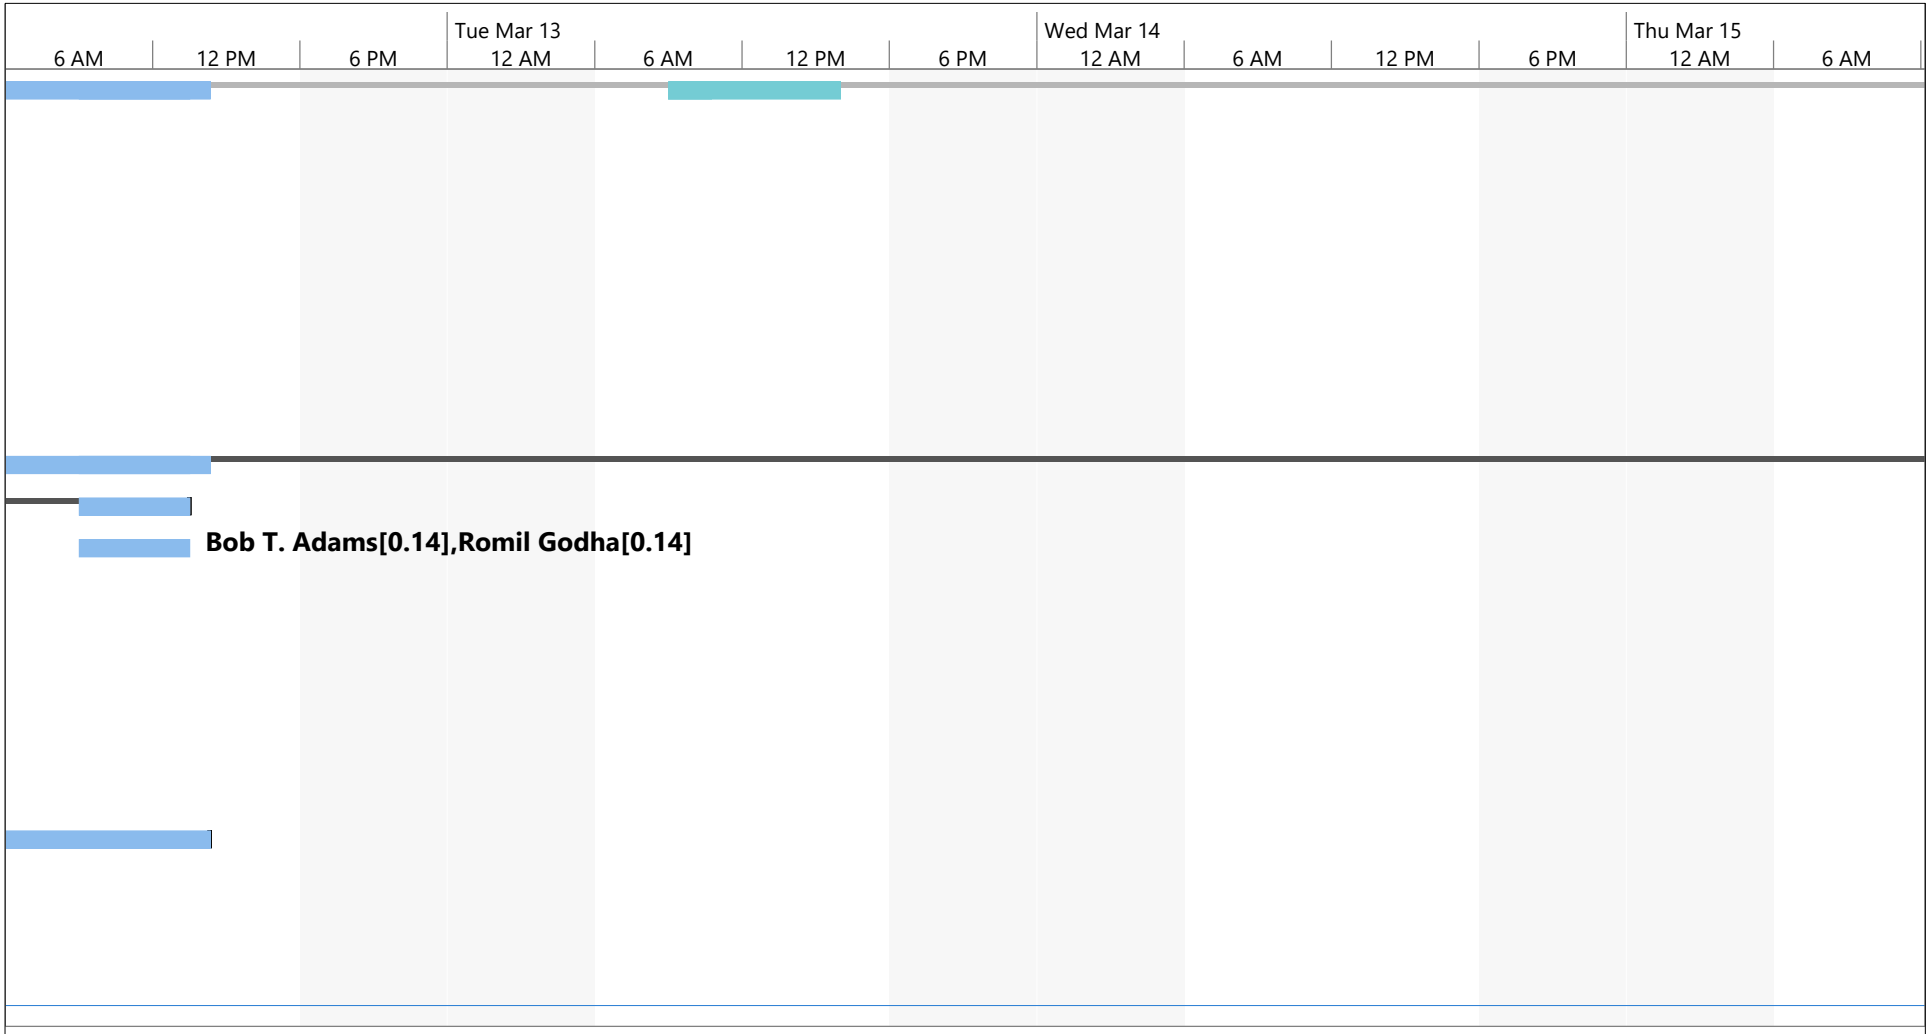

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

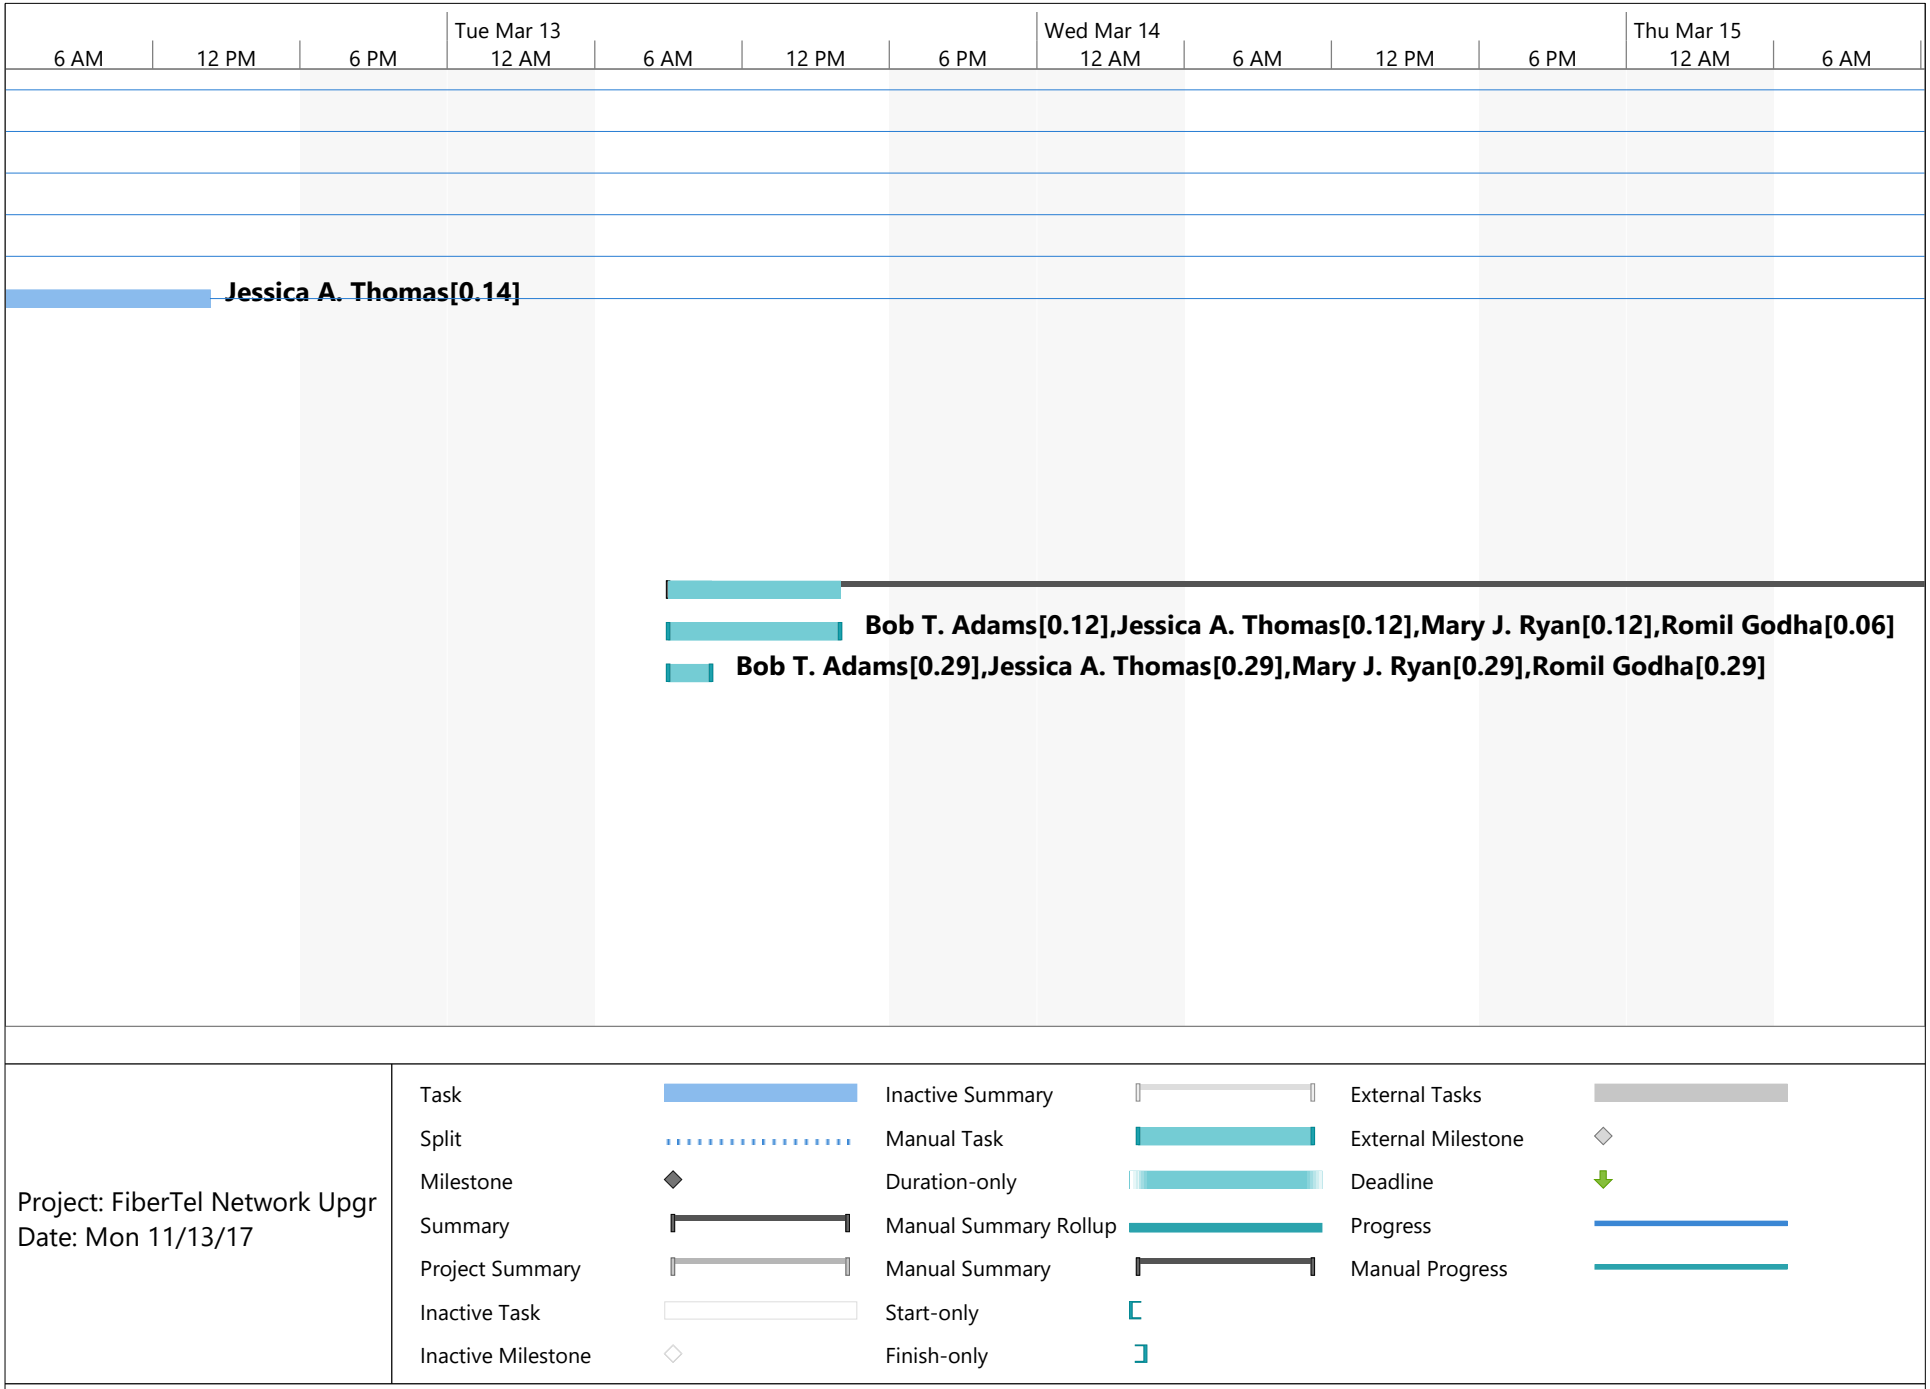

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

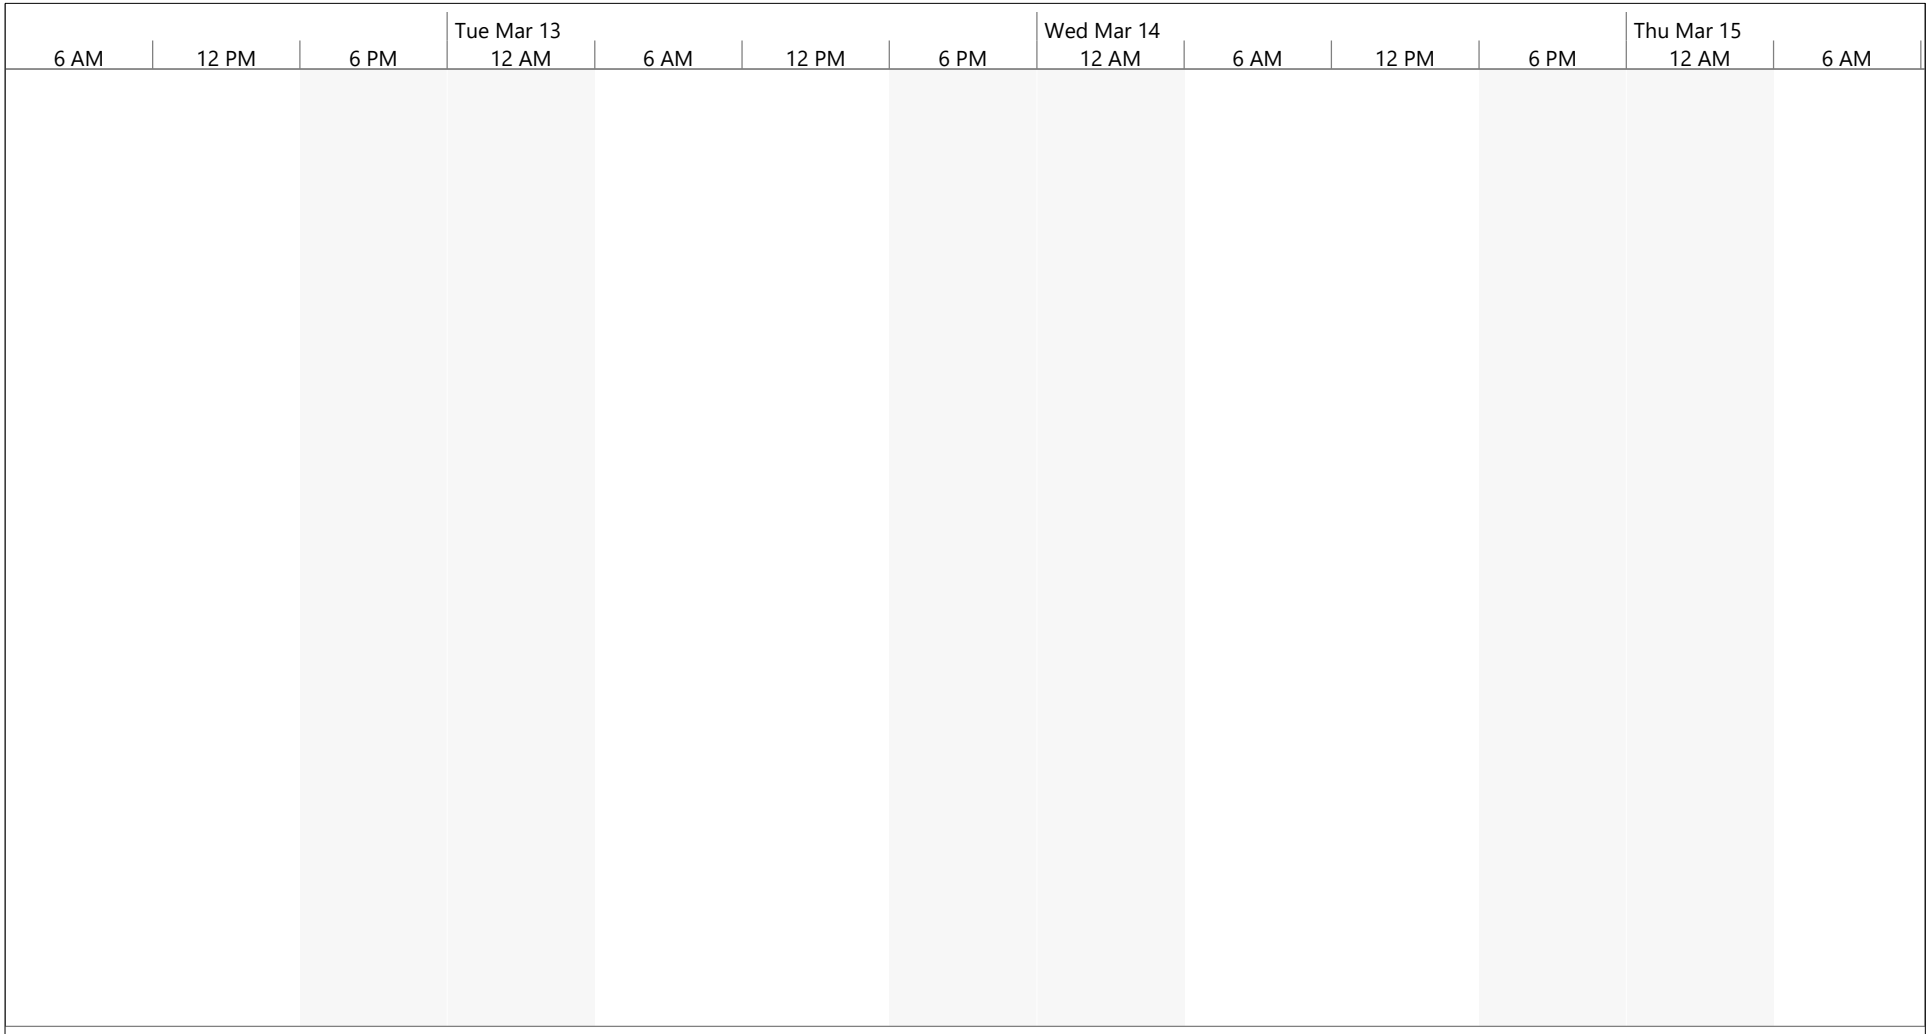

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

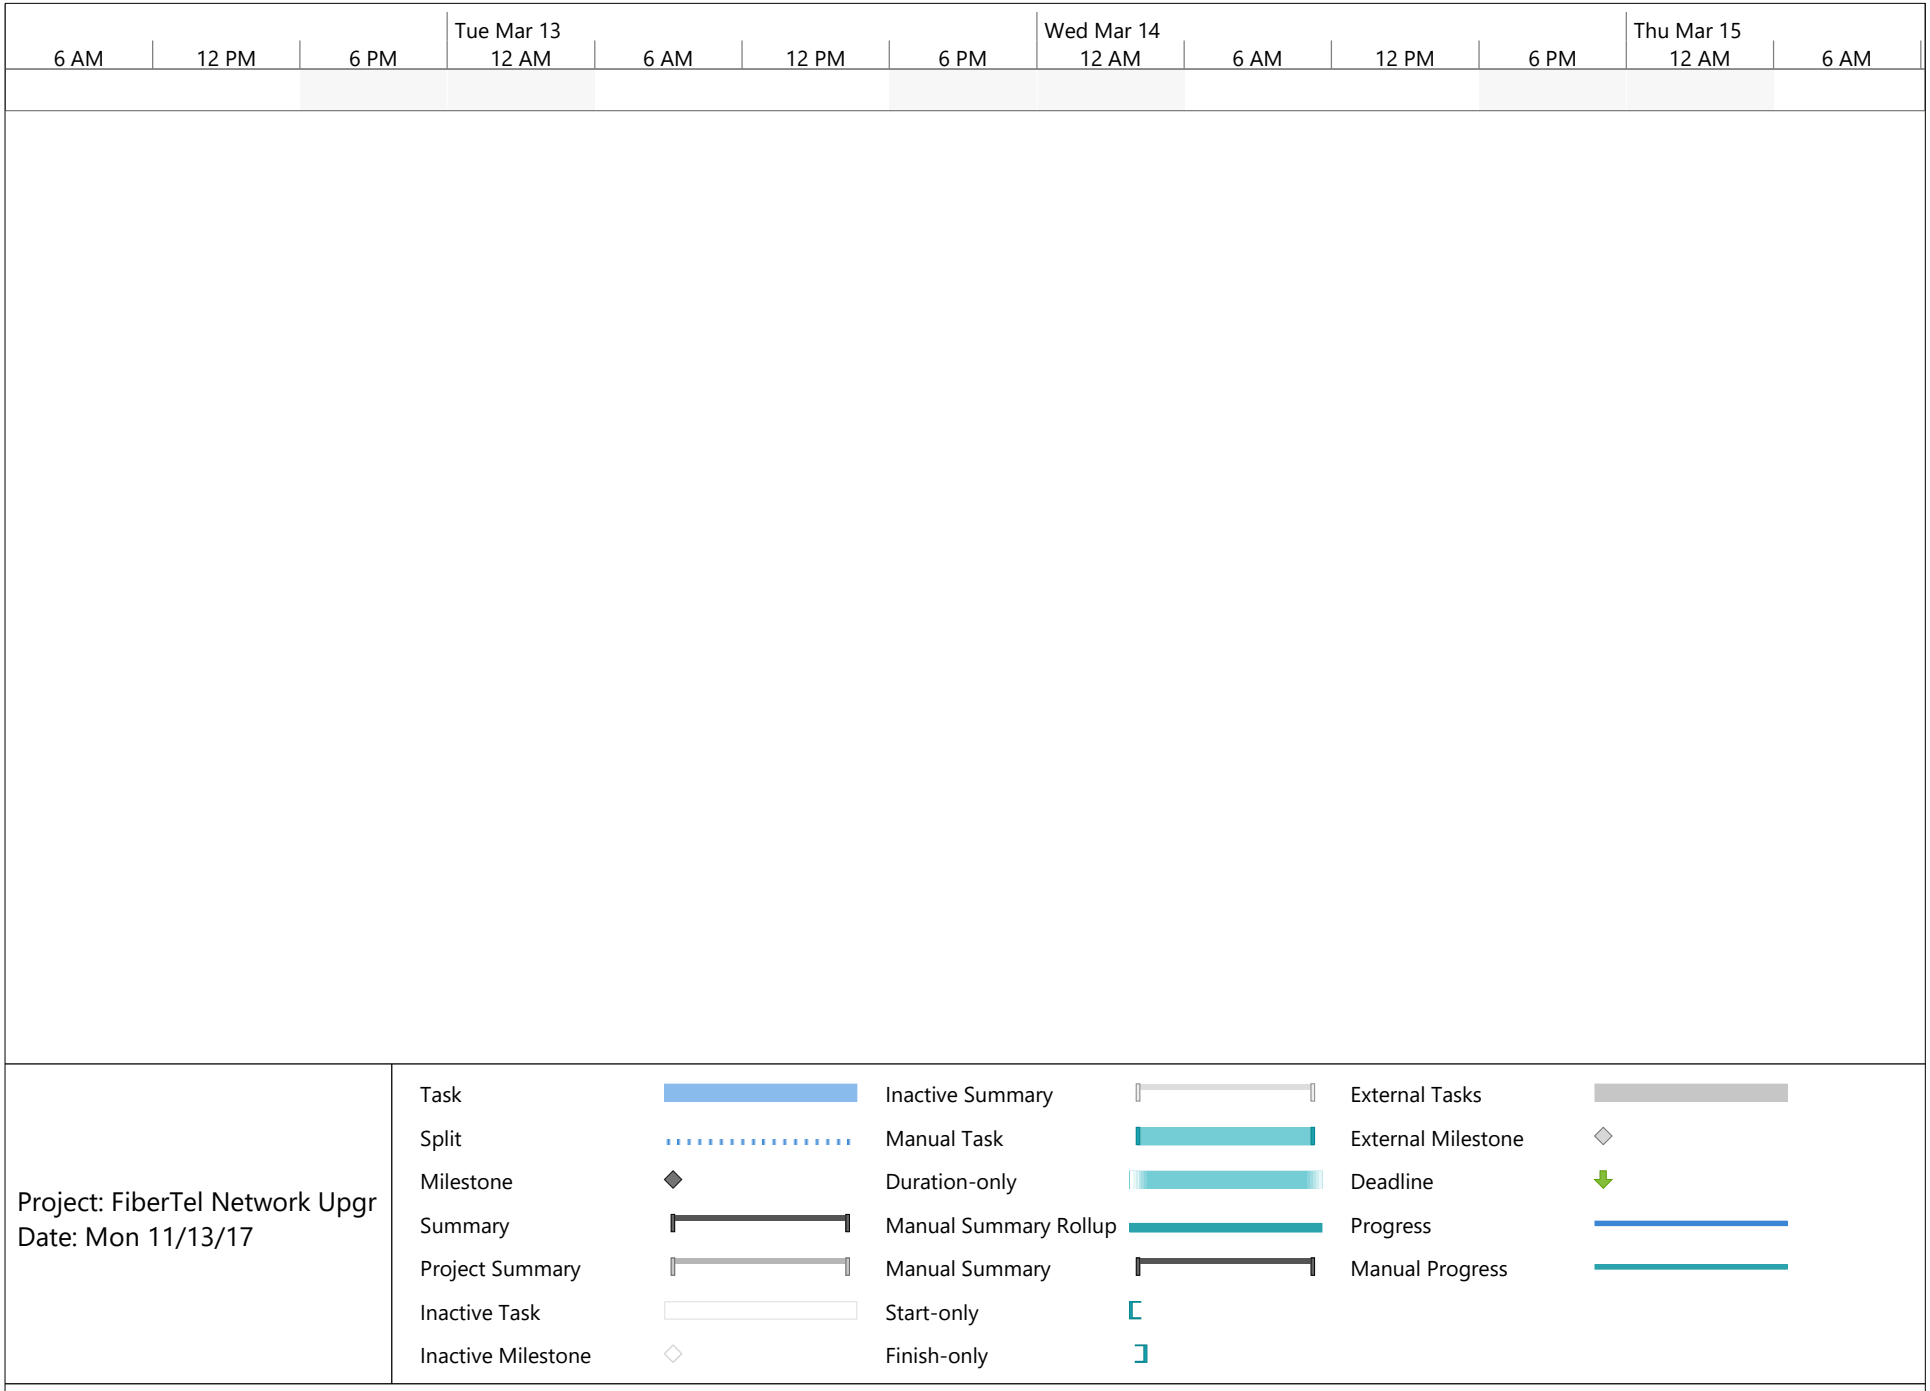
6 AM
12 PM
6 PM
Tue Mar 13
12 AM
6 AM
12 PM
6 PM
Wed Mar 14
12 AM
6 AM
12 PM
6 PM
Thu Mar 15
12 AM
6 AM
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

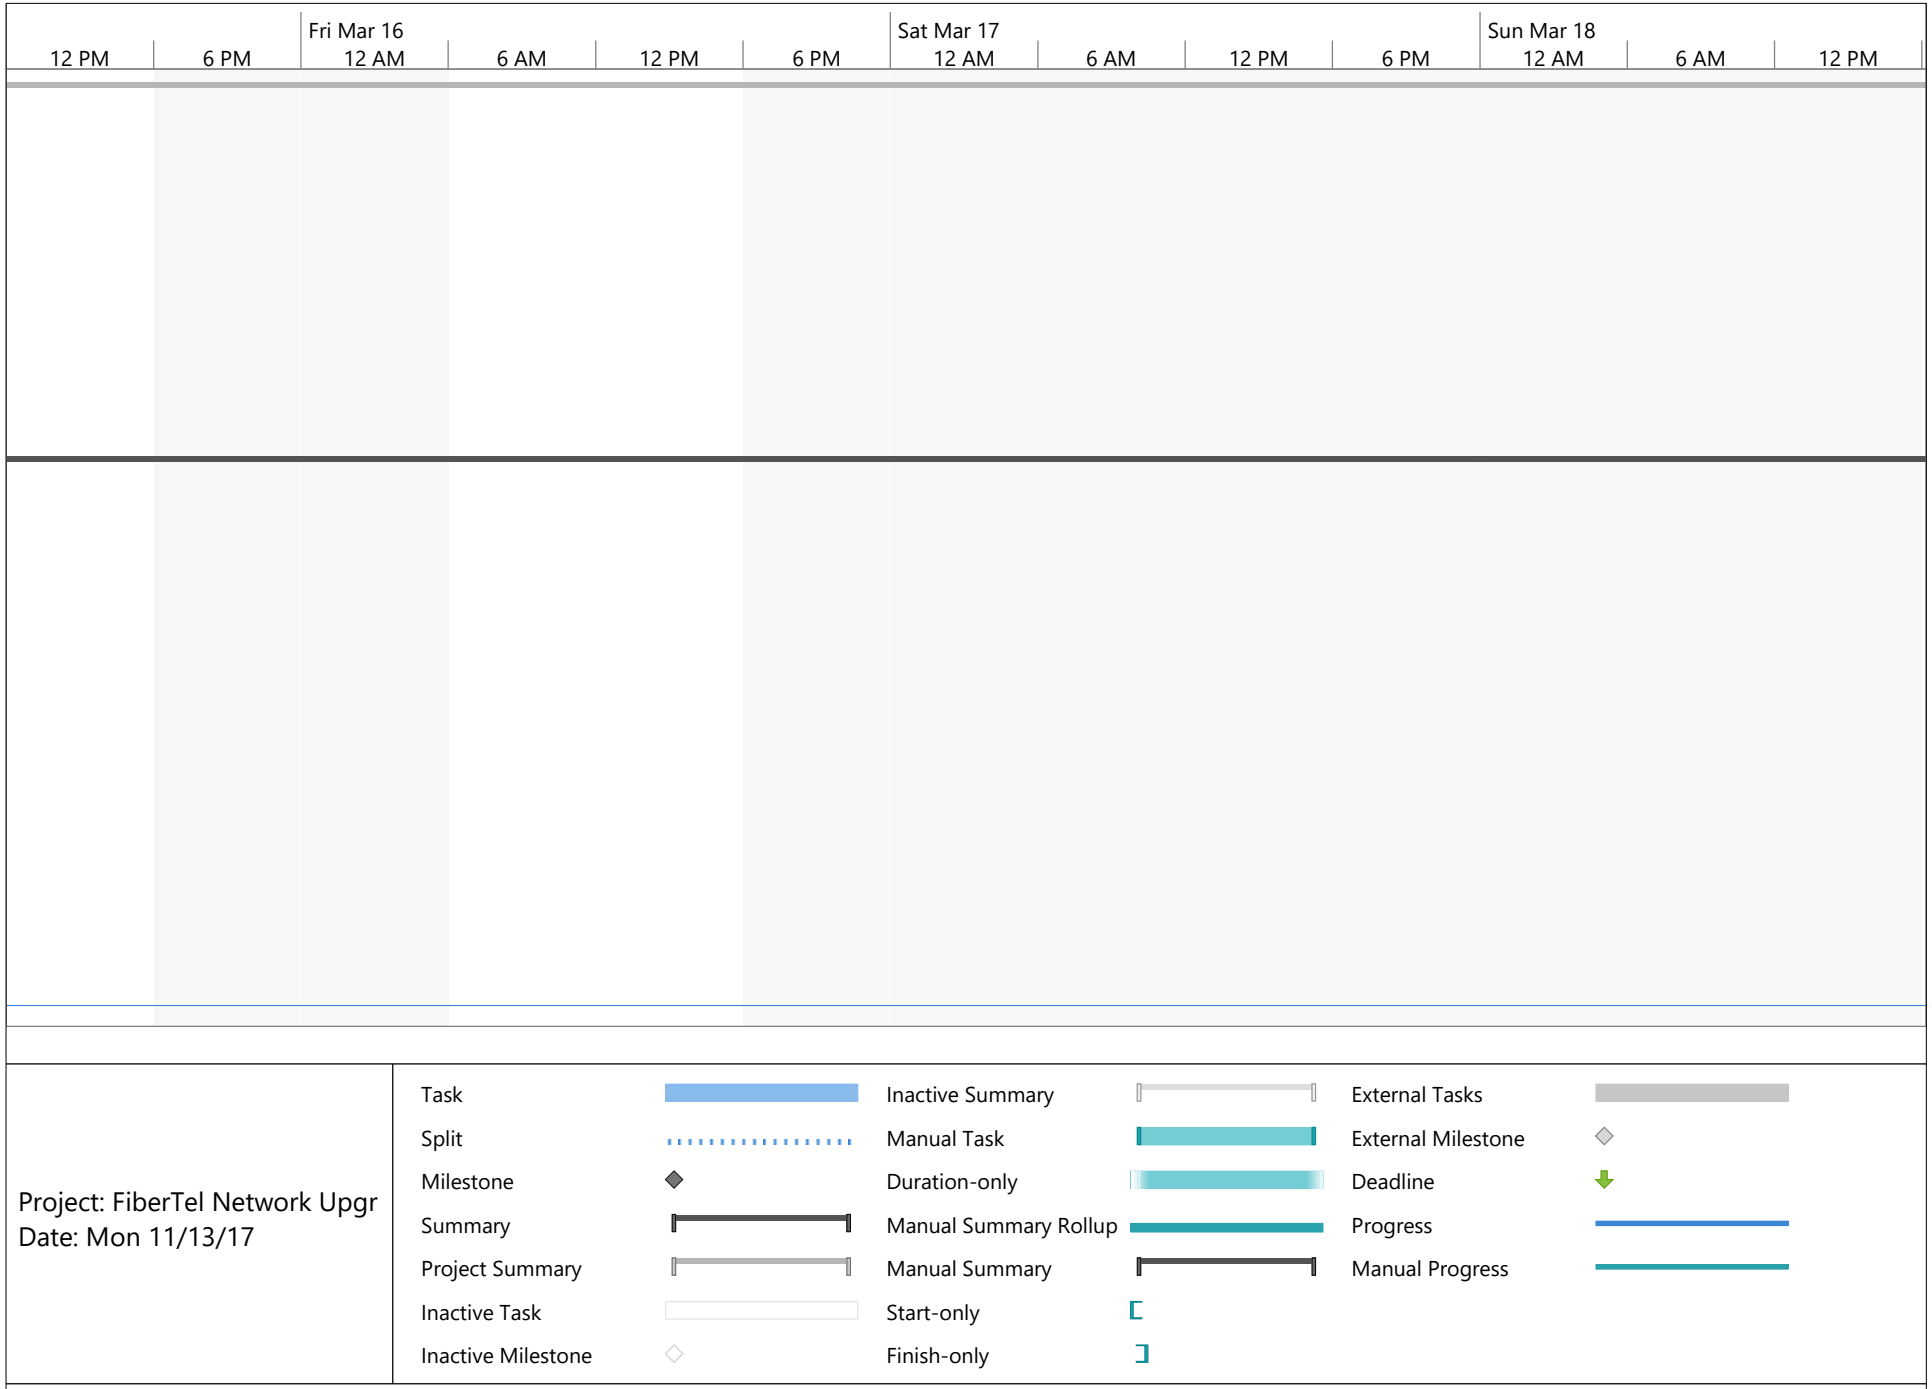

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

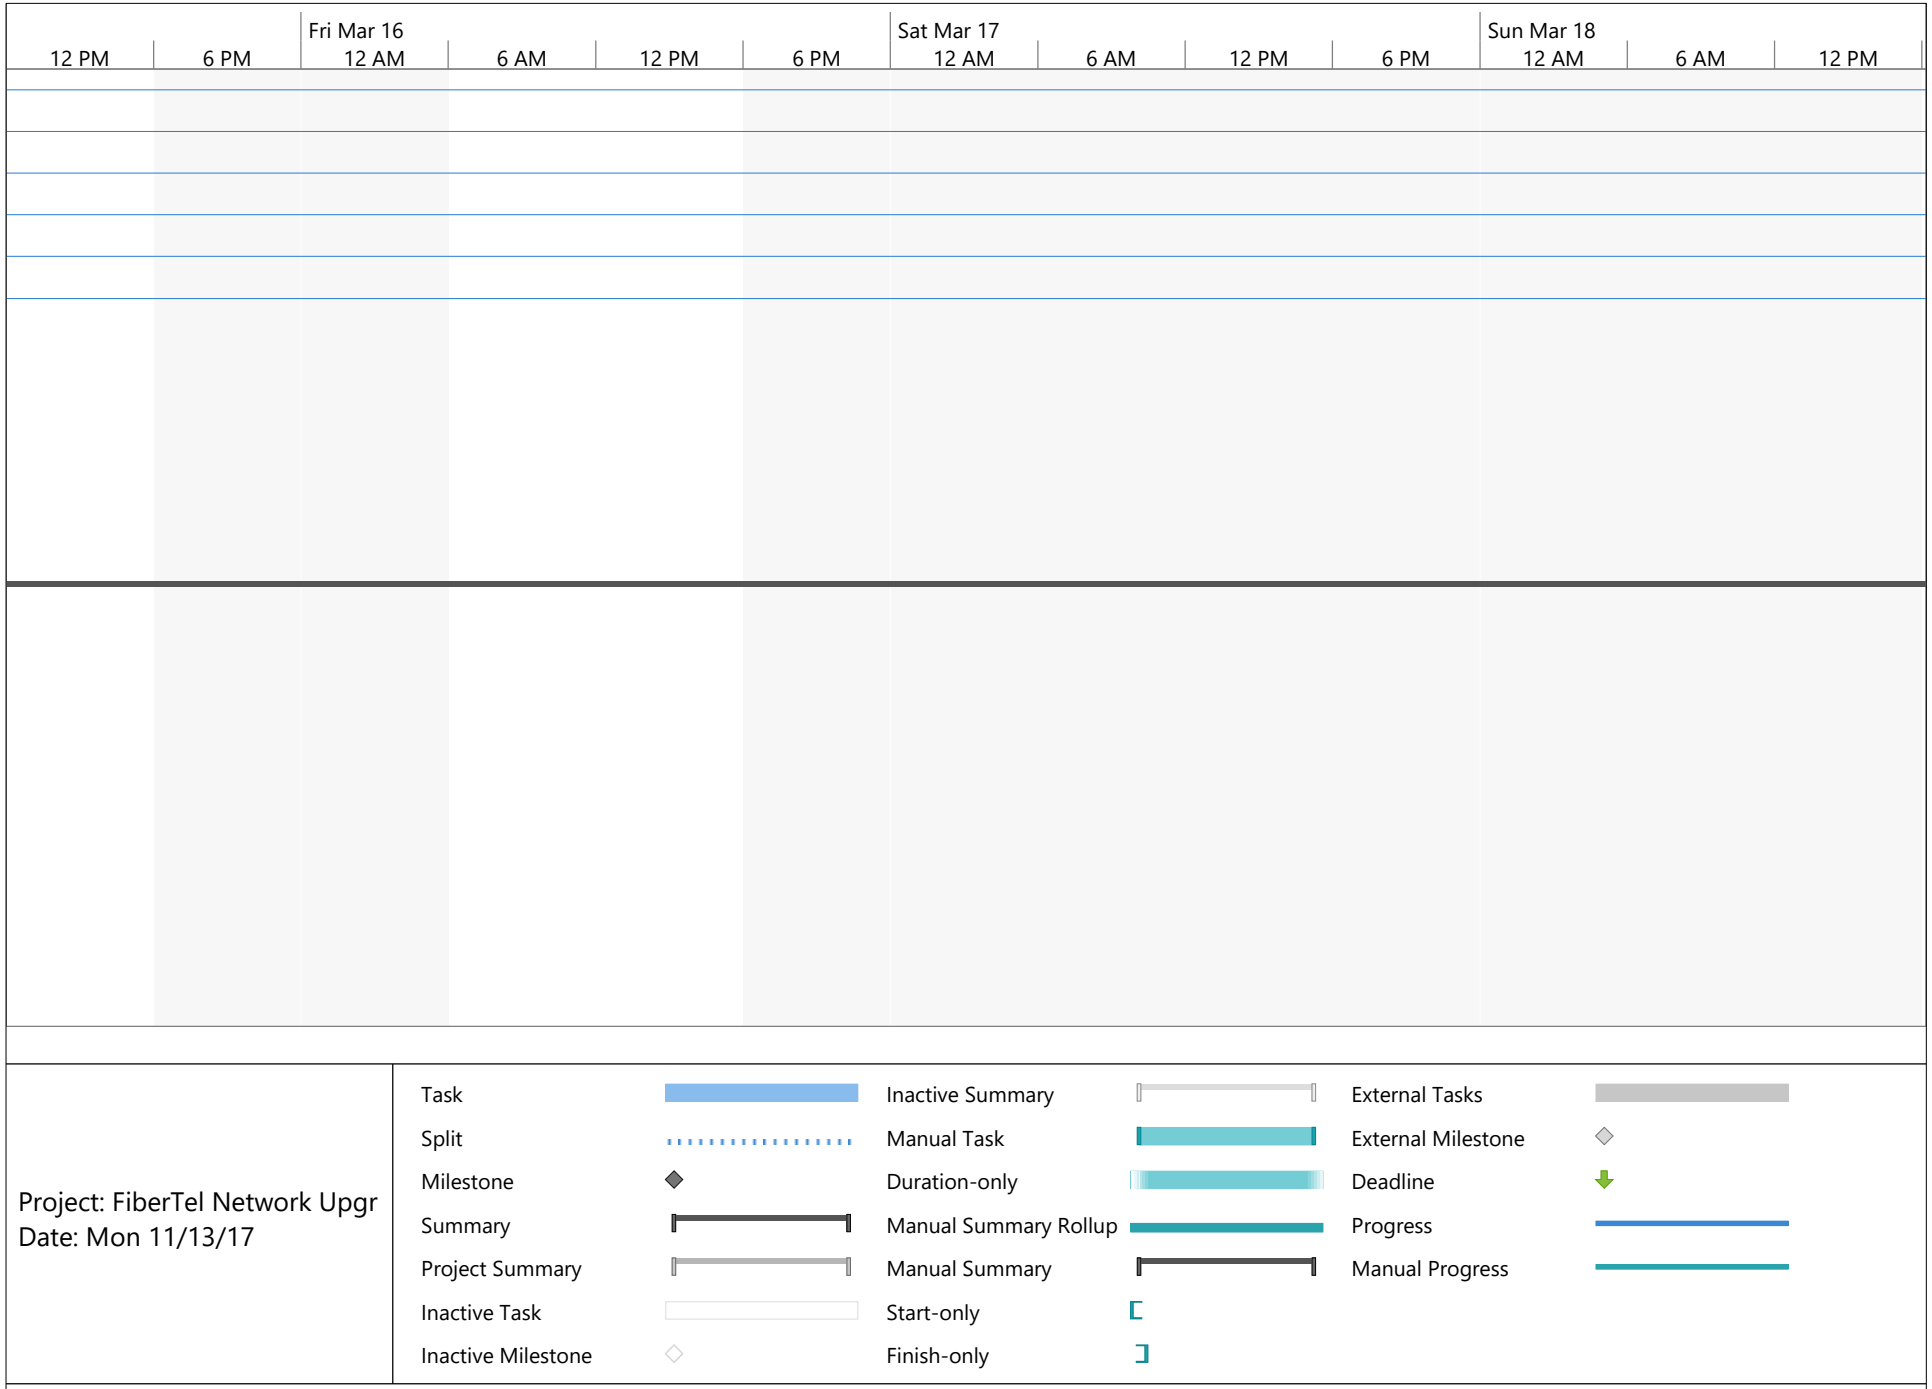

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

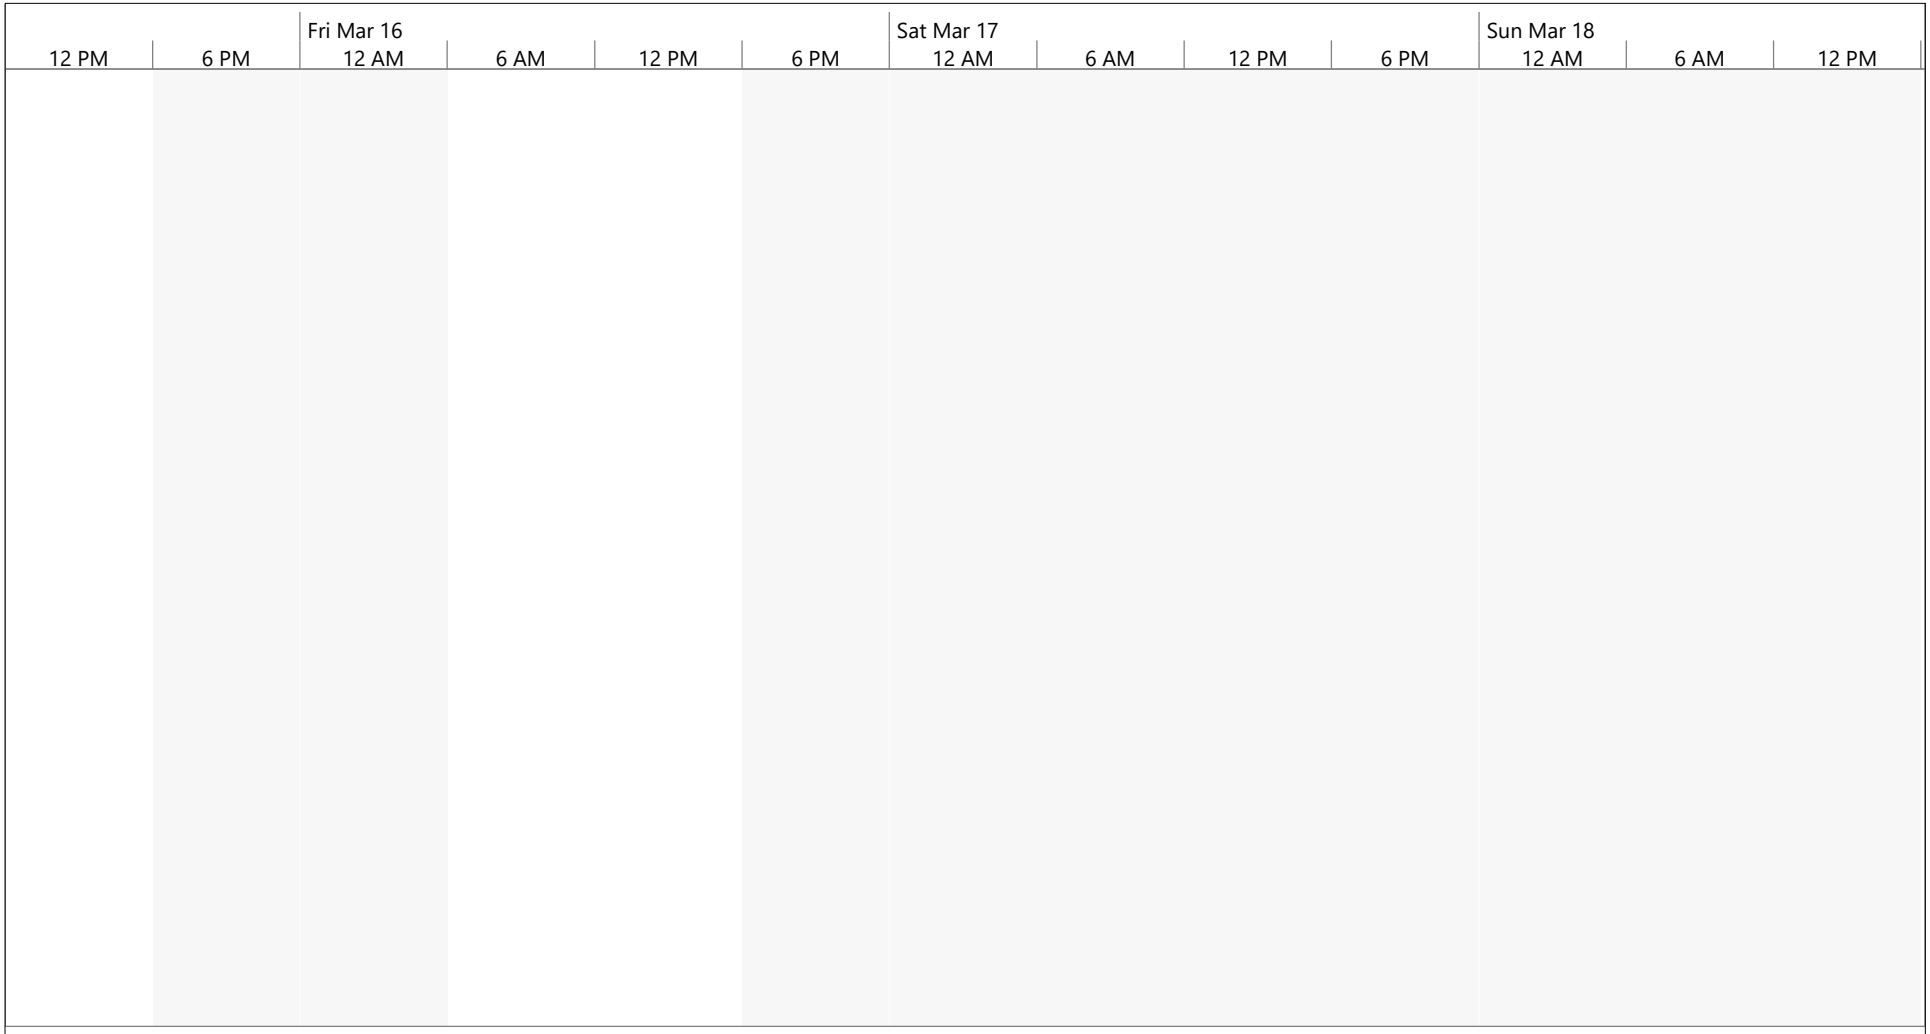

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

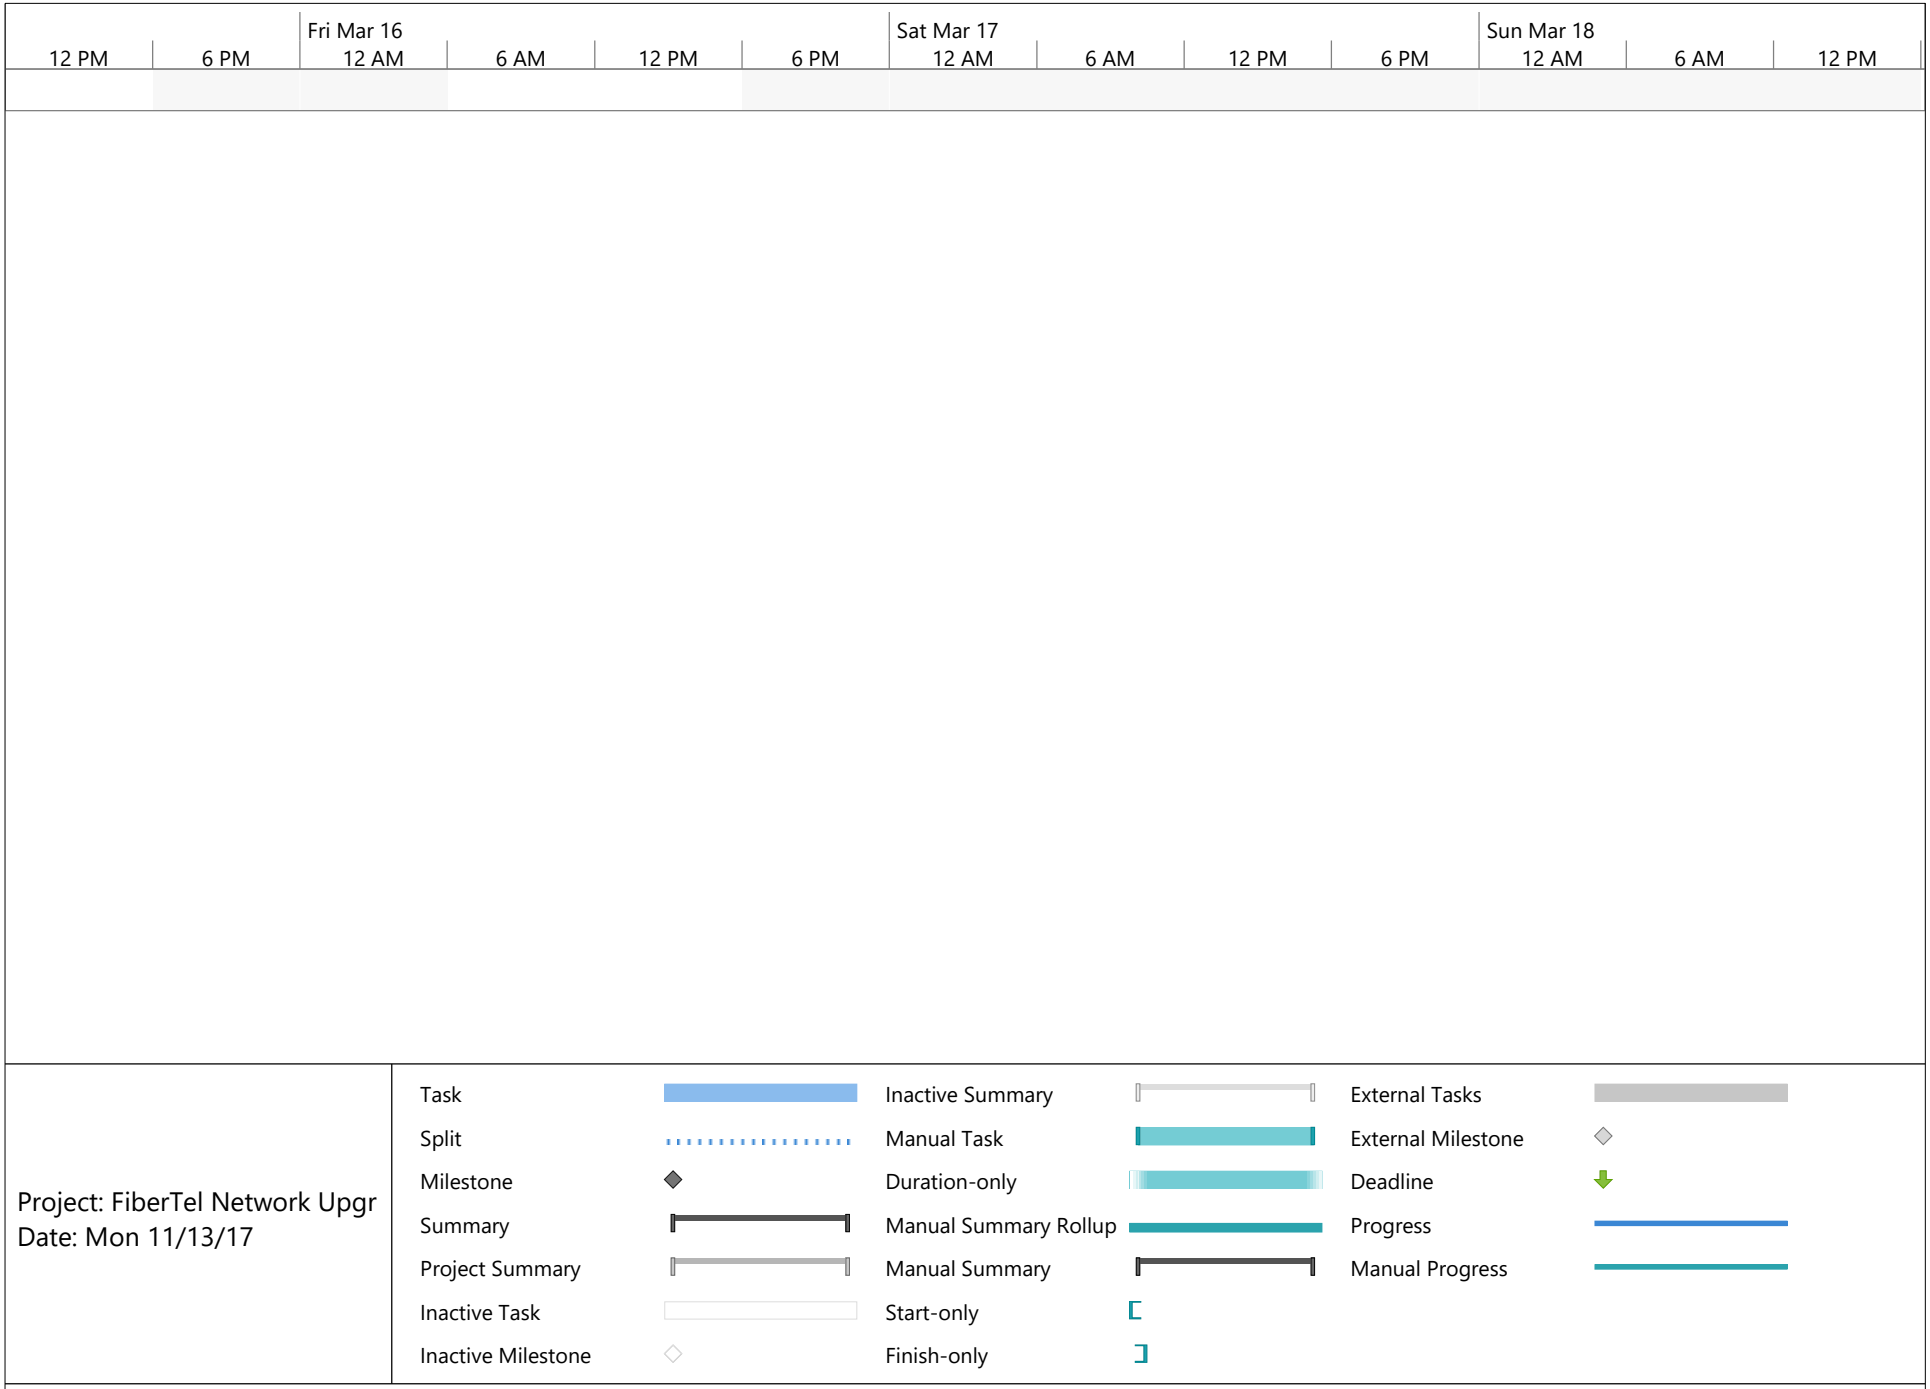
12 PM
6 PM
Fri Mar 16
12 AM
6 AM
12 PM
6 PM
Sat Mar 17
12 AM
6 AM
12 PM
6 PM
Sun Mar 18
12 AM
6 AM
12 PM
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

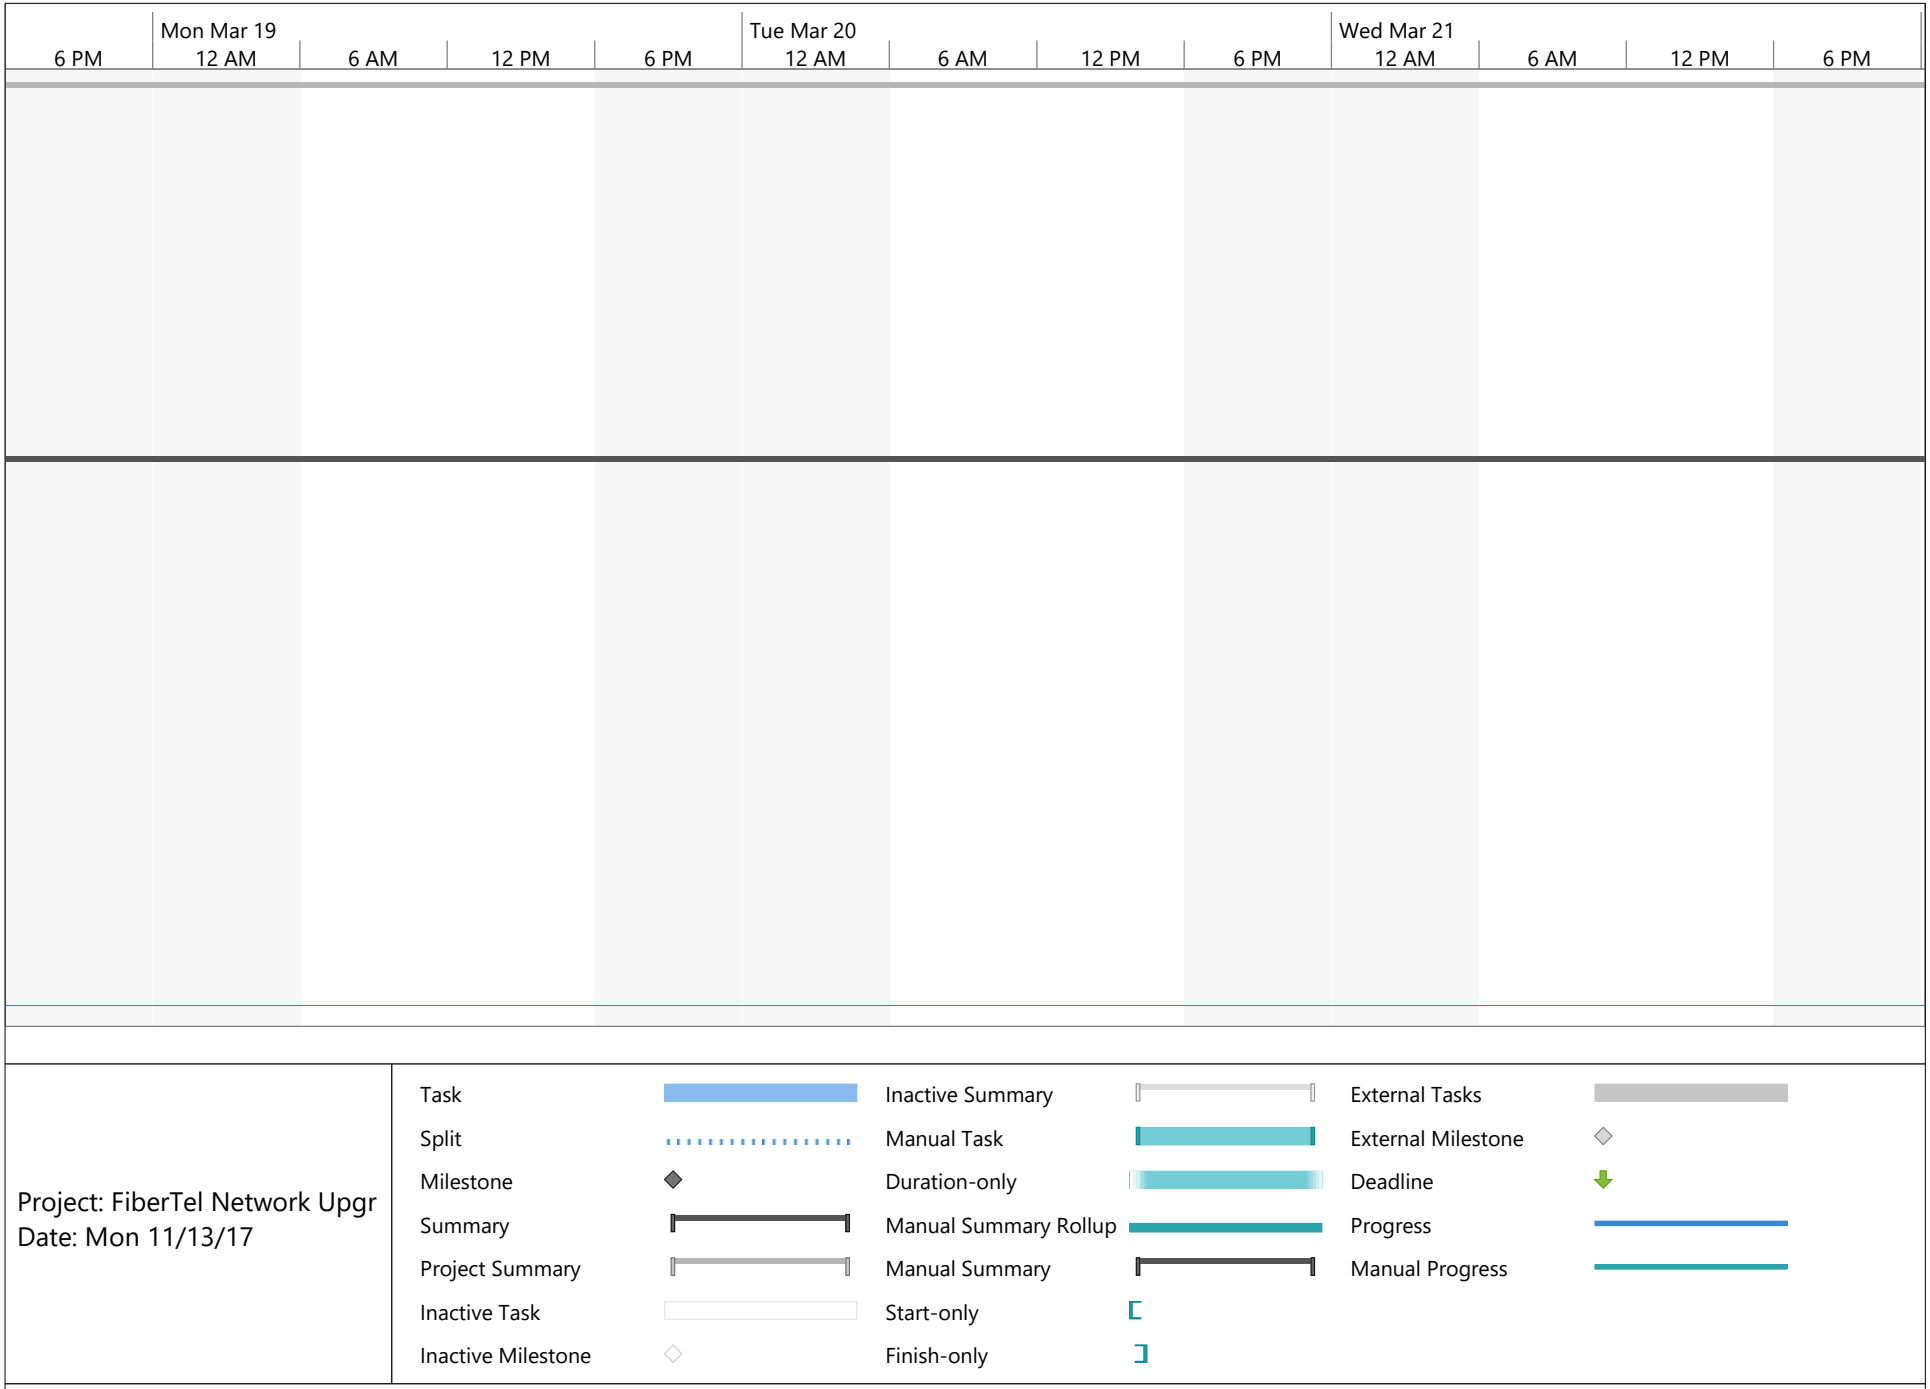

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

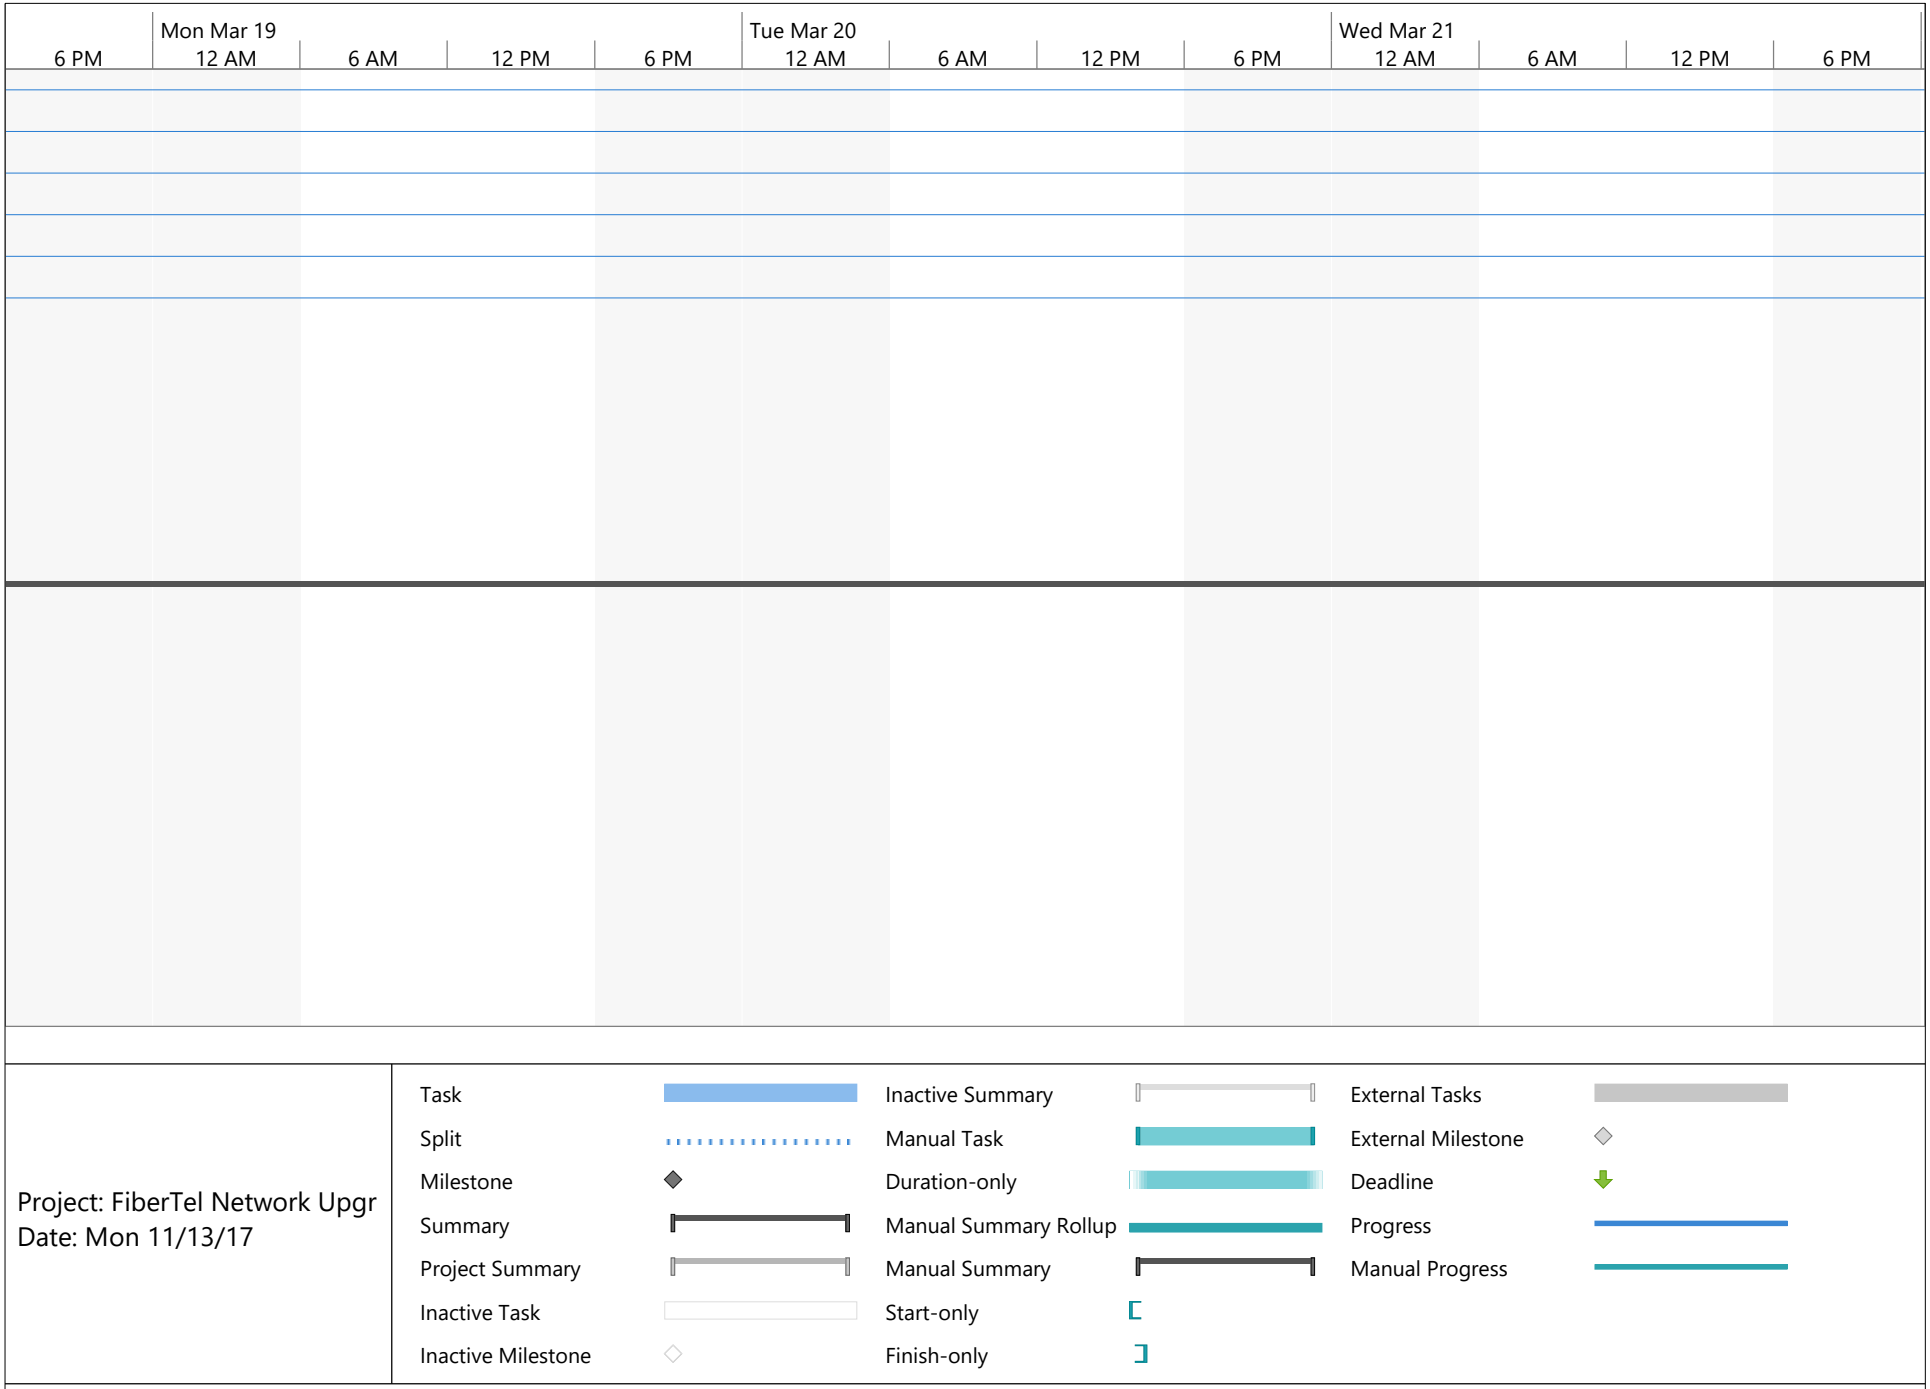

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

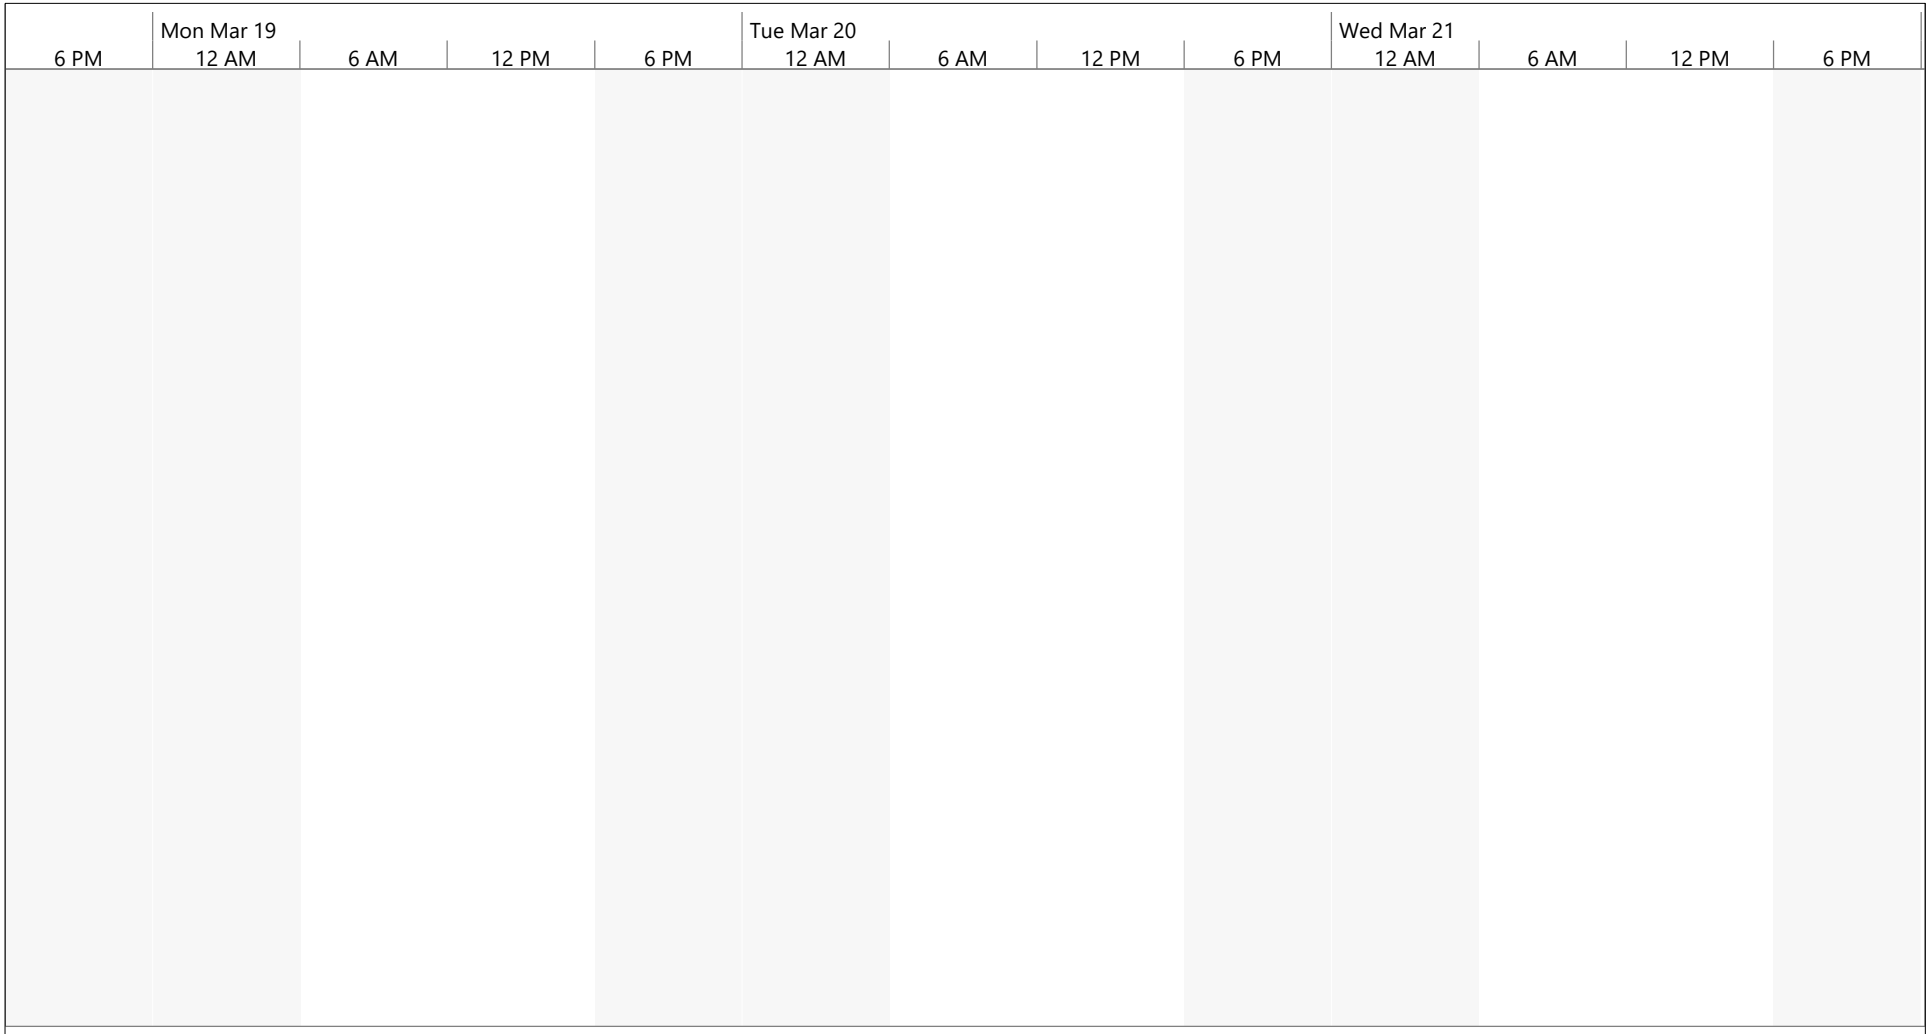

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

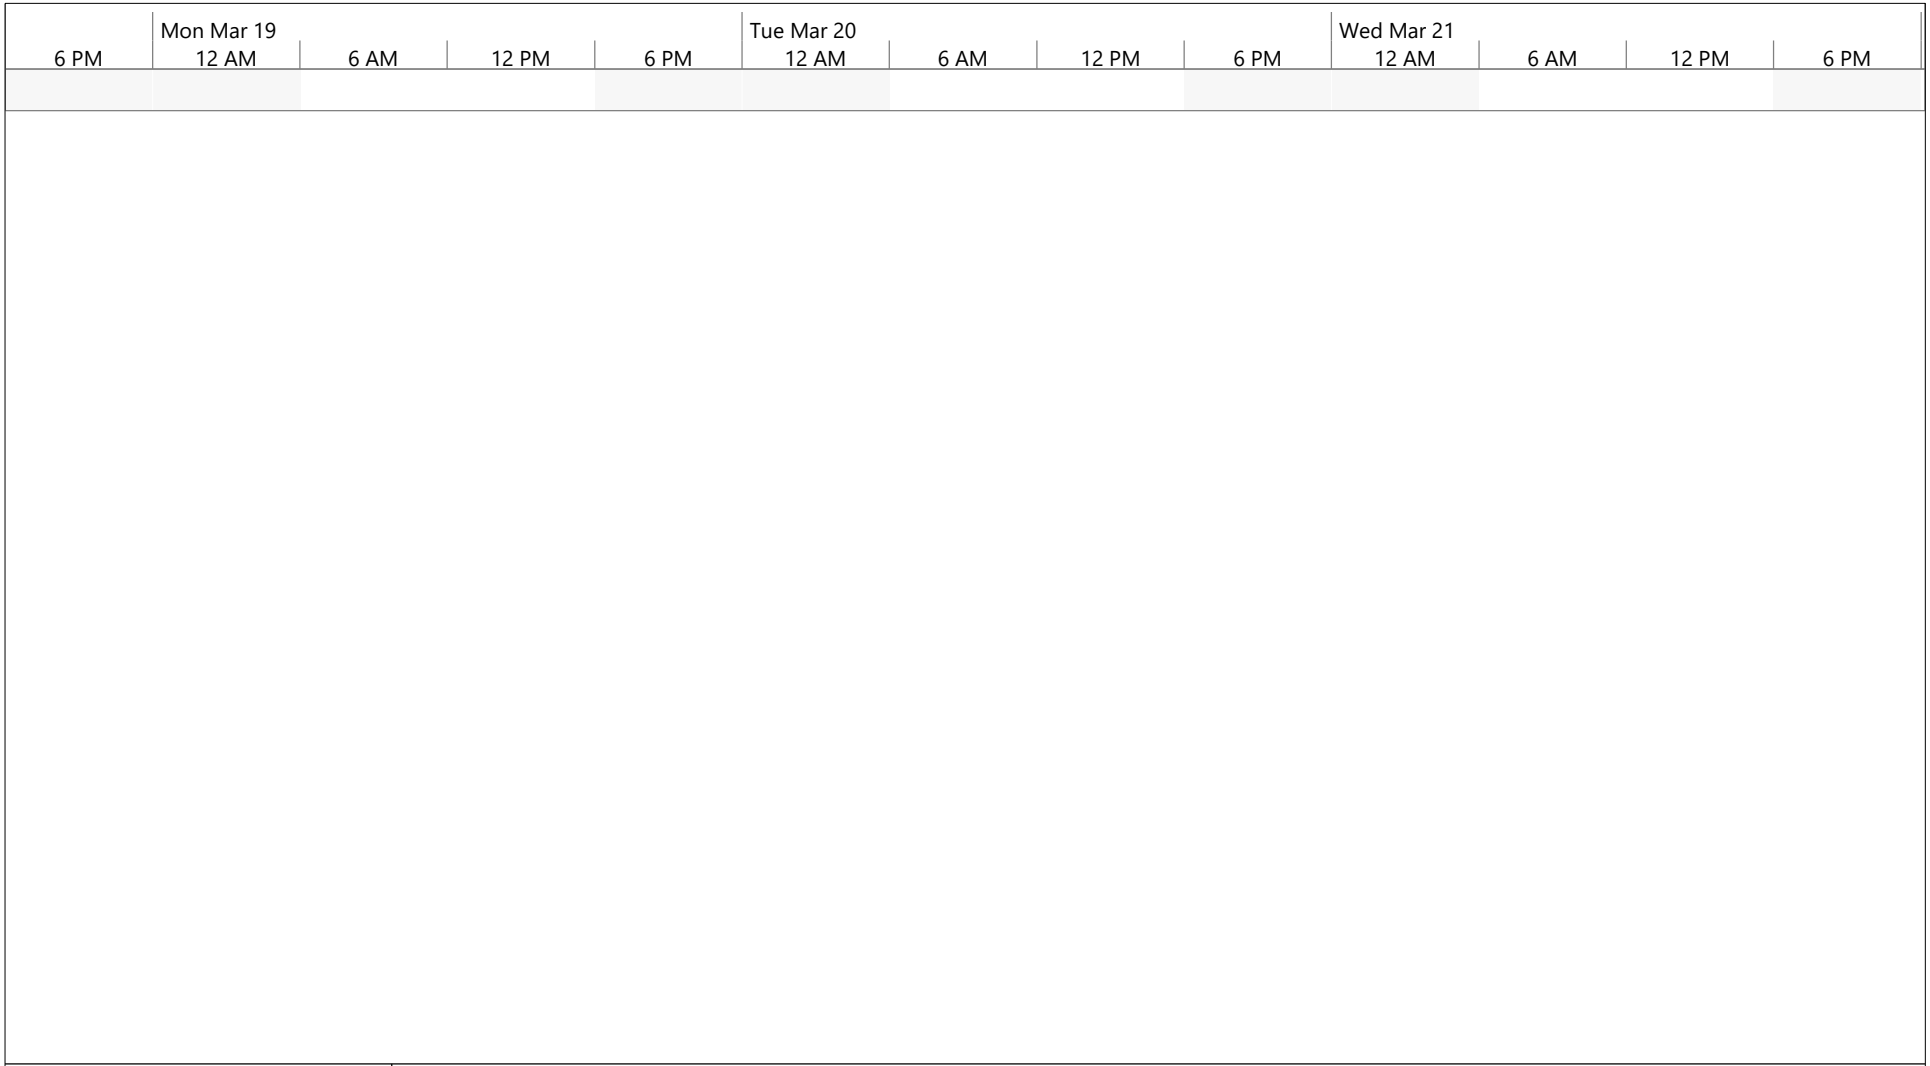

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

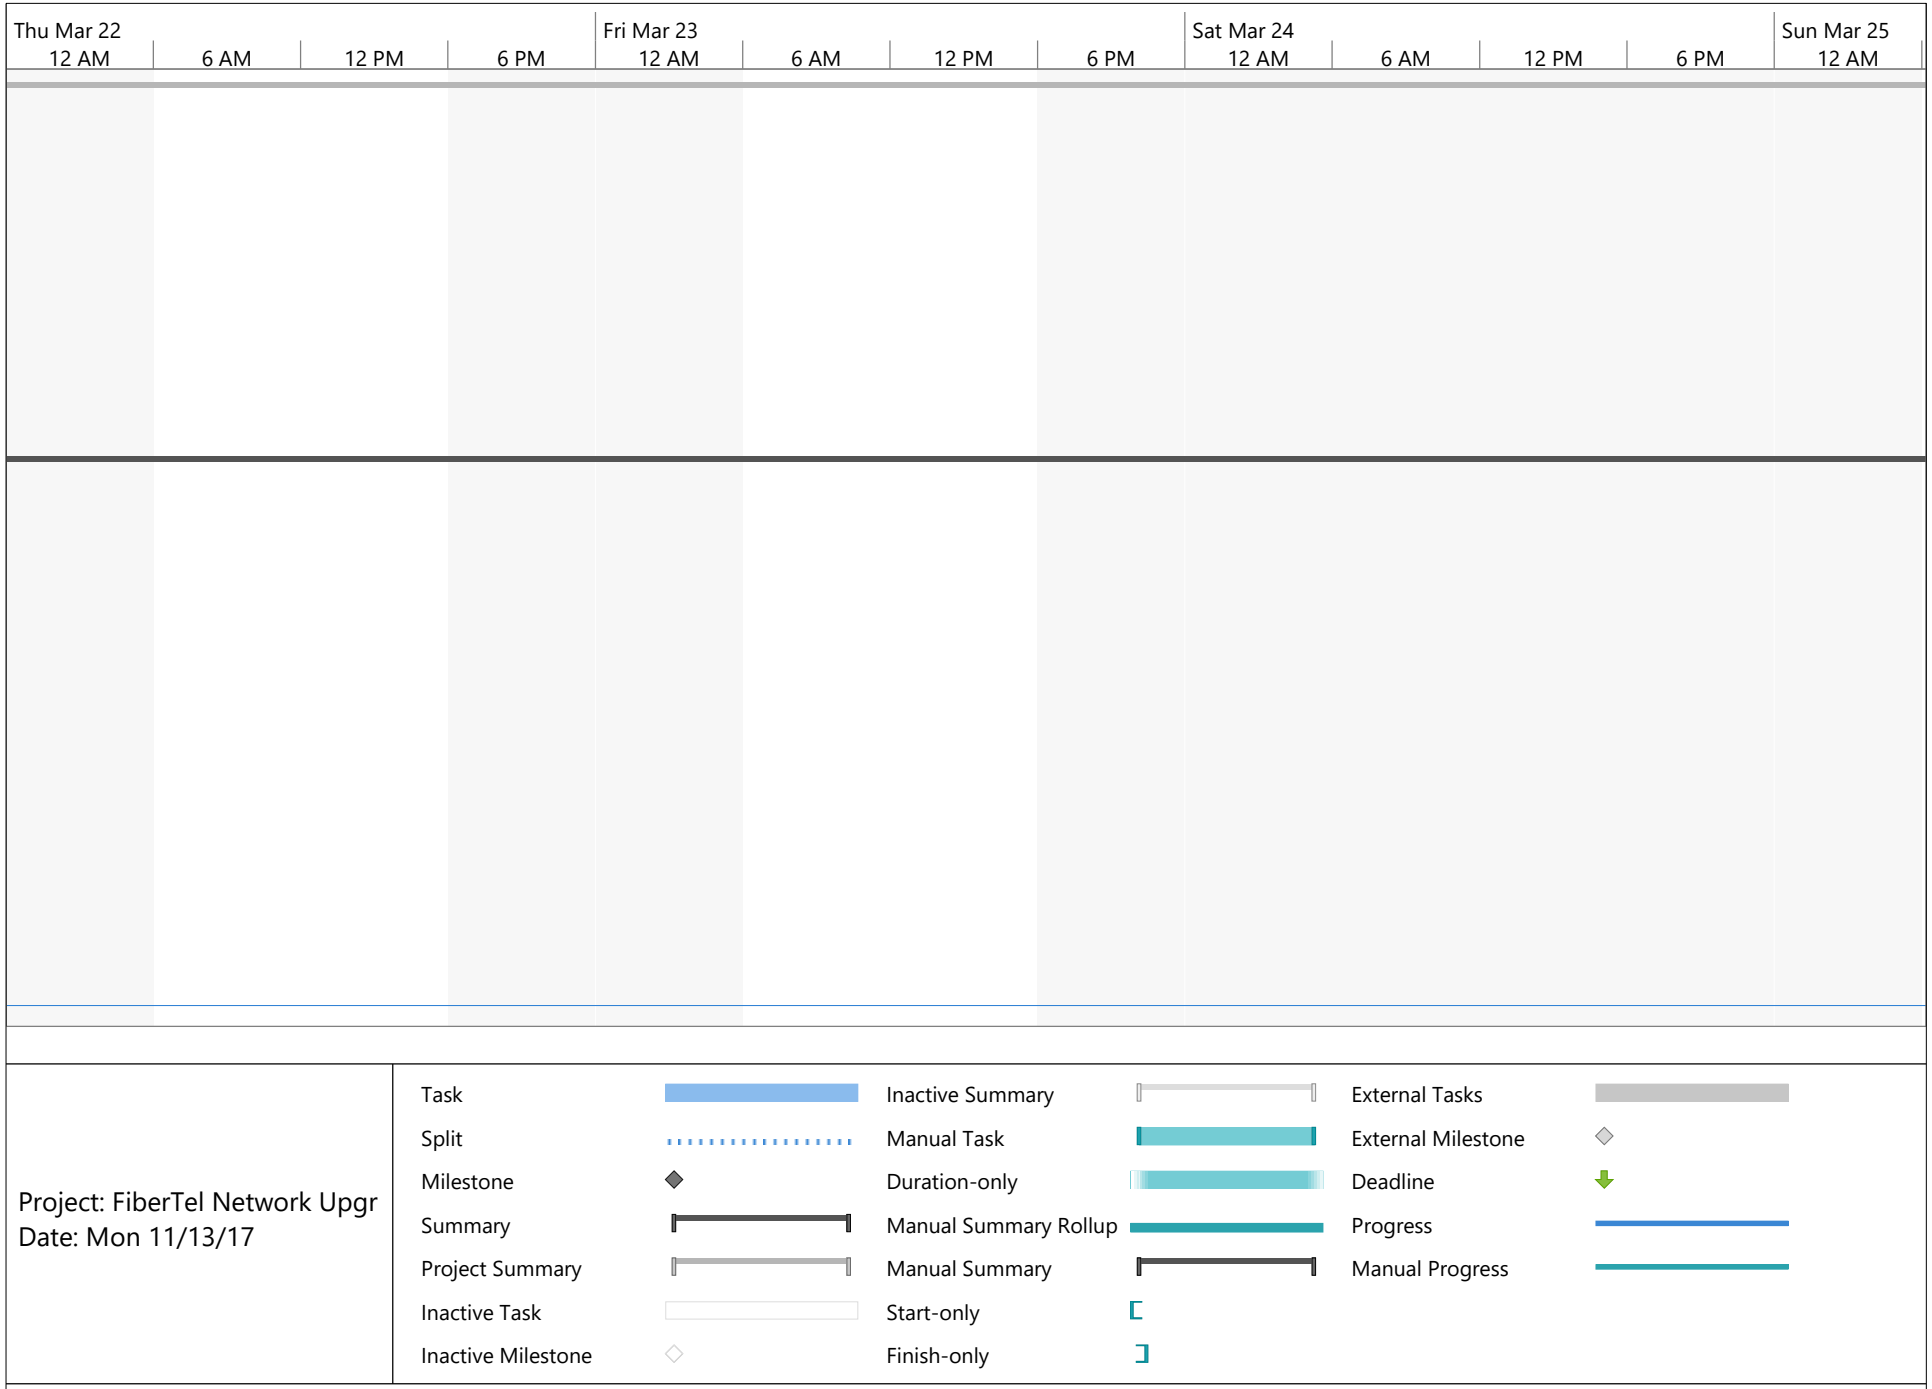

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

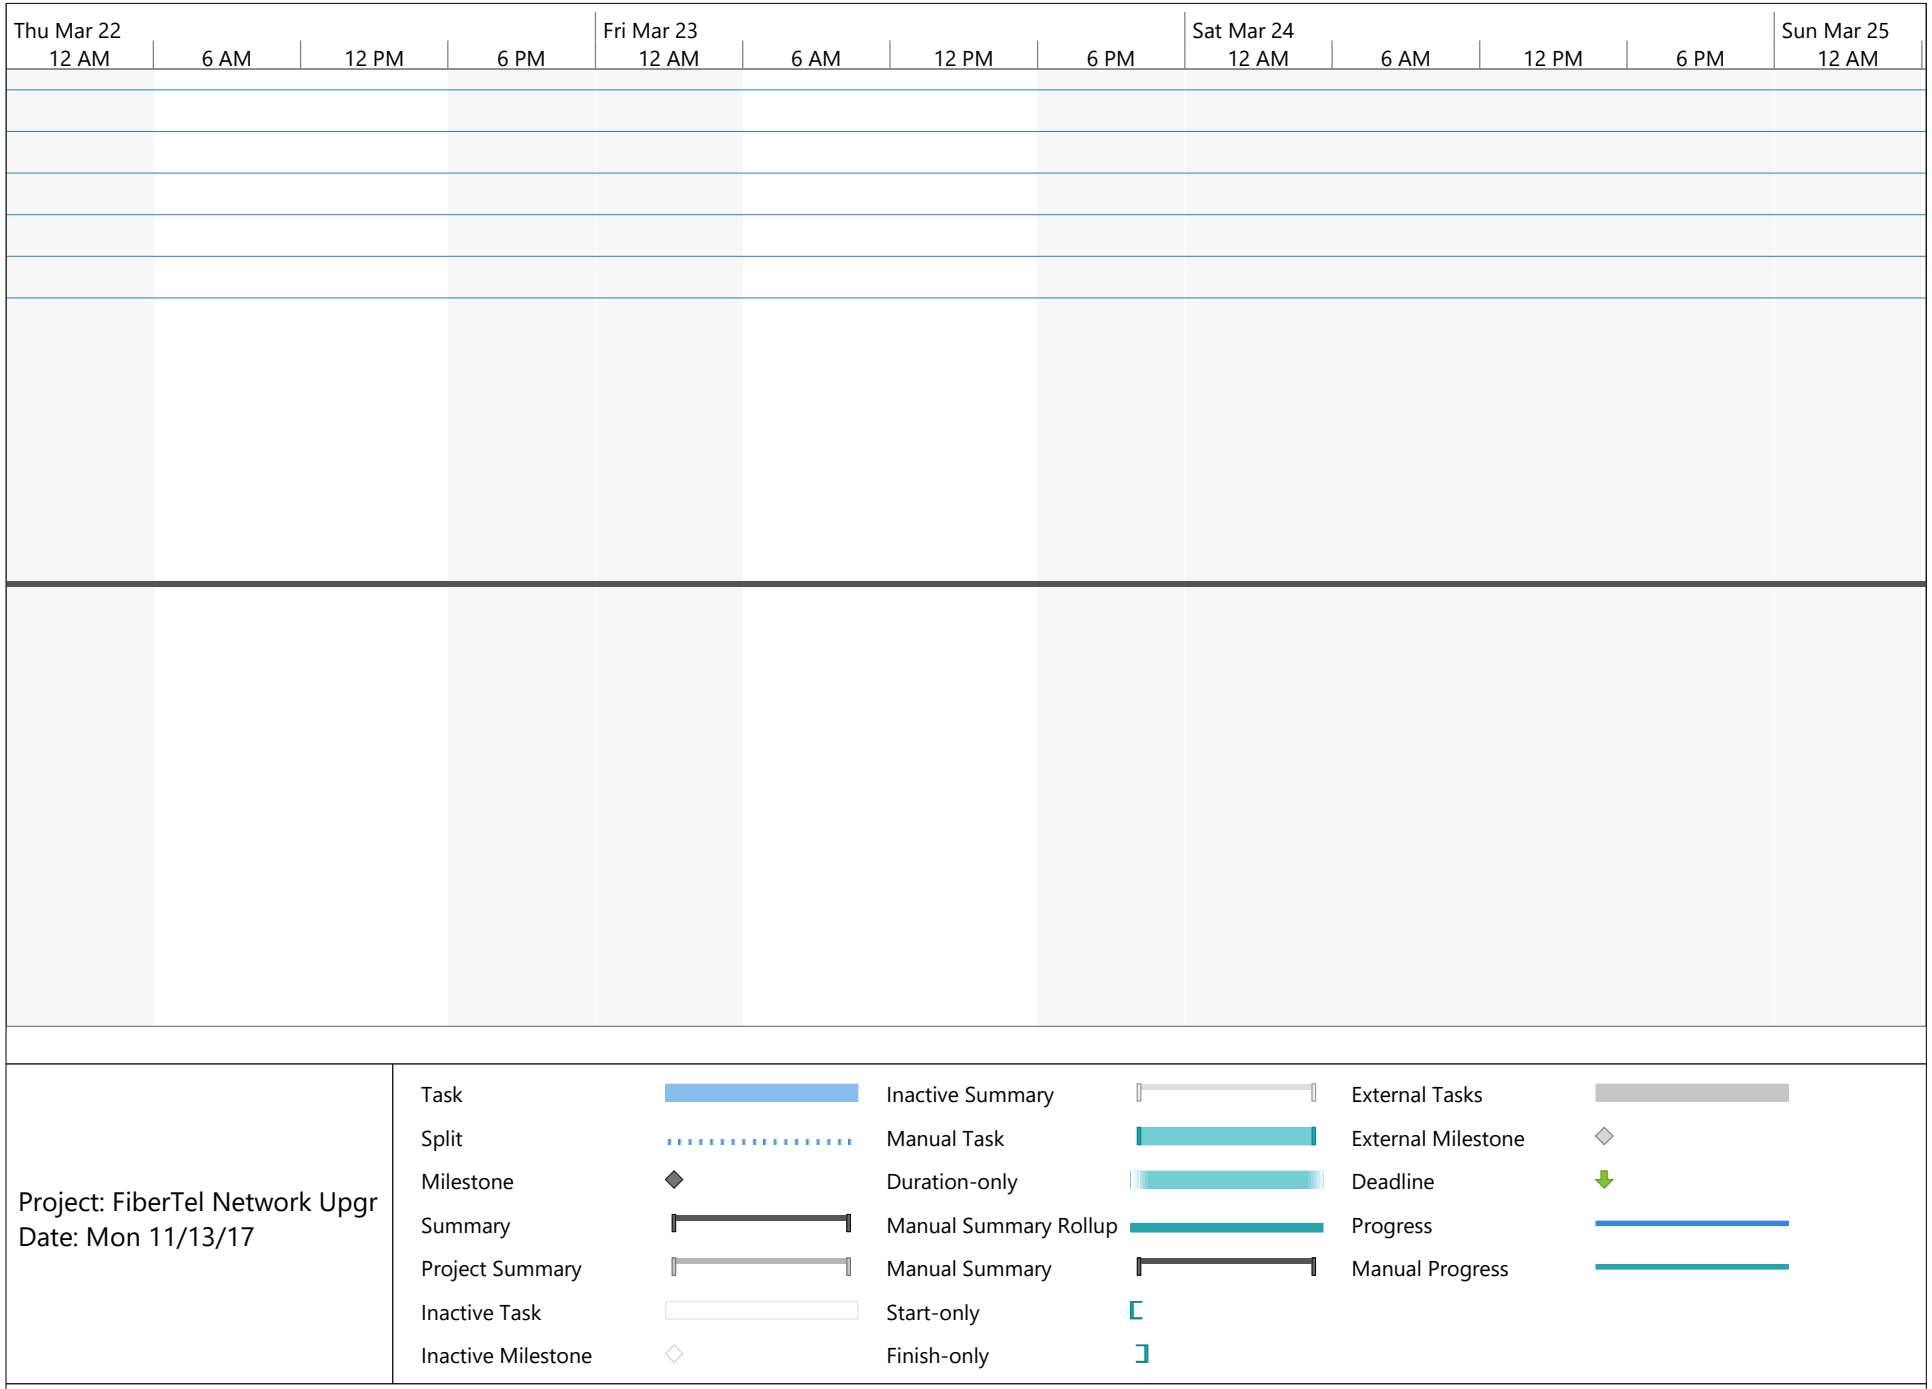

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

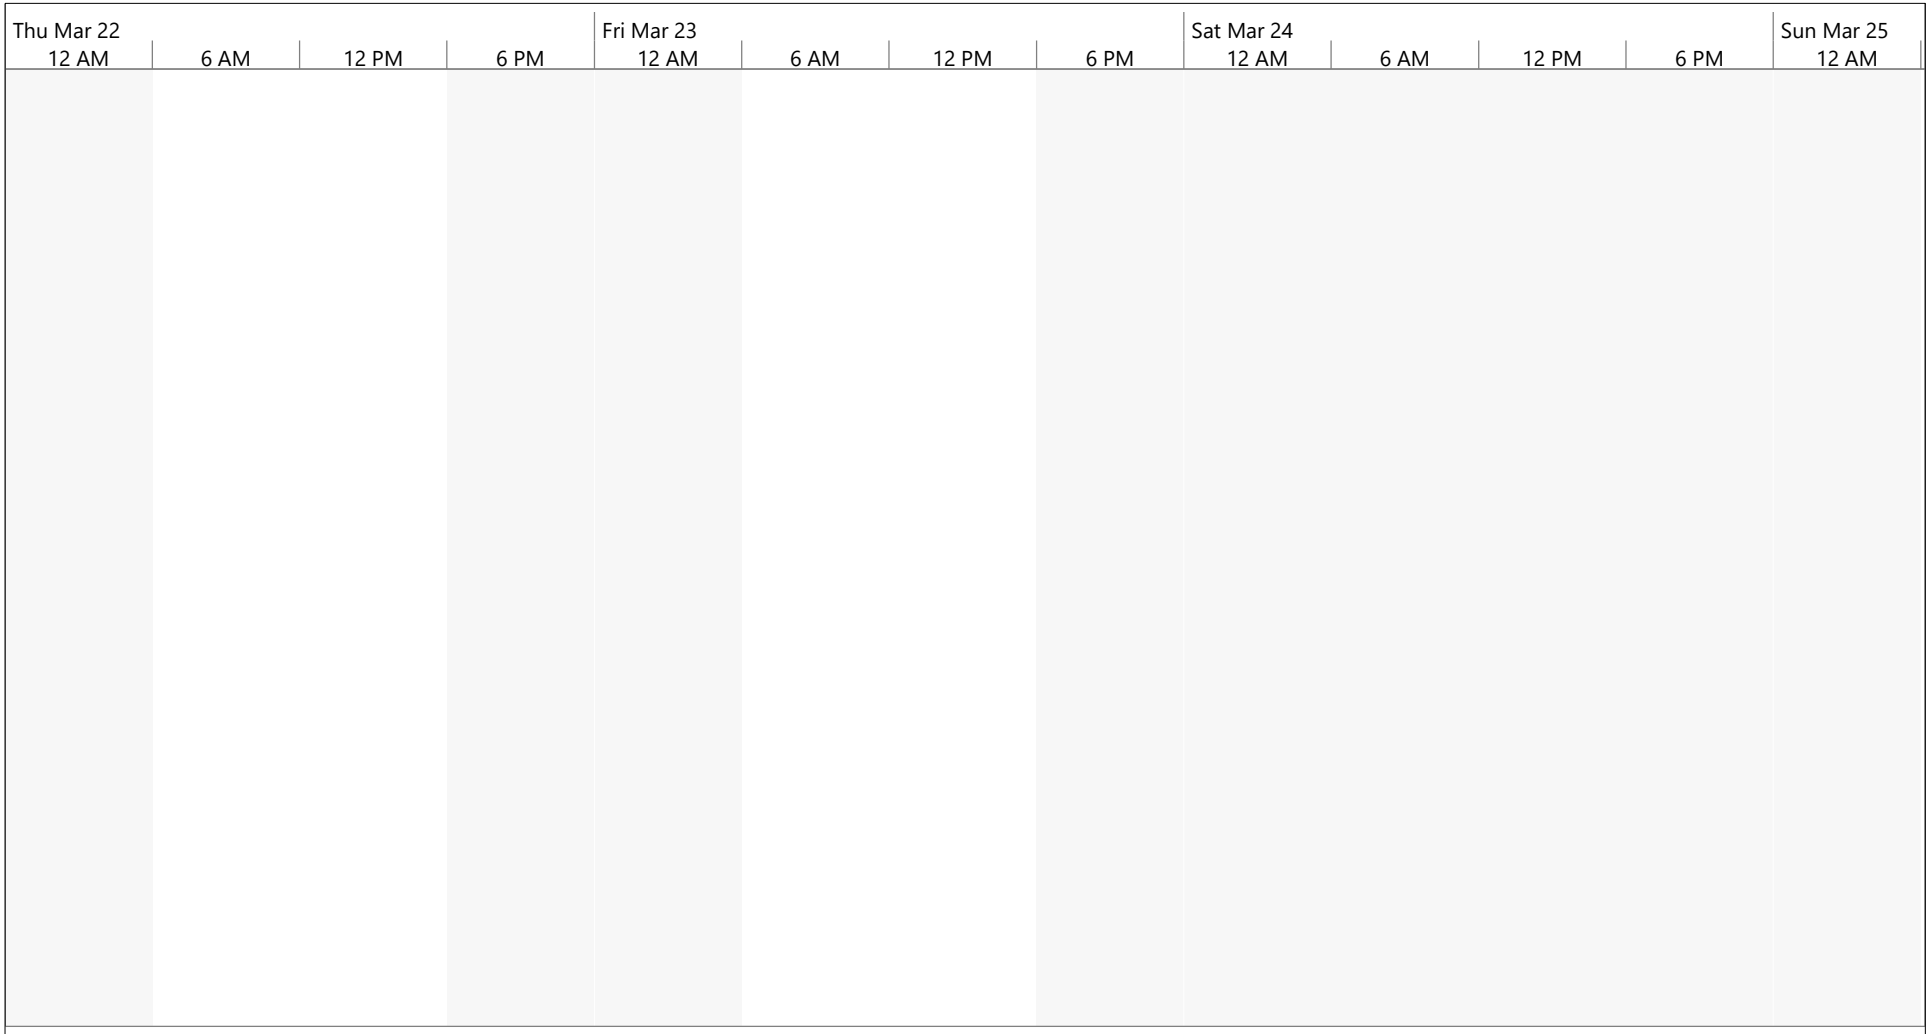

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

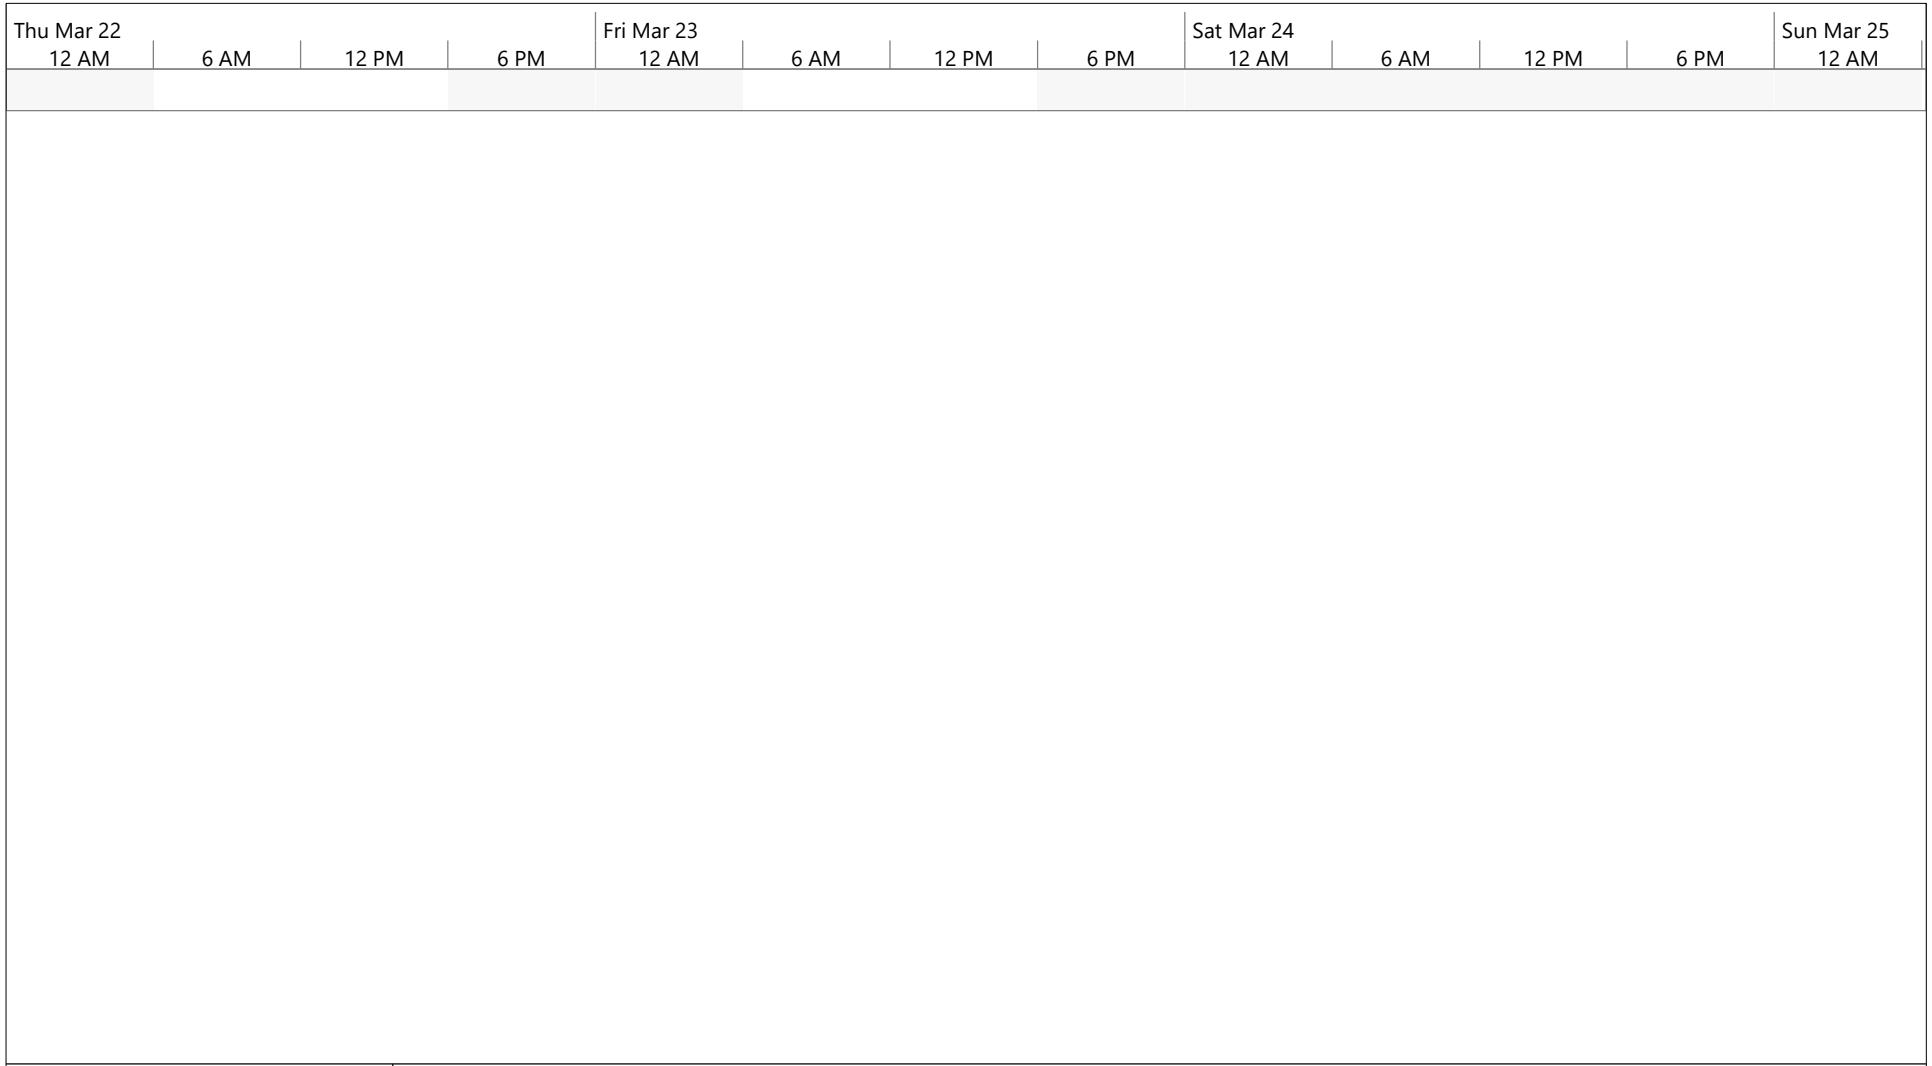

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

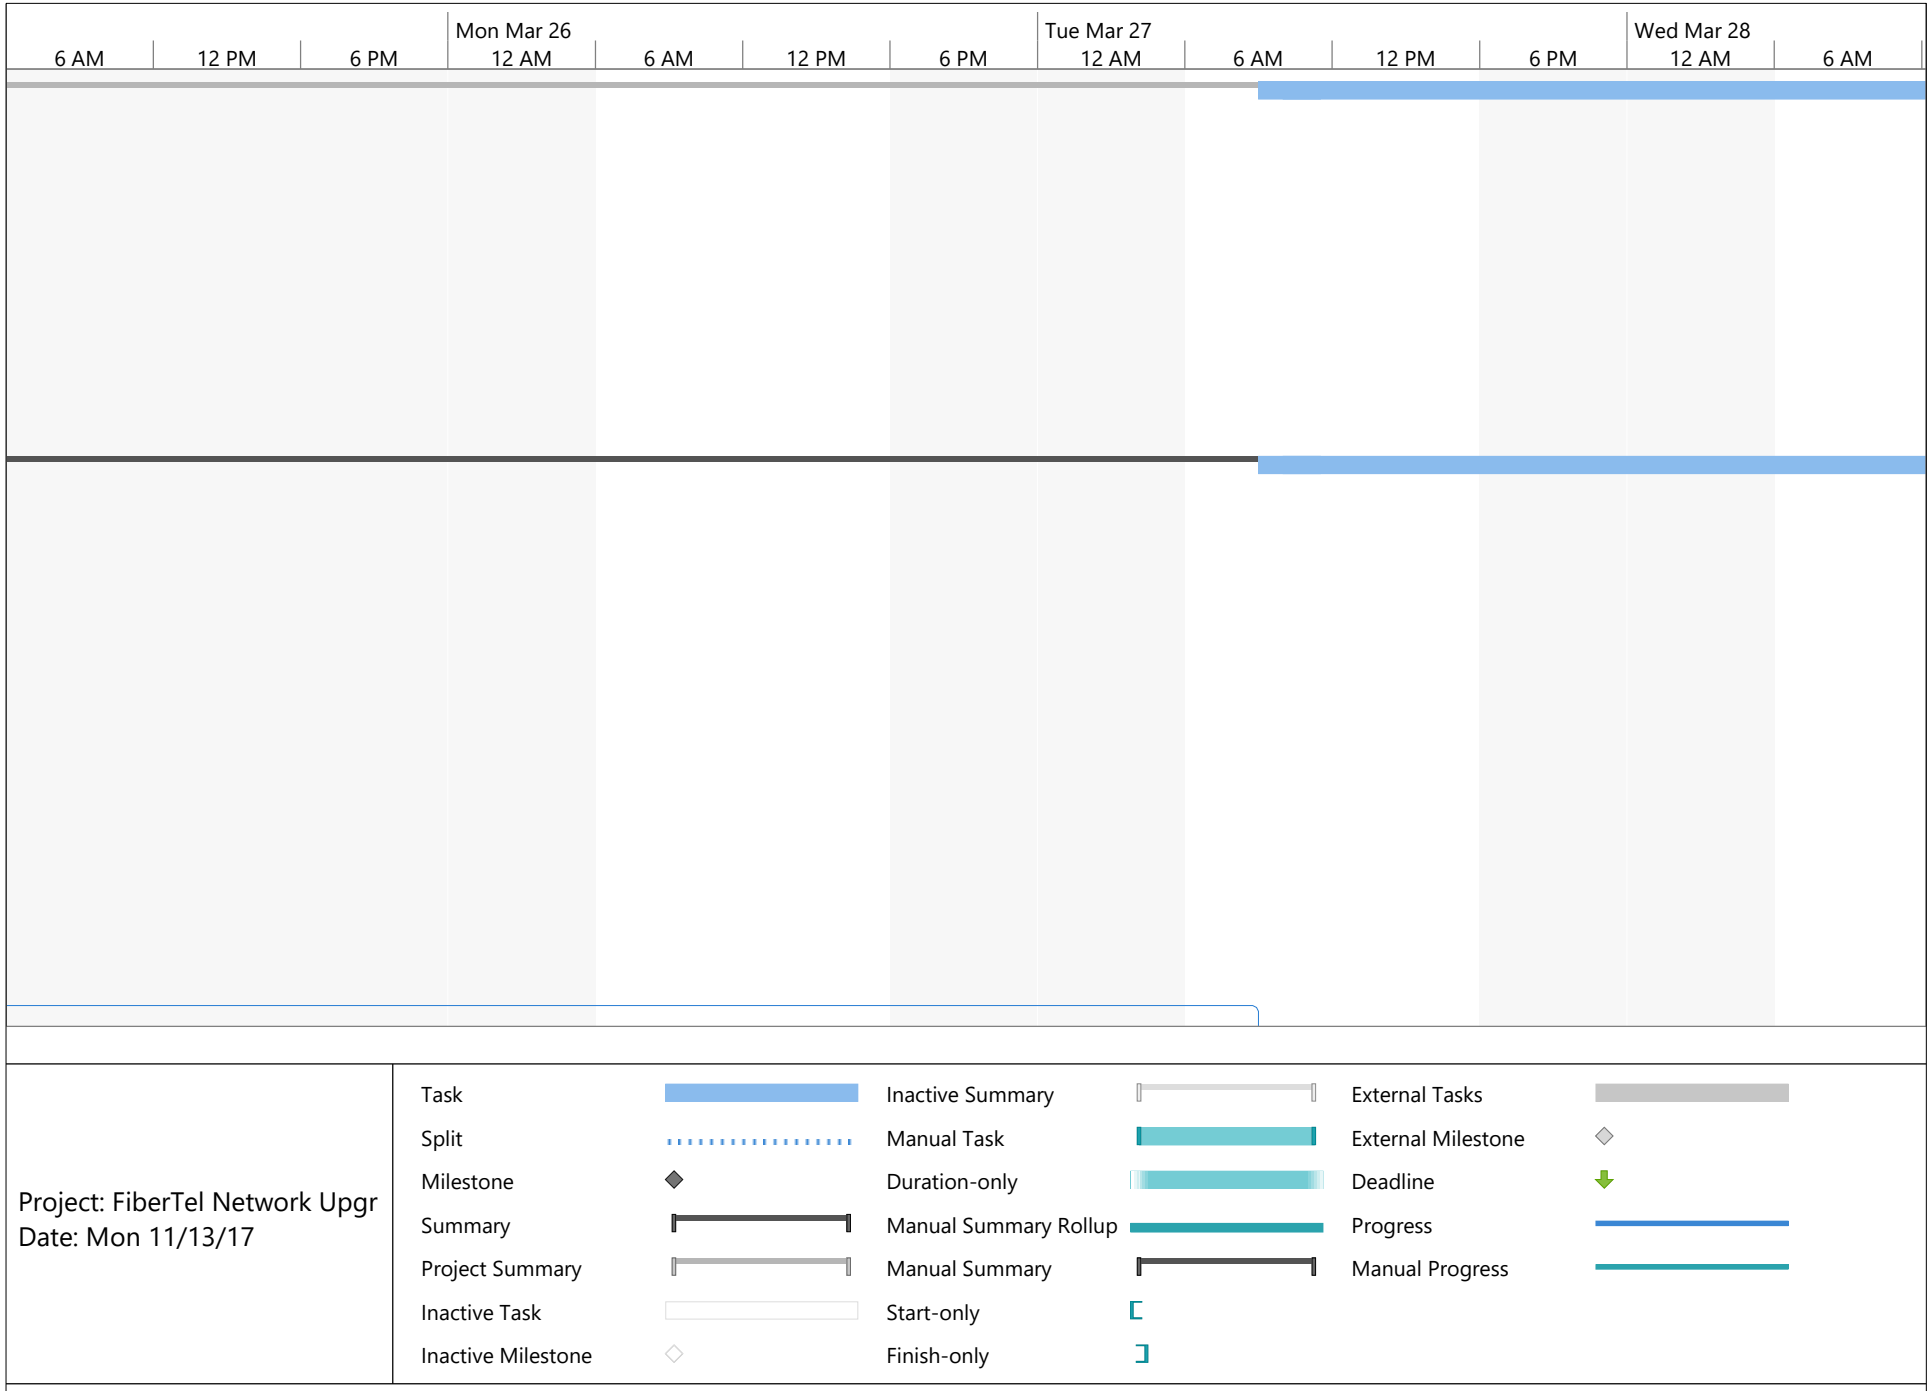

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

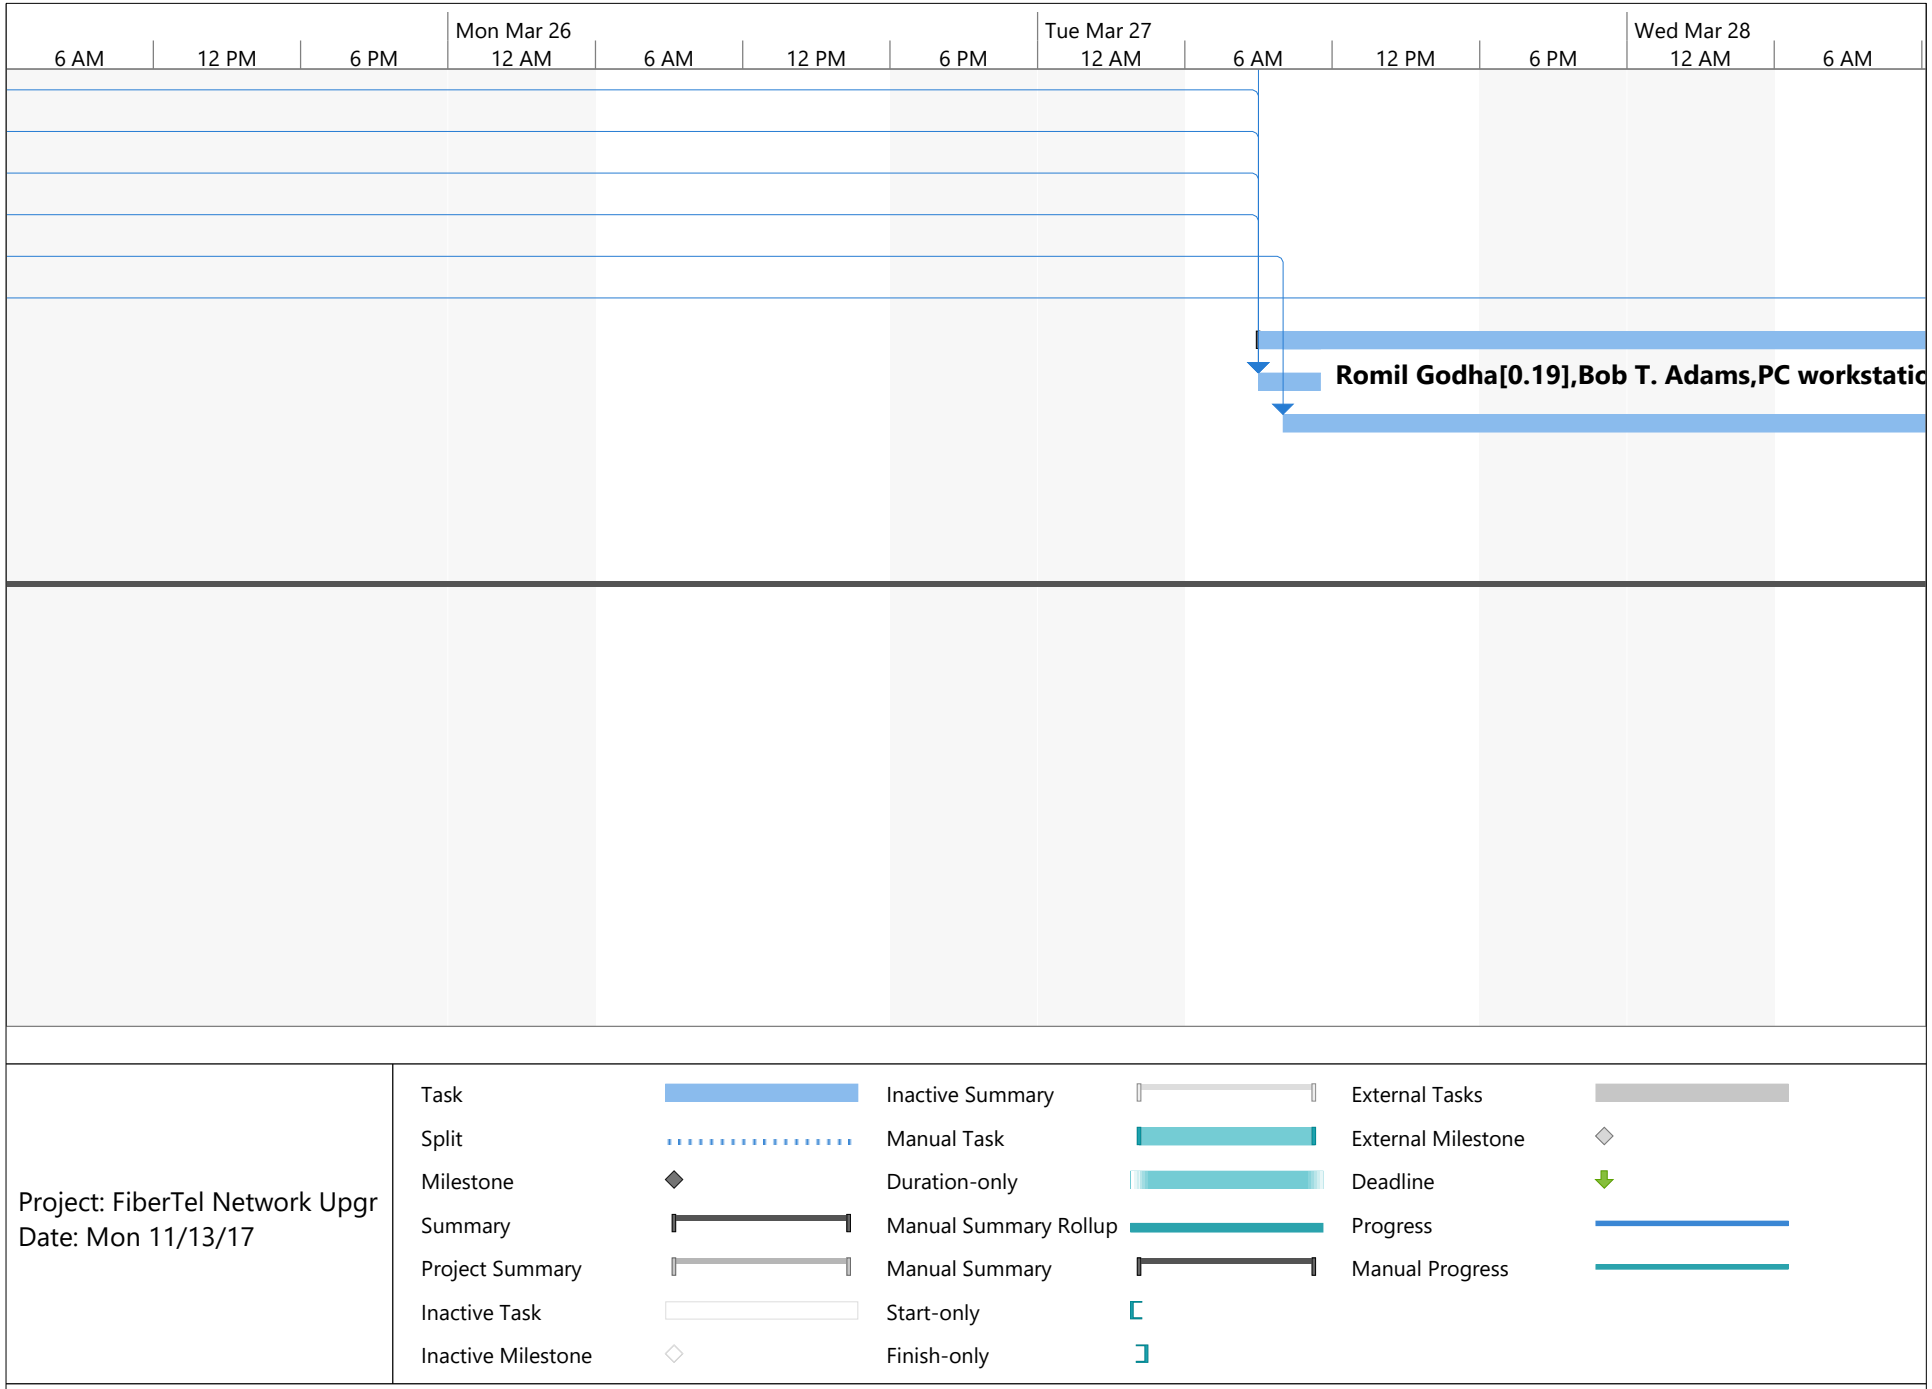
6 AM
12 PM
6 PM
Mon Mar 26
12 AM
6 AM
12 PM
6 PM
Tue Mar 27
12 AM
6 AM
12 PM
6 PM
Wed Mar 28
12 AM
6 AM
Romil Godha[0.19],Bob T. Adams,PC workstatic
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

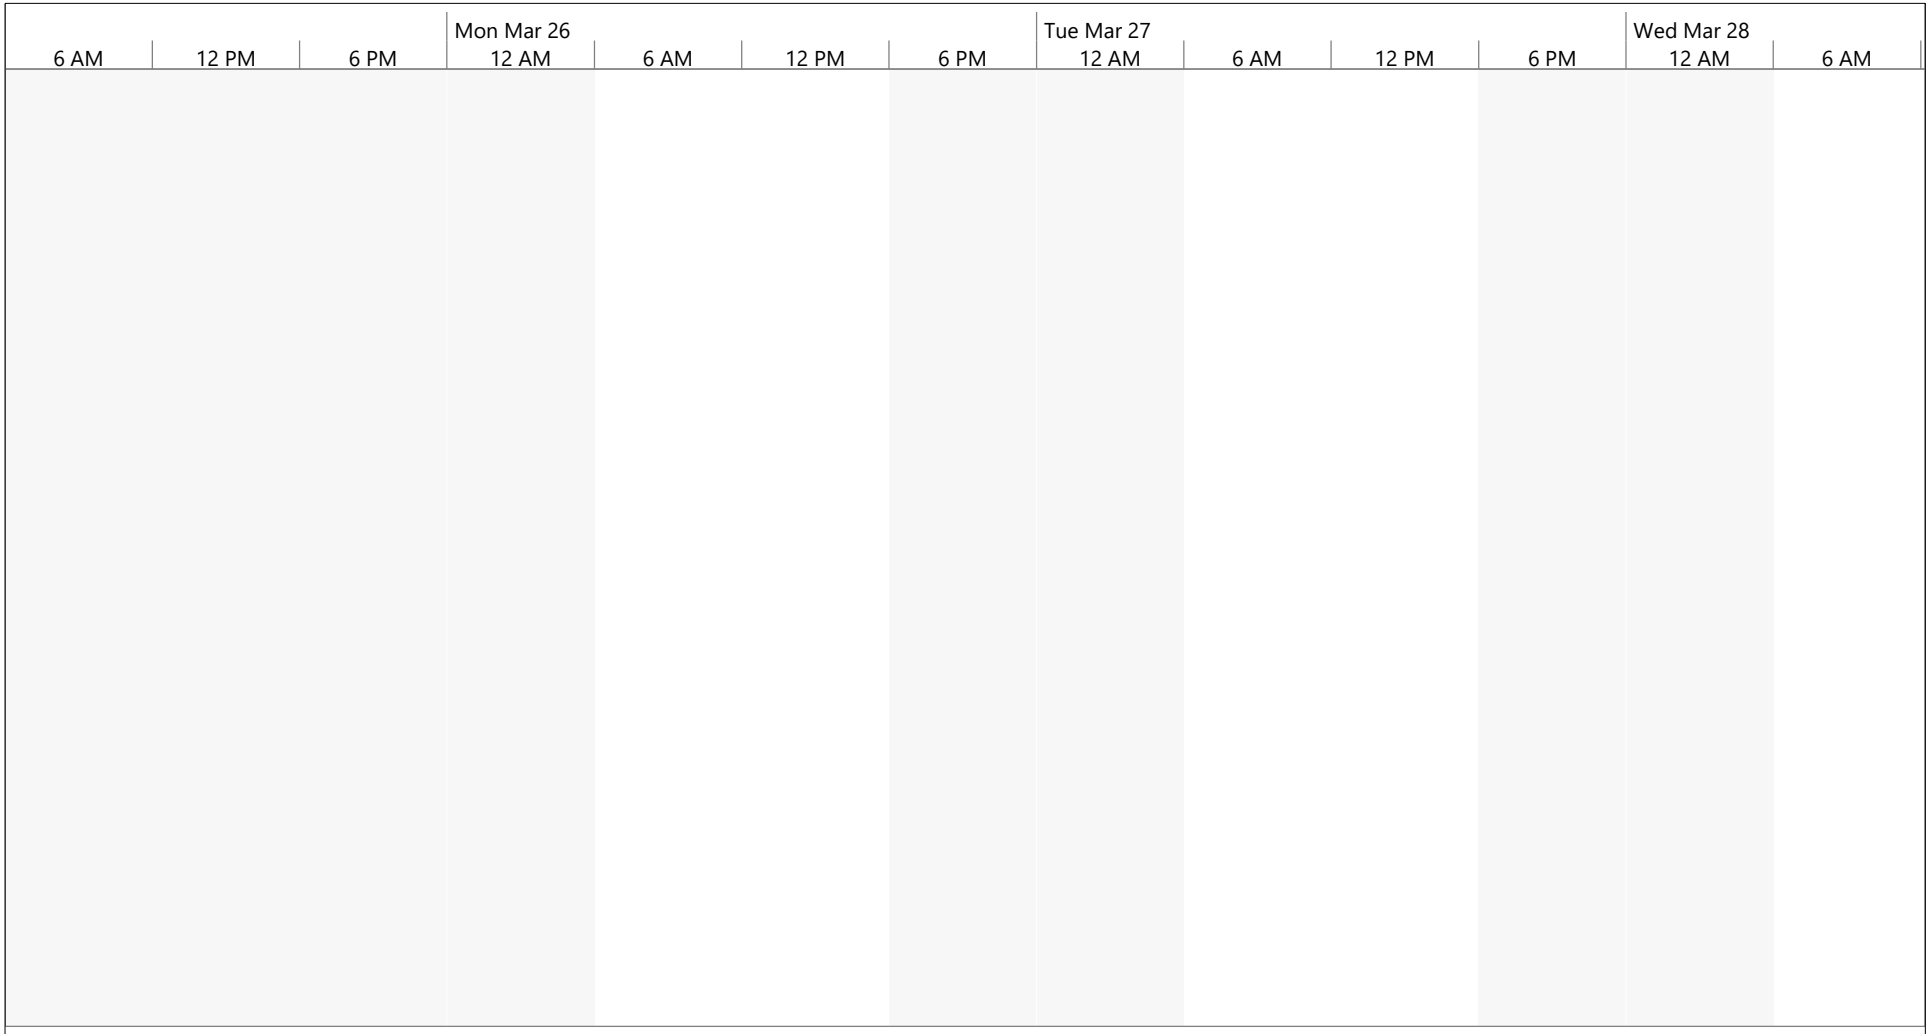

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

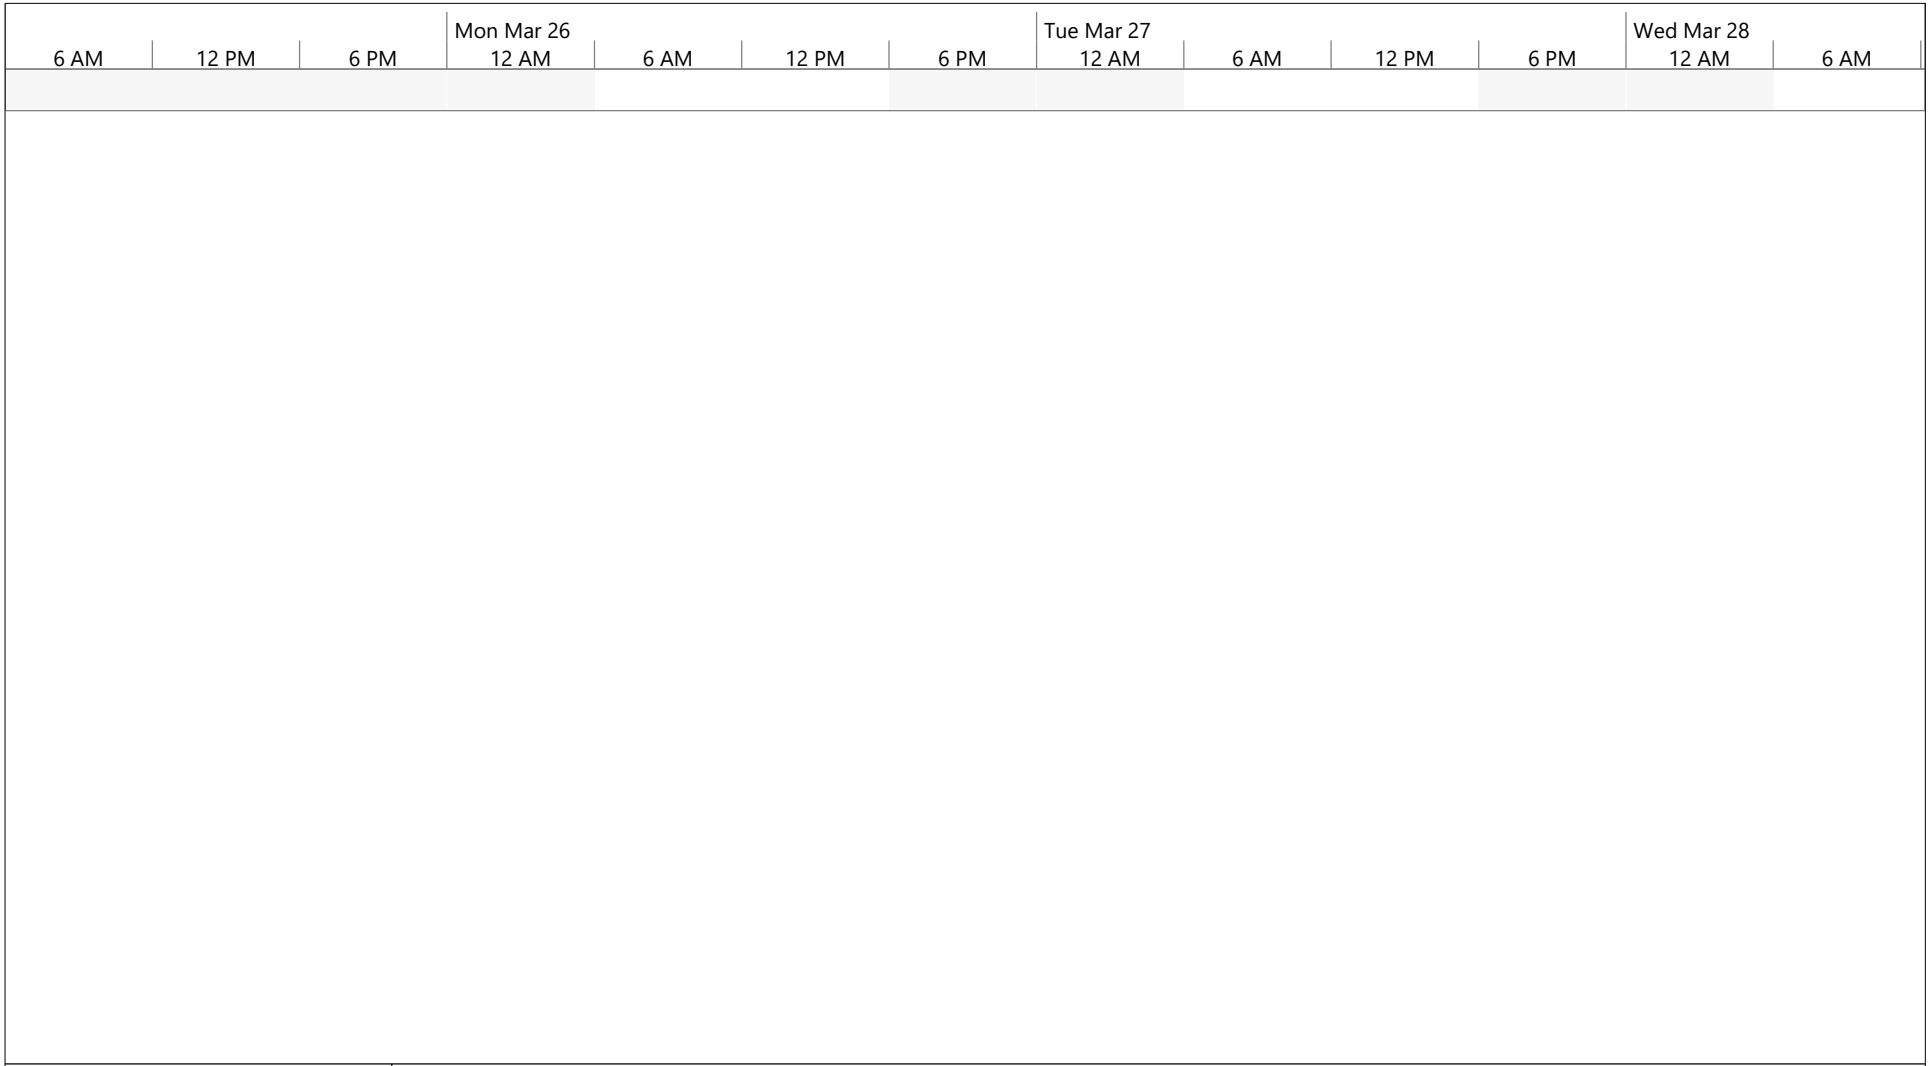

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

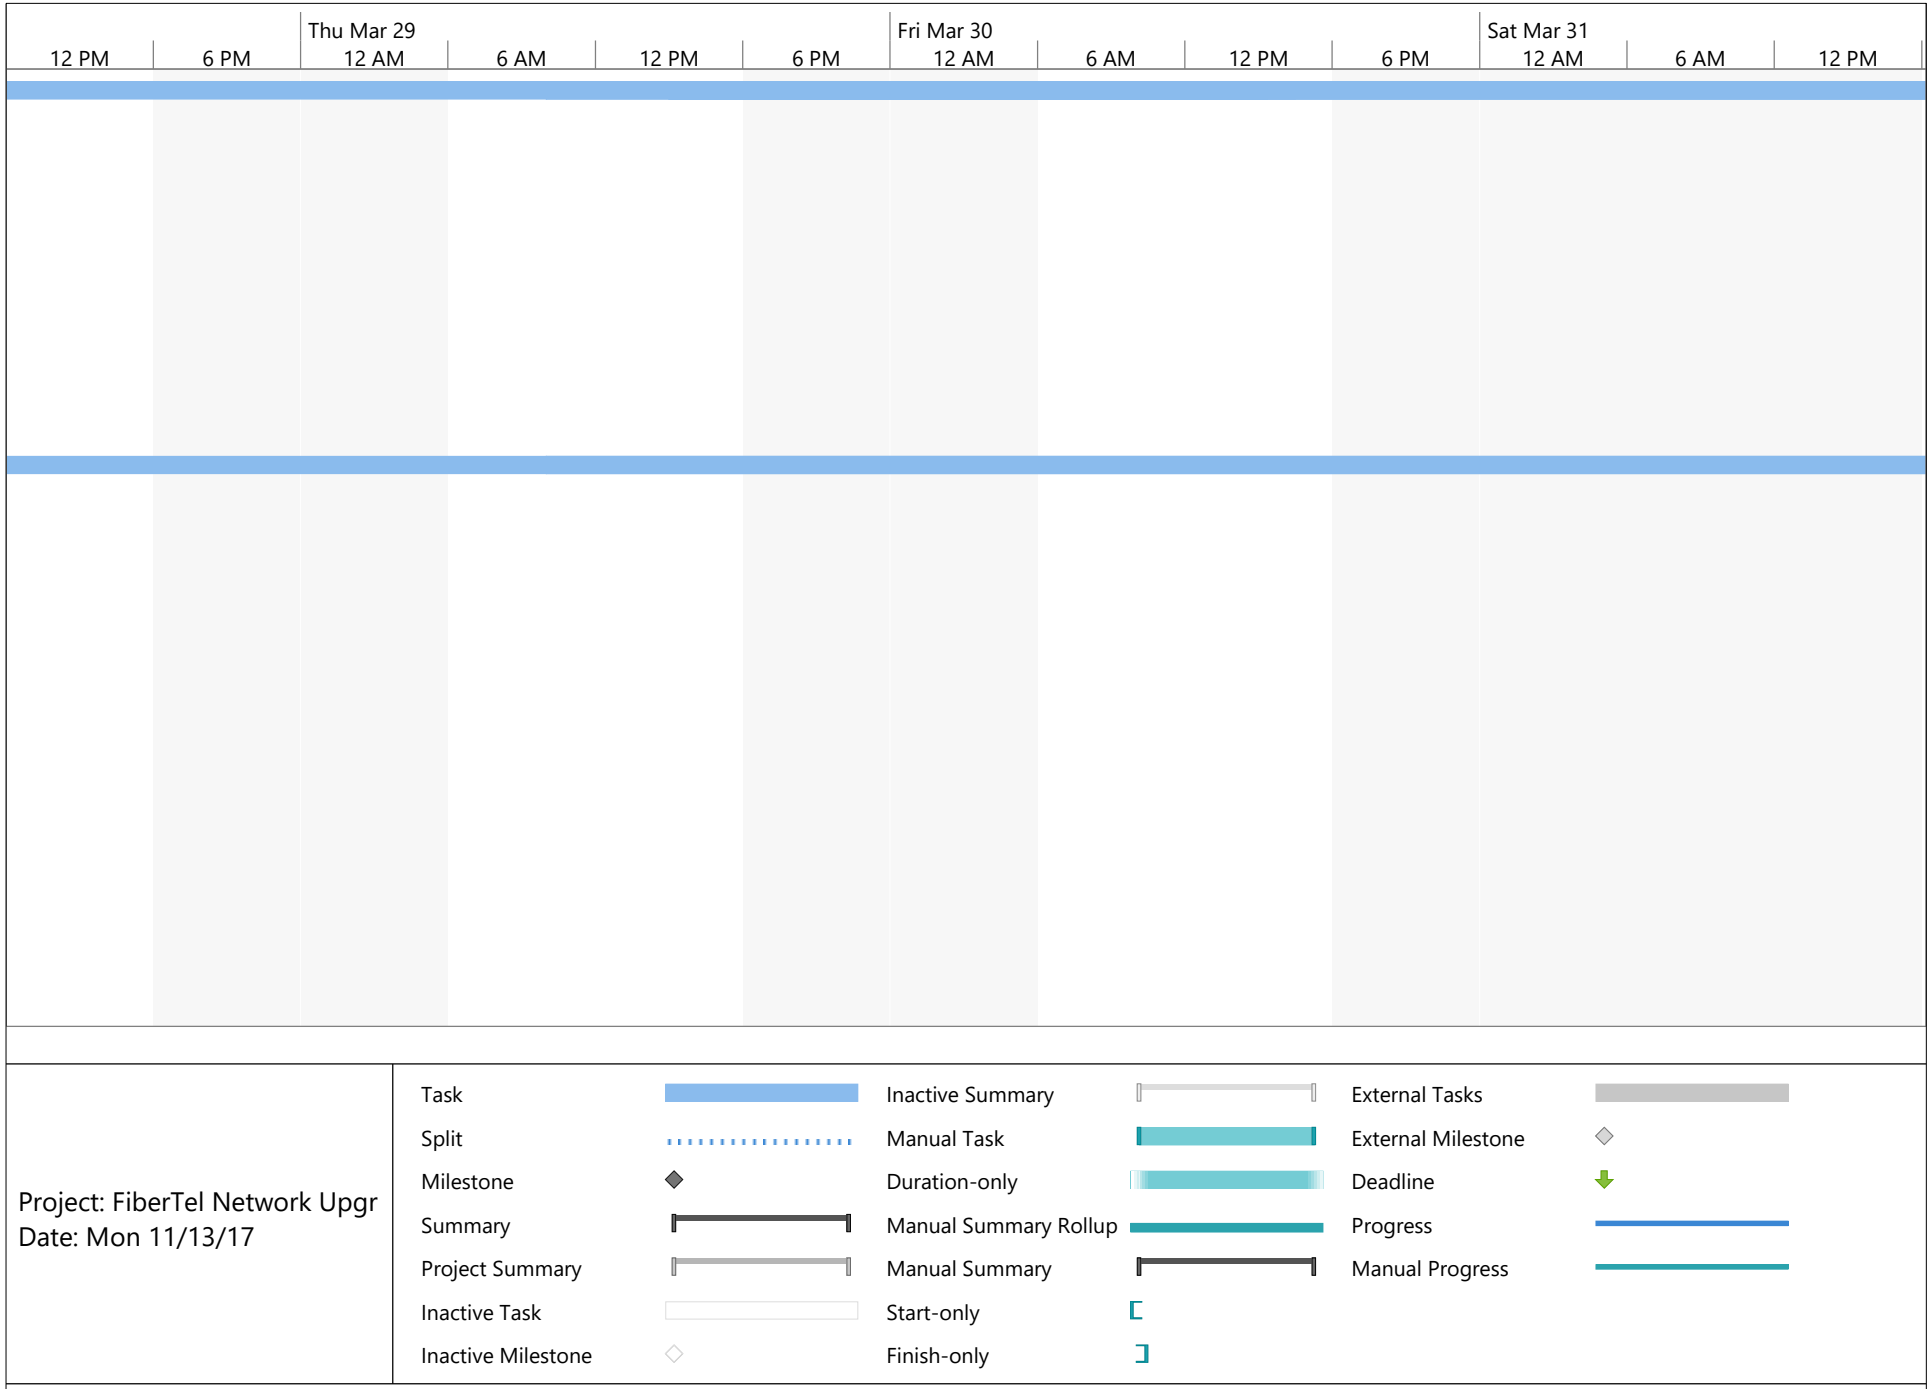

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

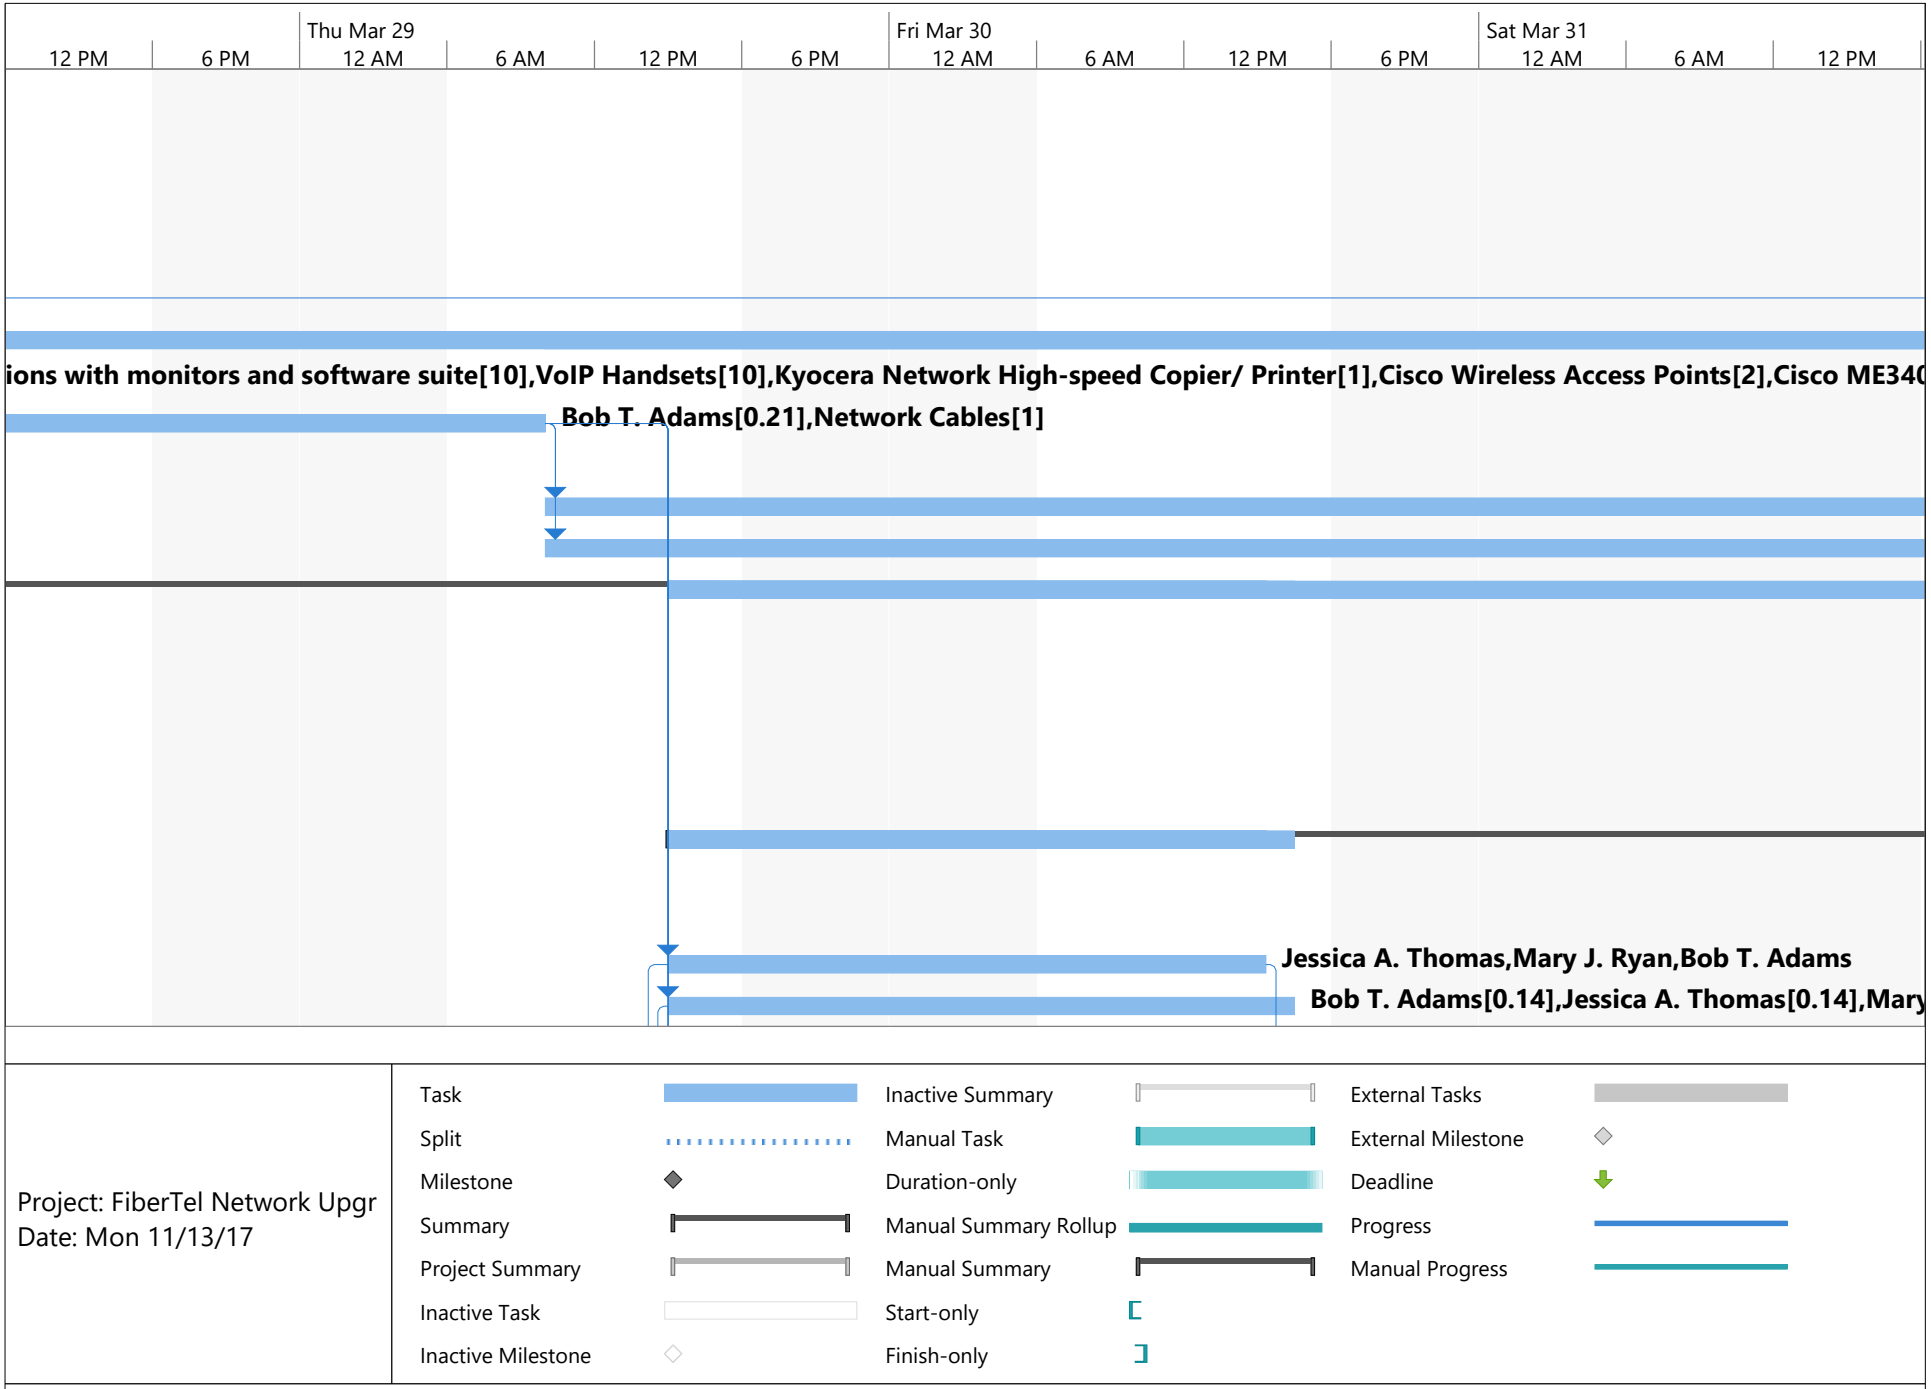

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

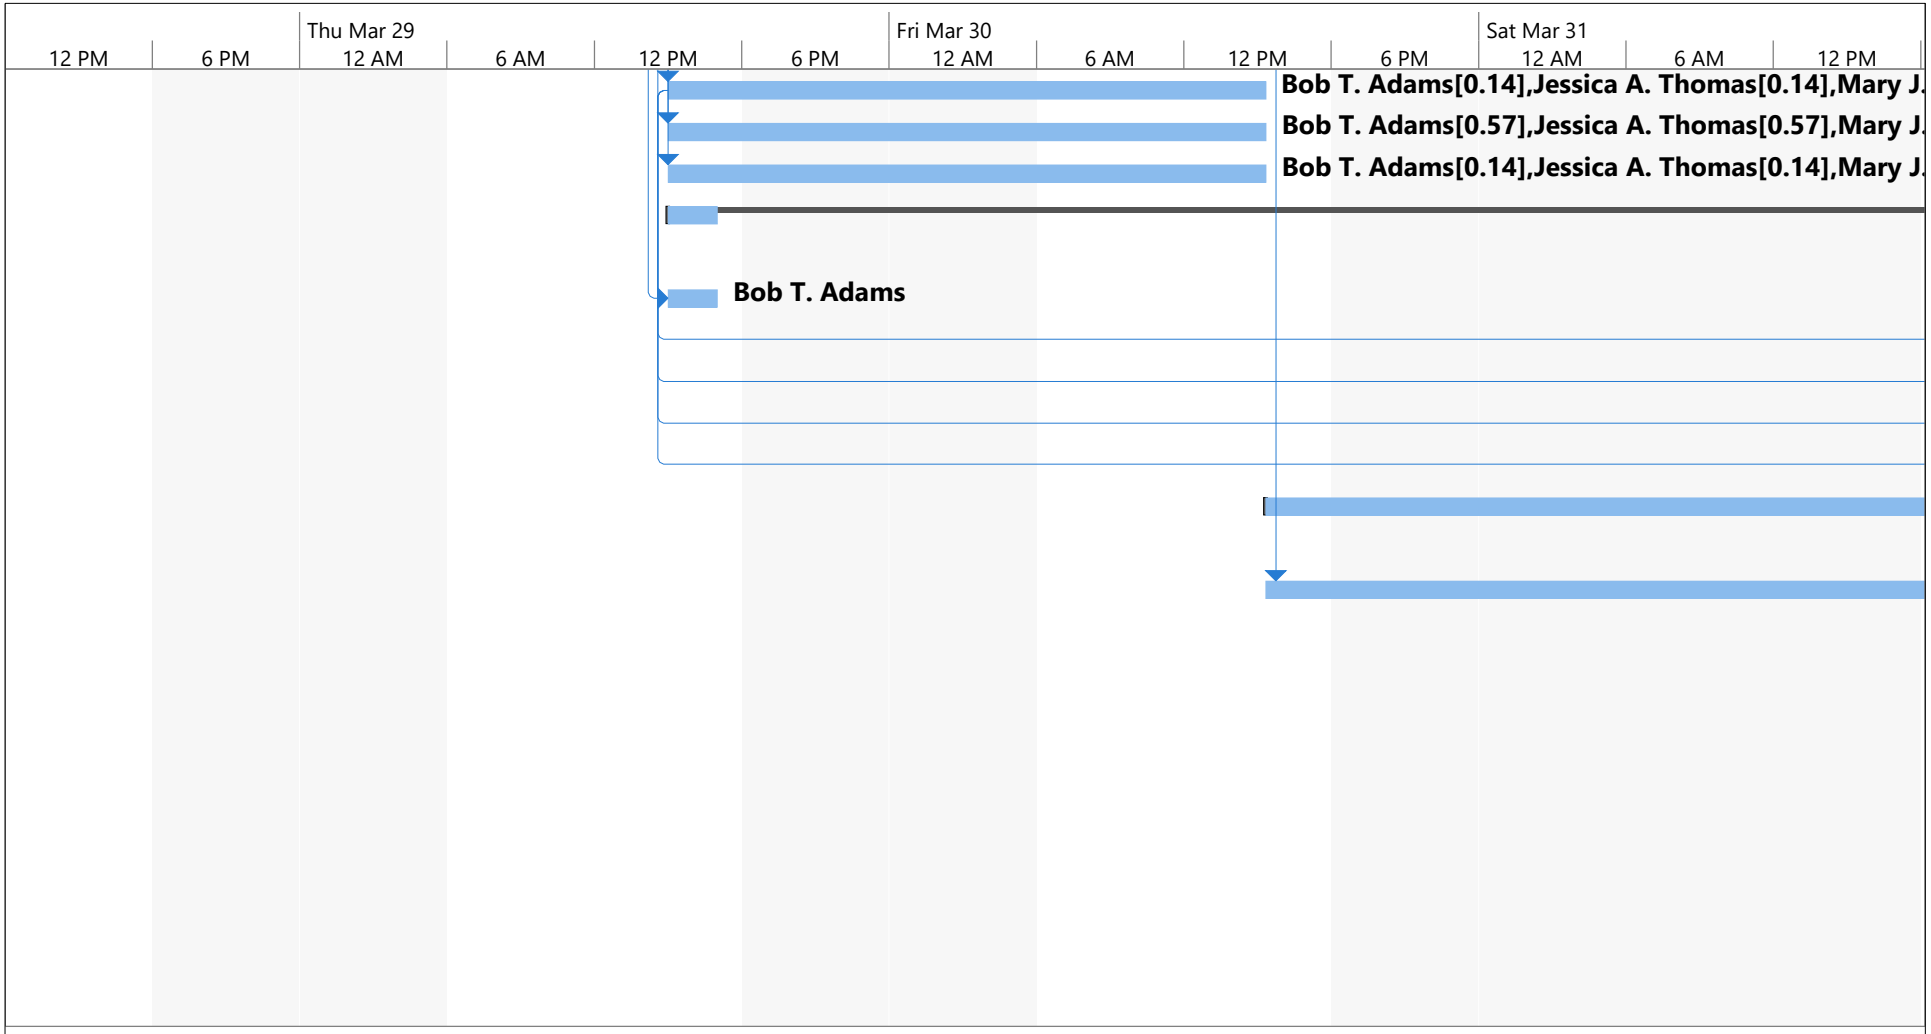

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

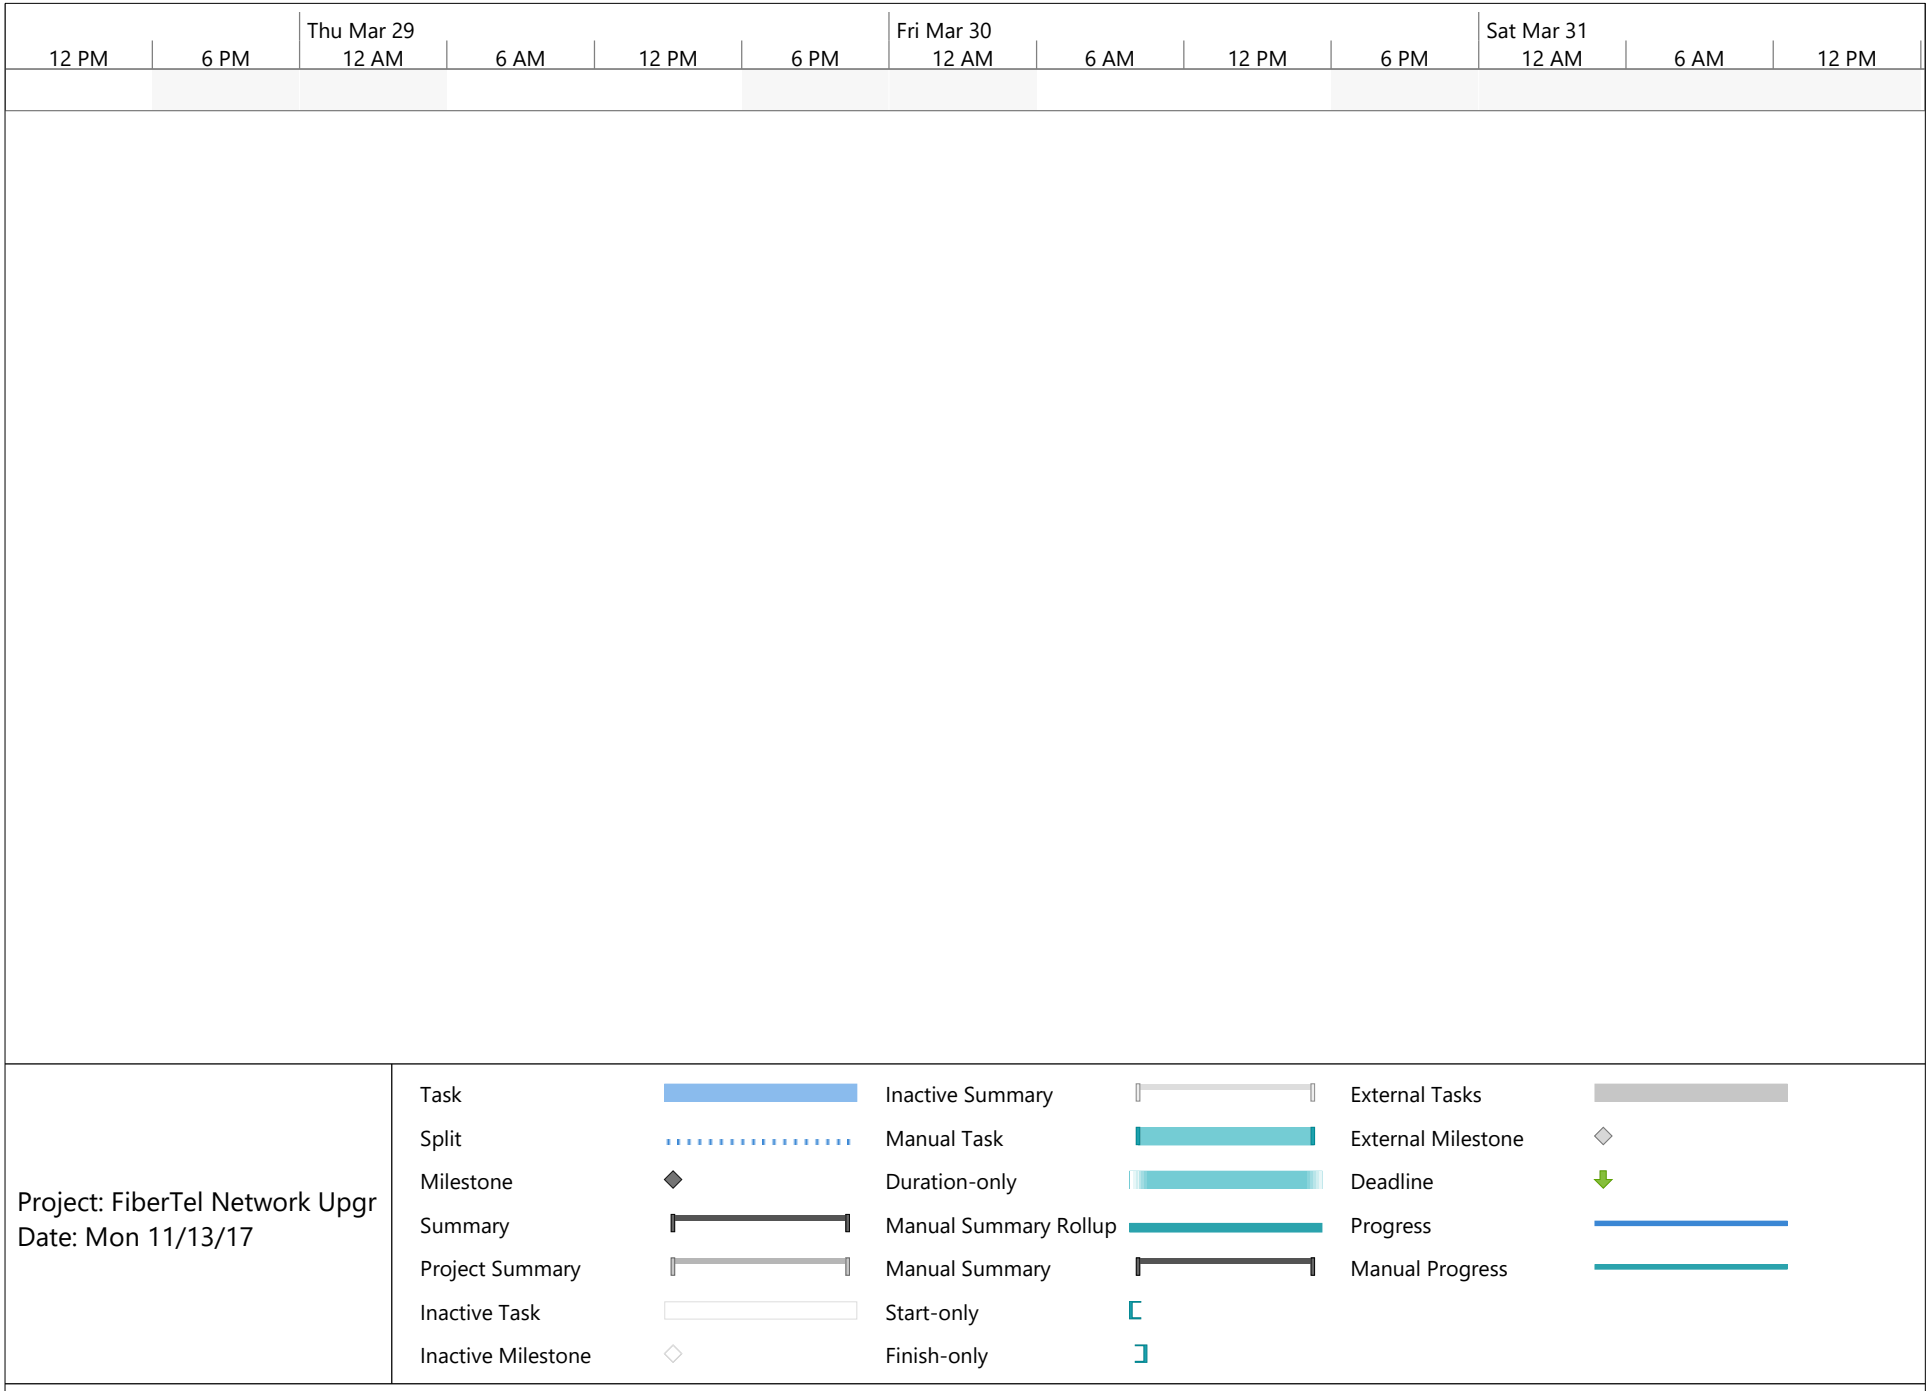
12 PM
6 PM
Thu Mar 29
12 AM
6 AM
12 PM
6 PM
Fri Mar 30
12 AM
6 AM
12 PM
6 PM
Sat Mar 31
12 AM
6 AM
12 PM
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

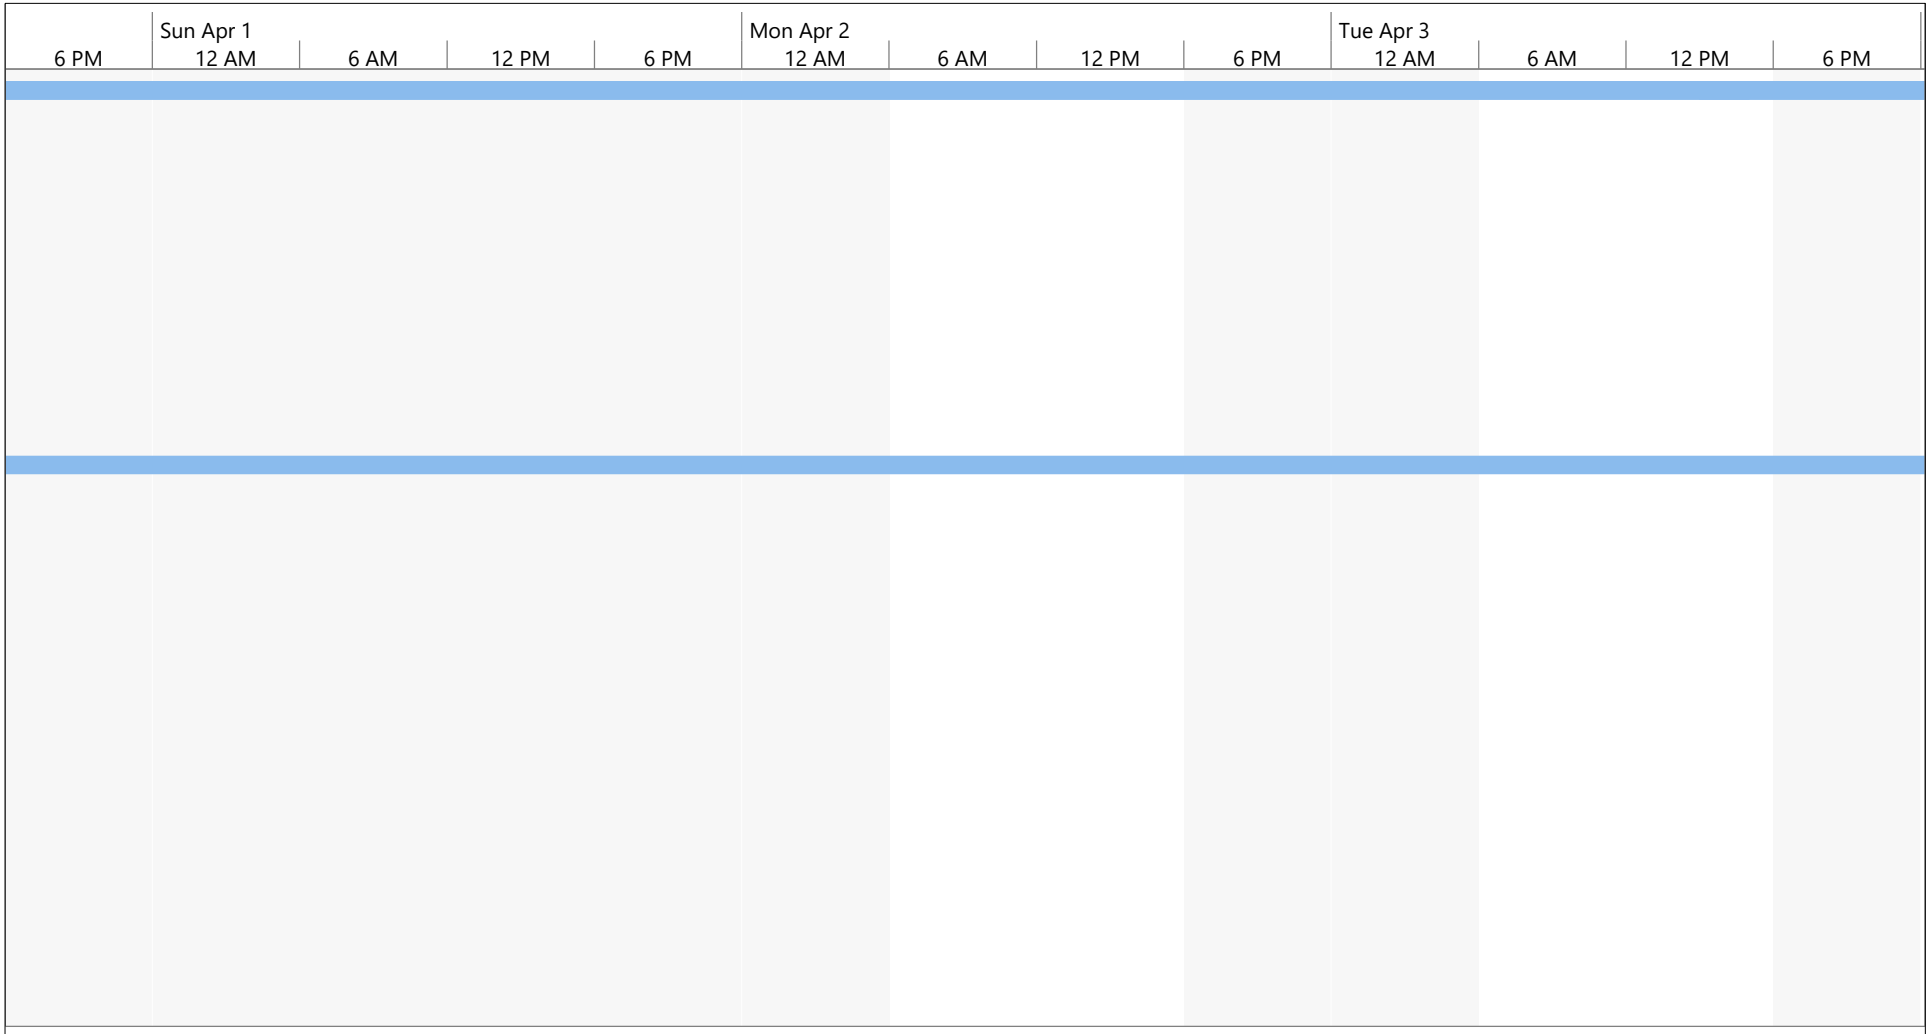

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

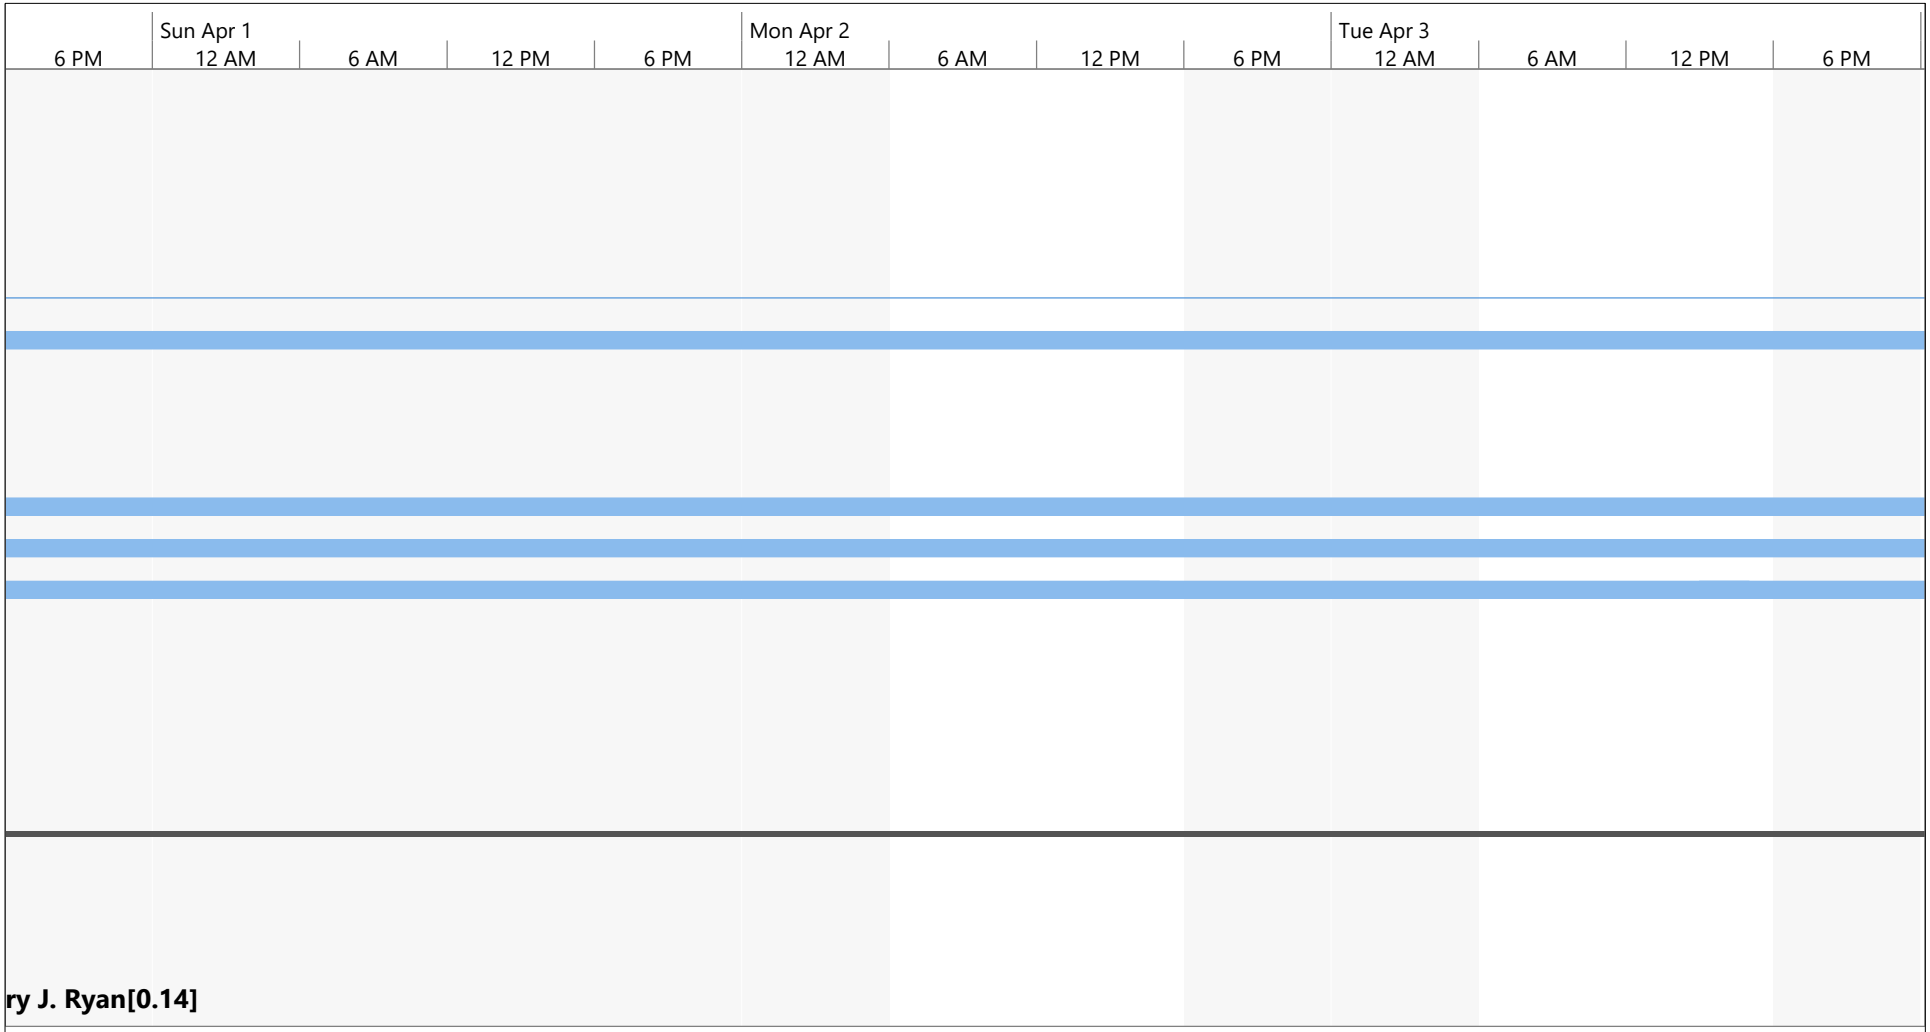

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

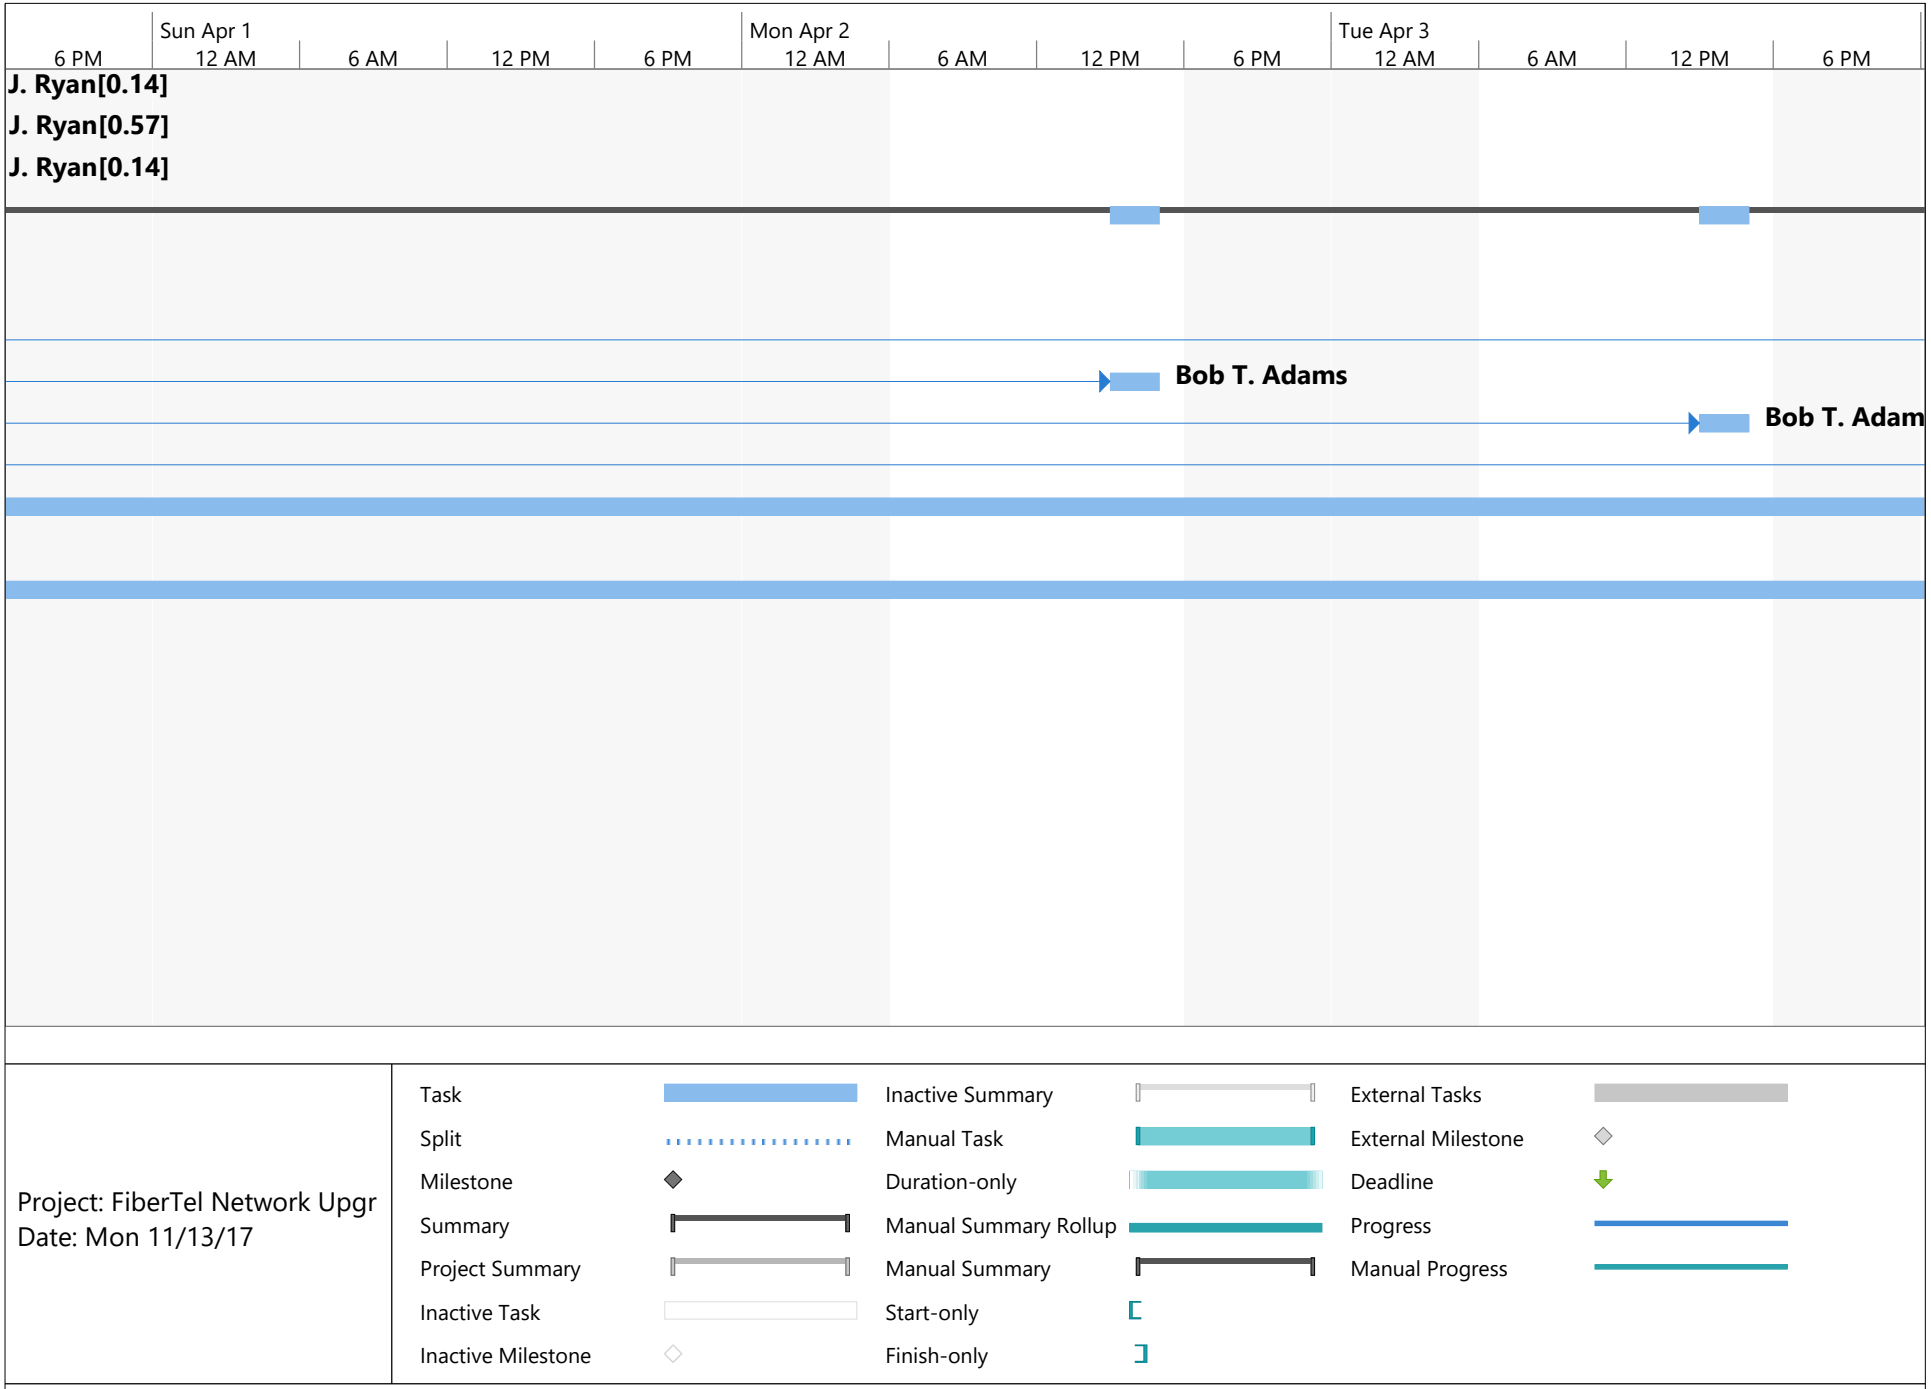

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

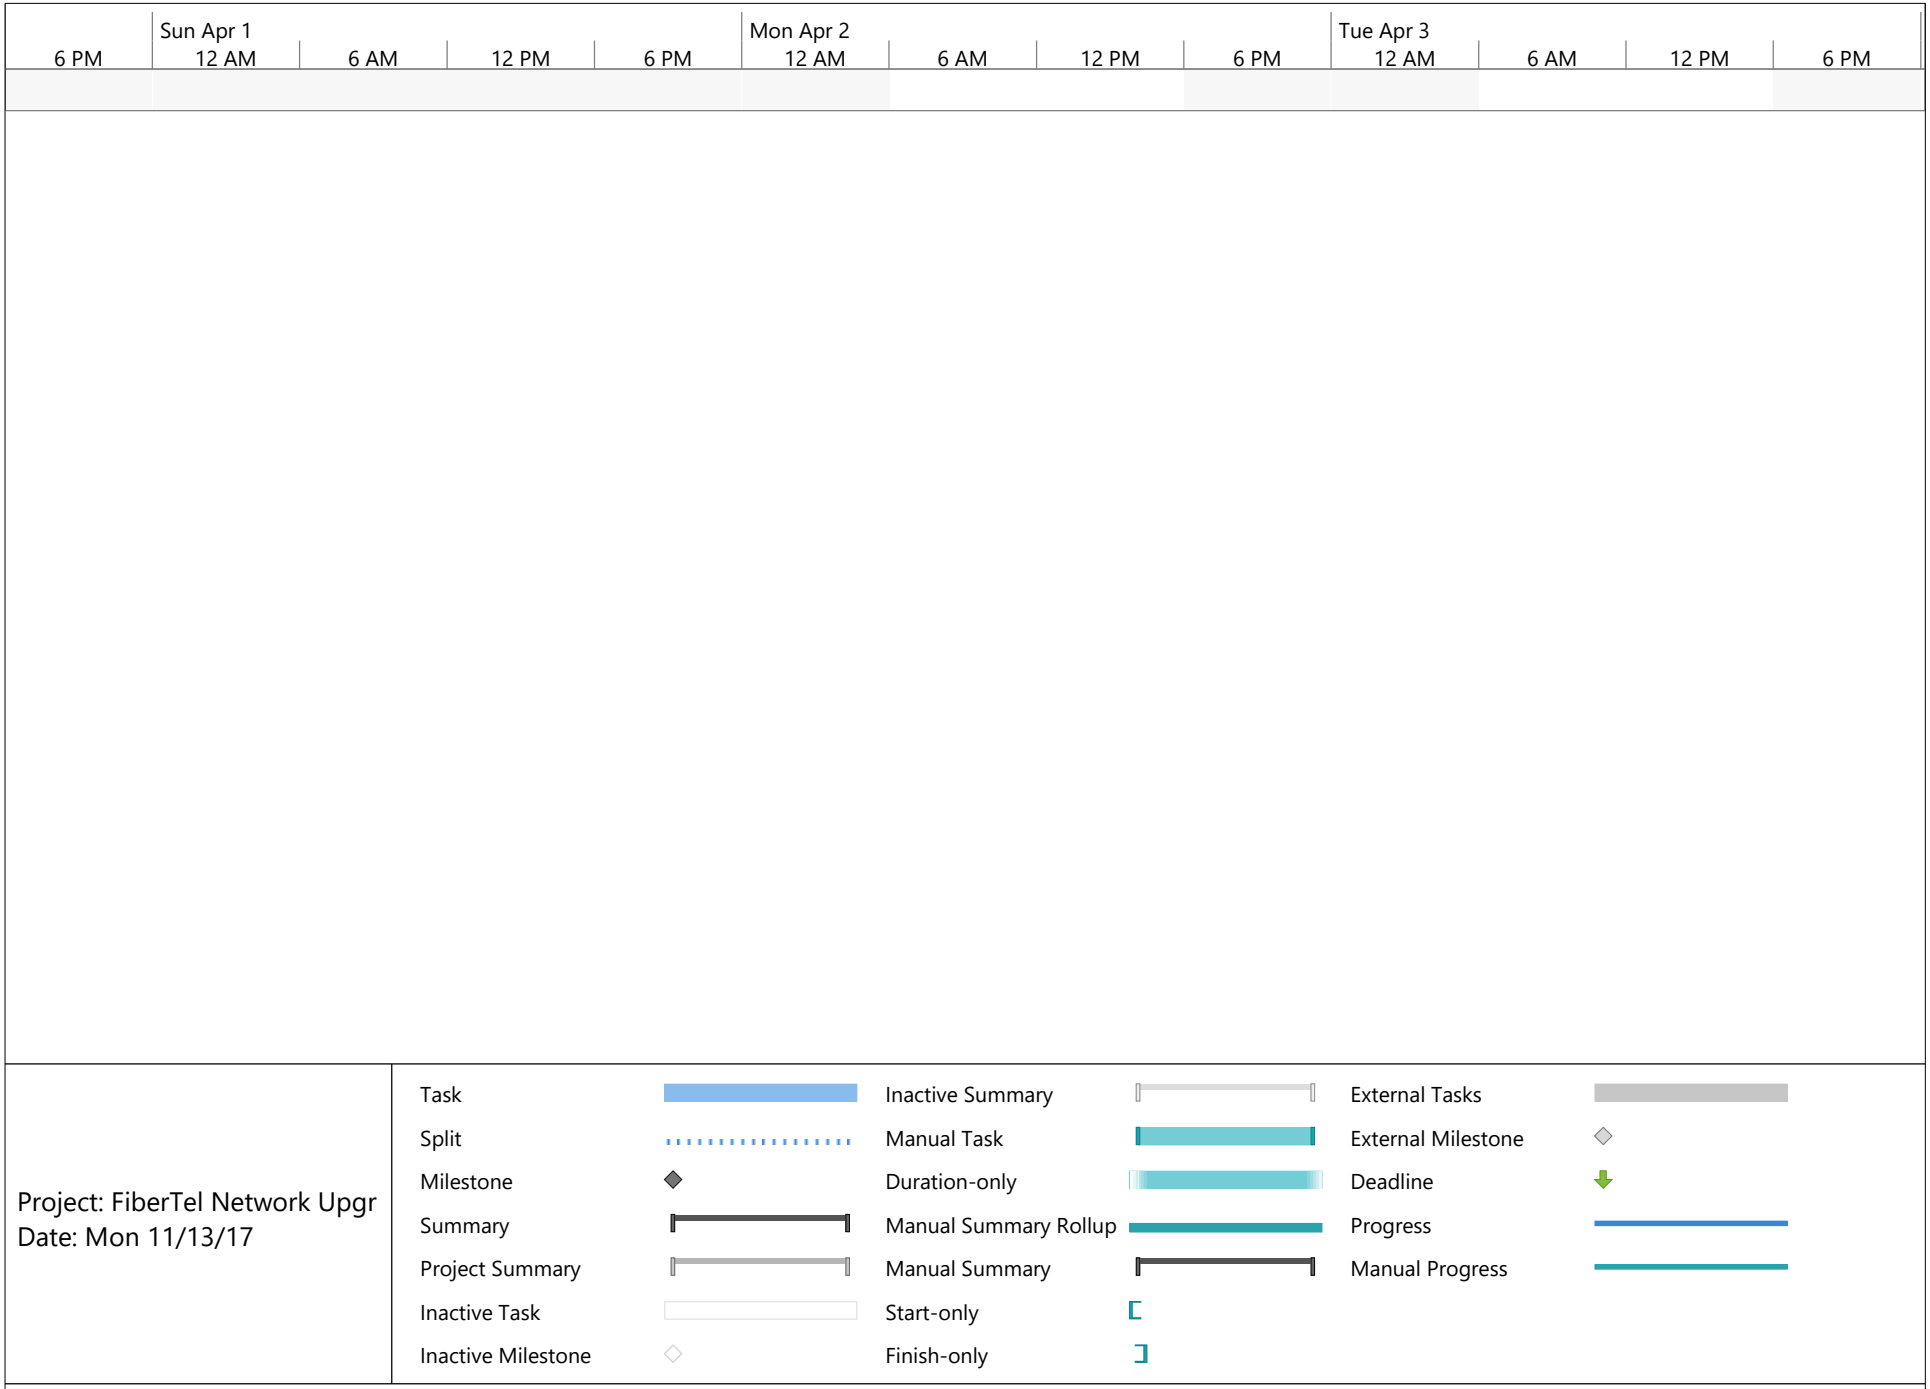

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

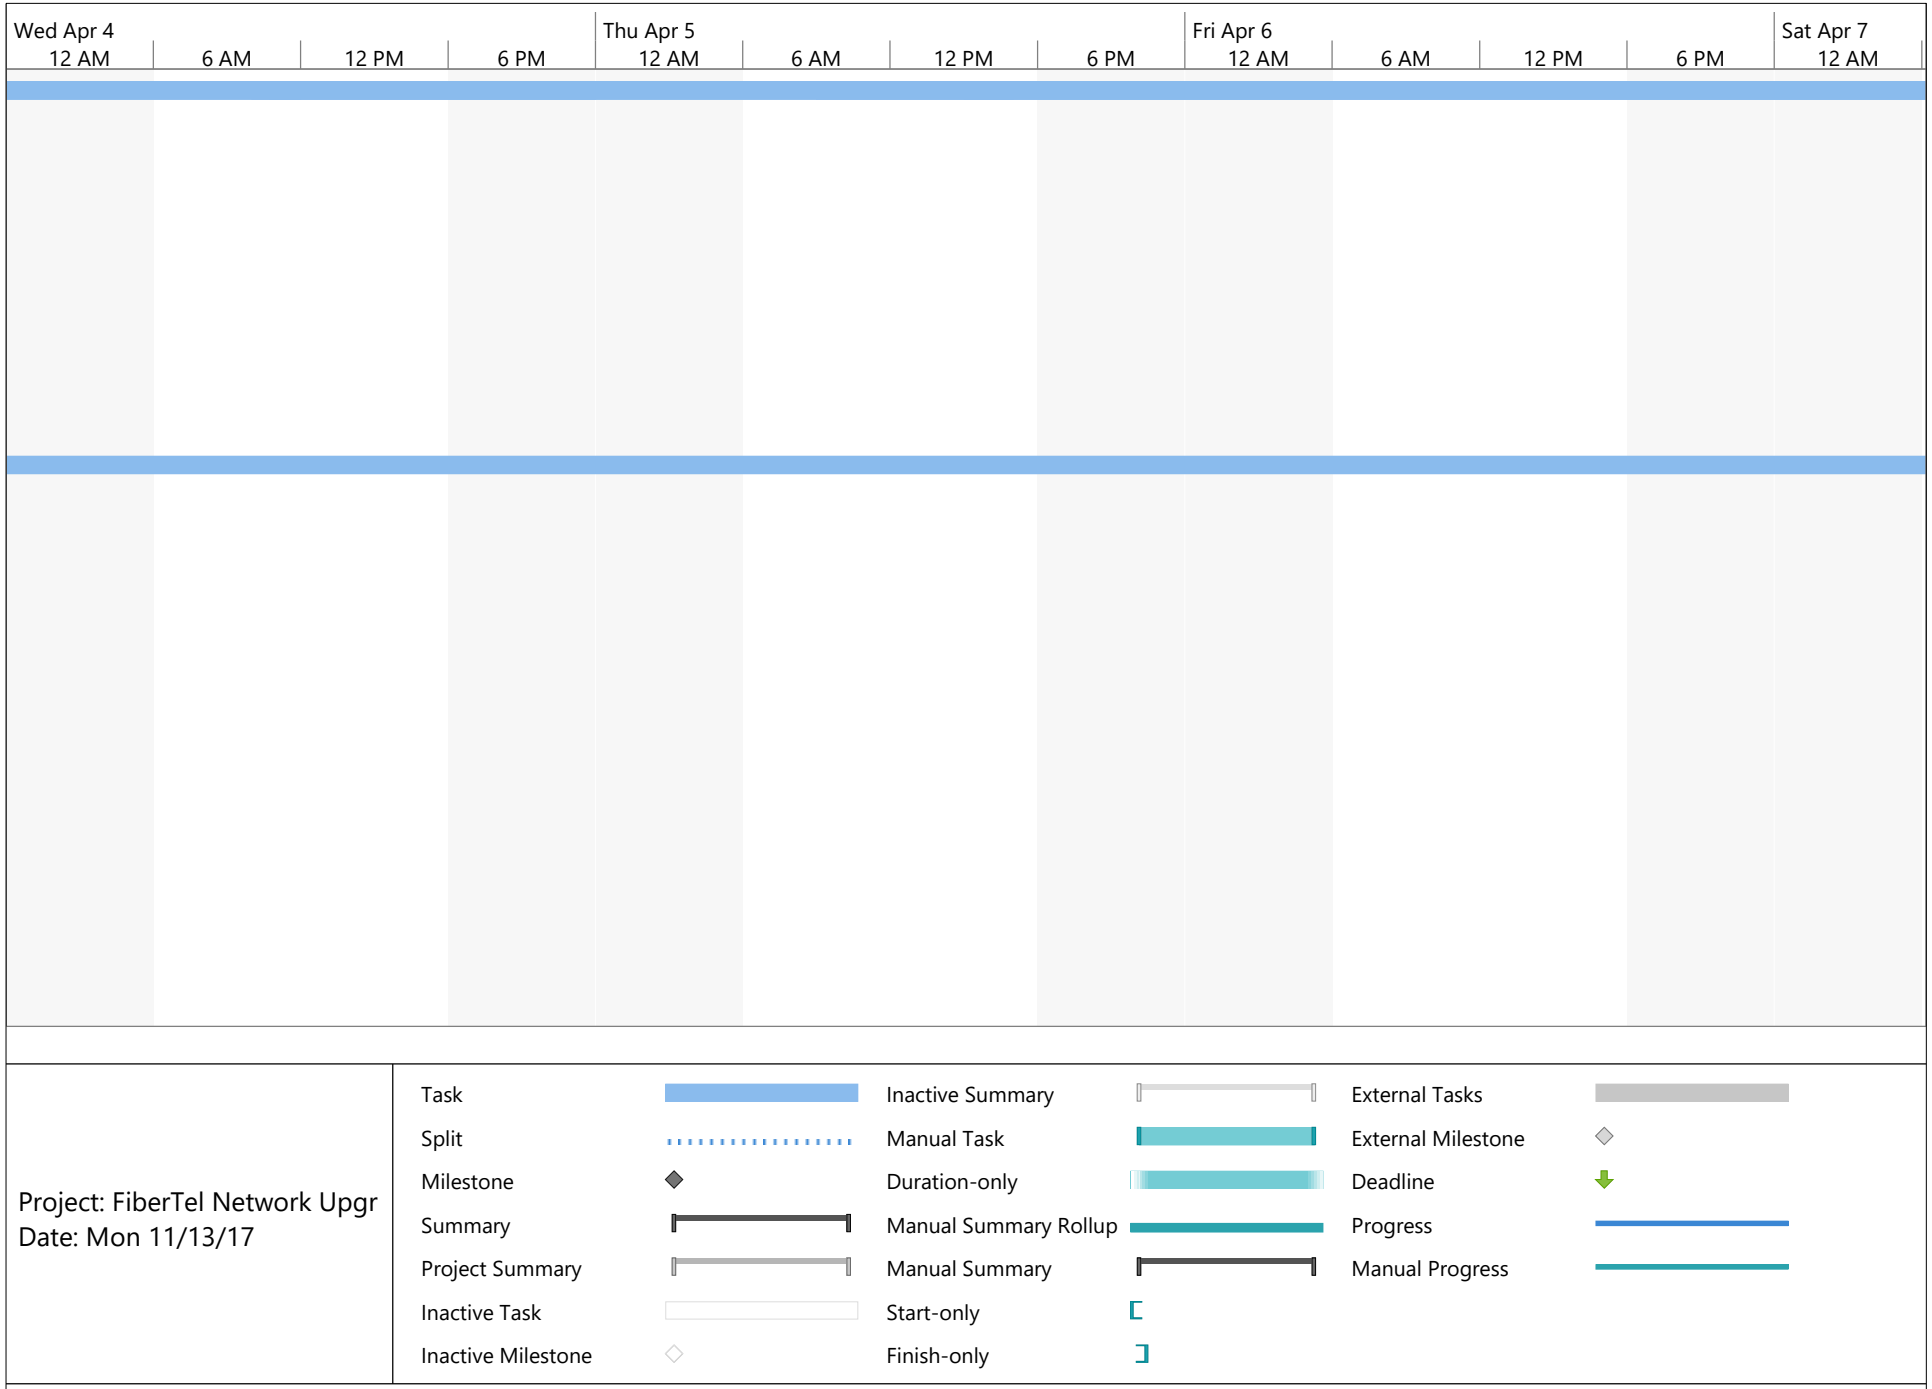

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

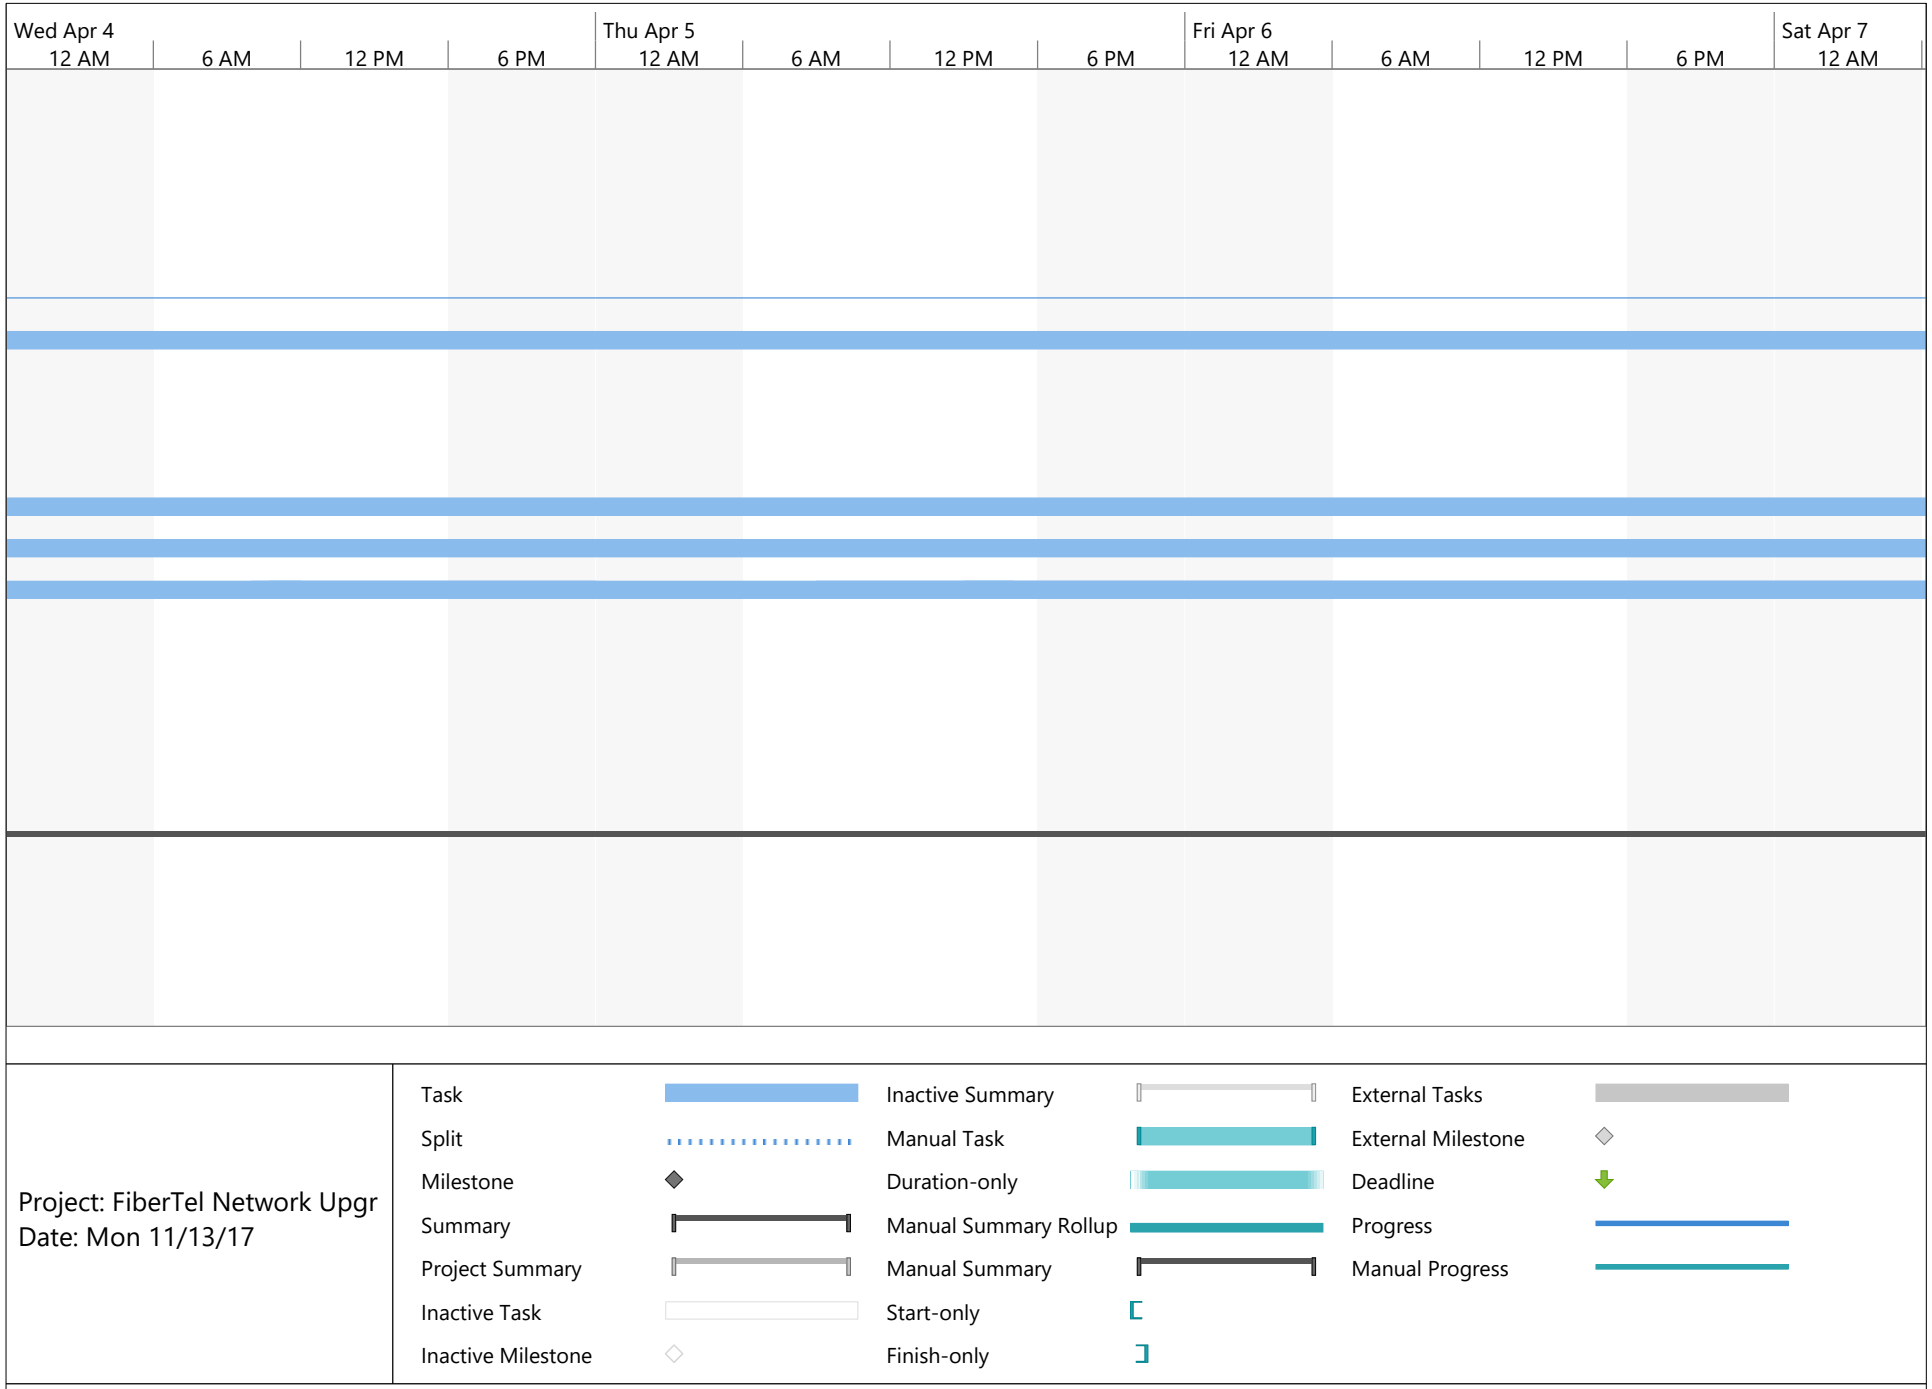

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

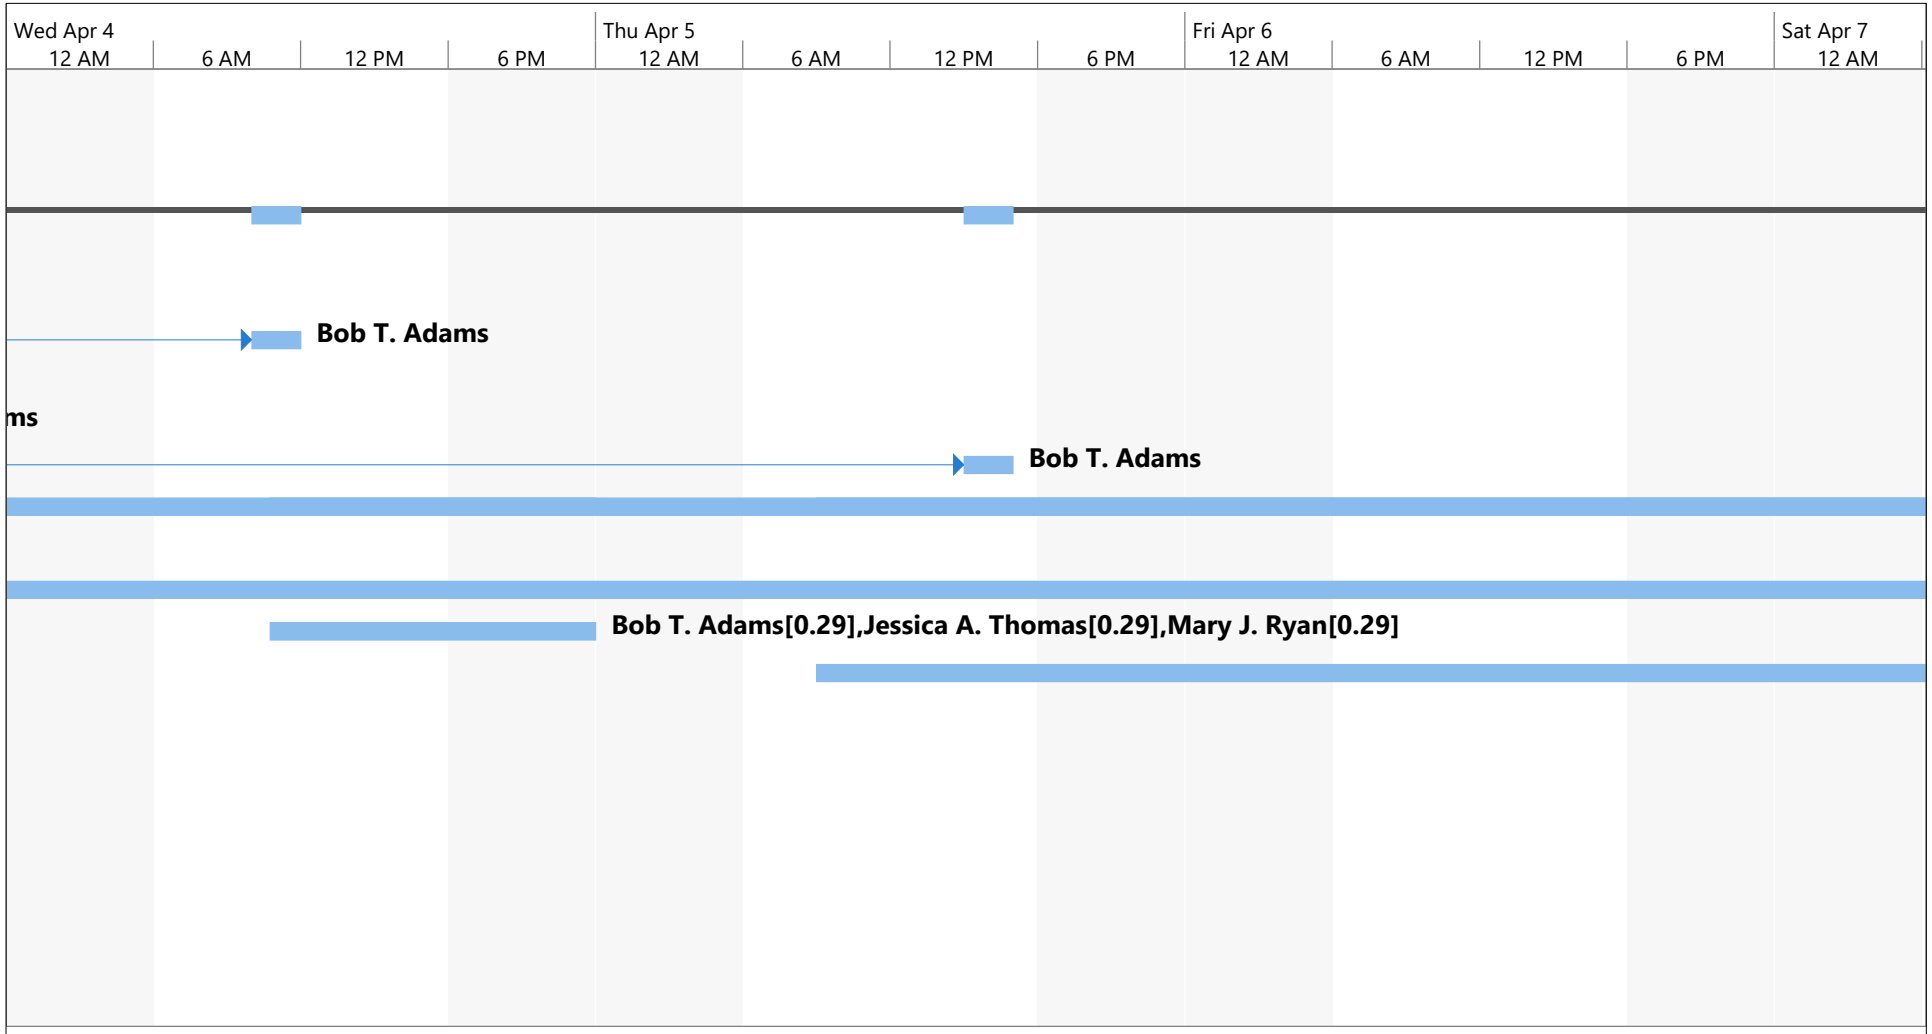

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

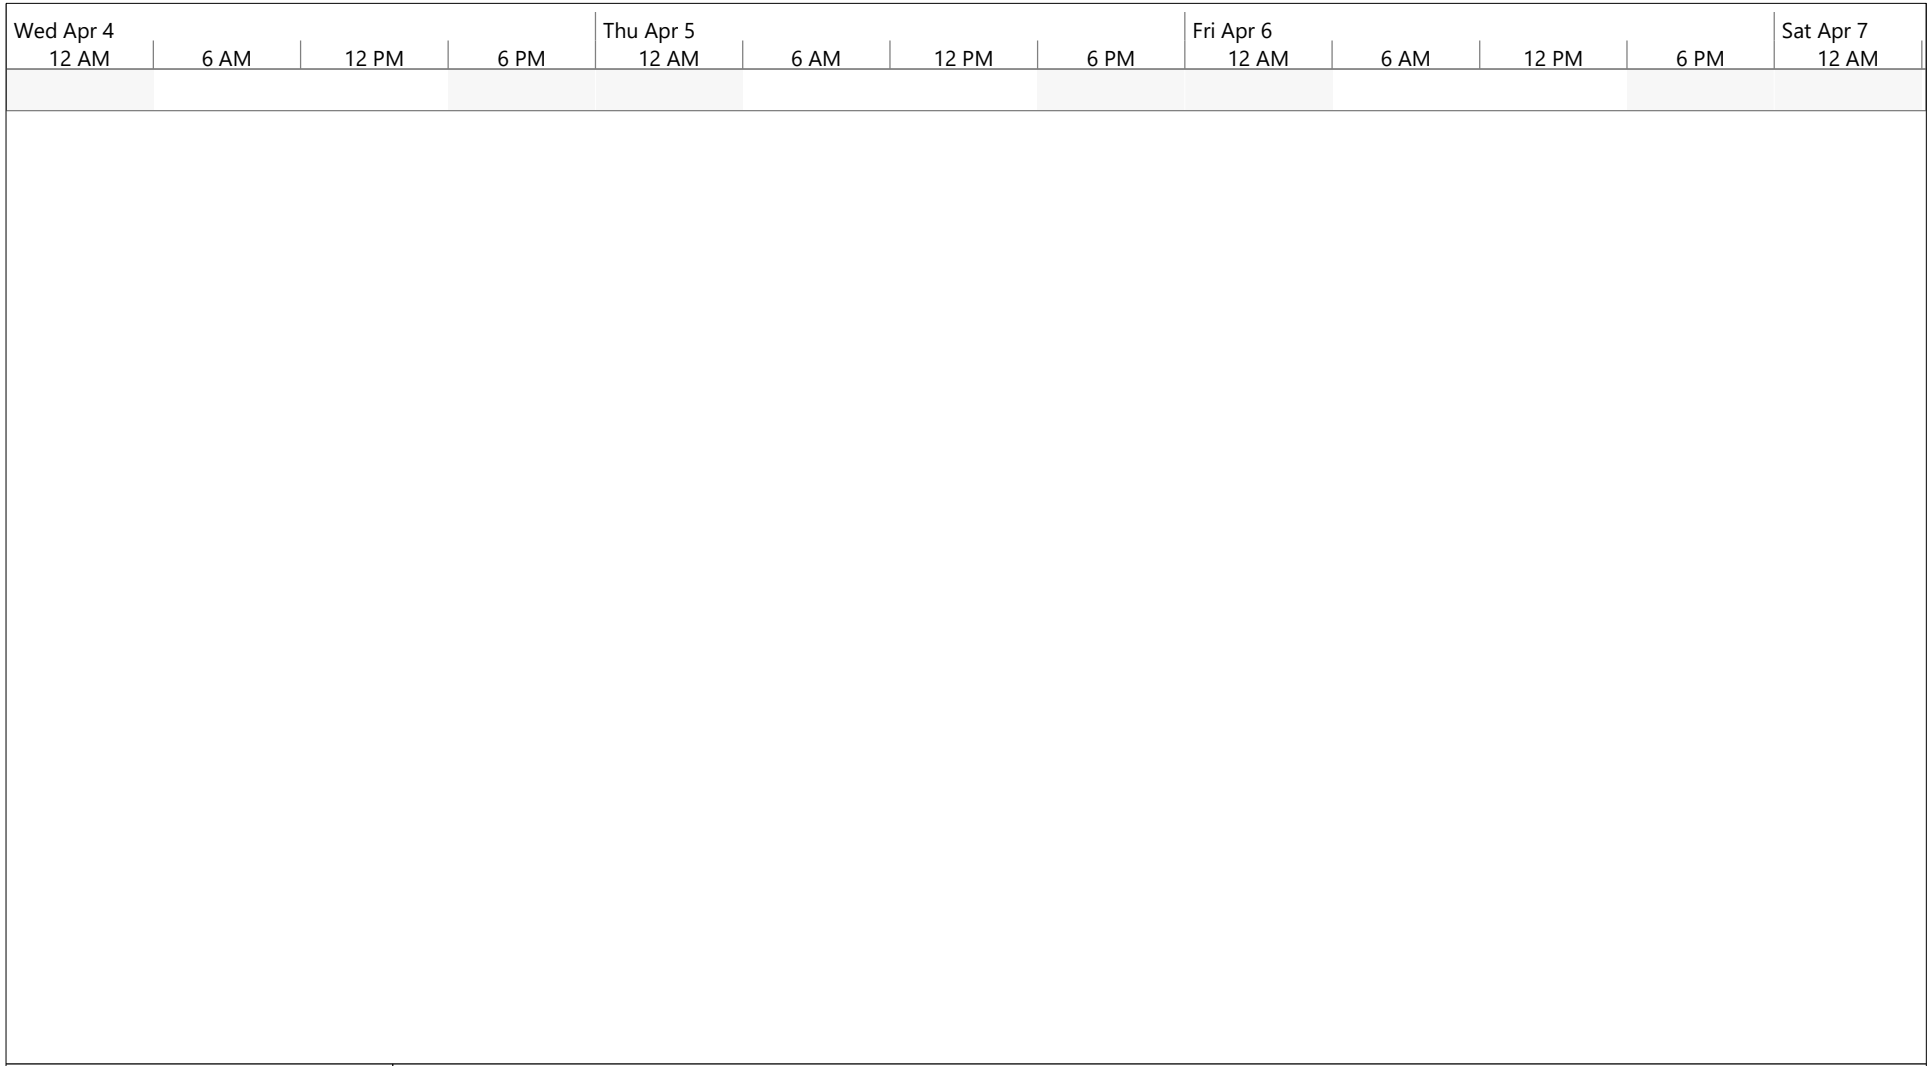

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

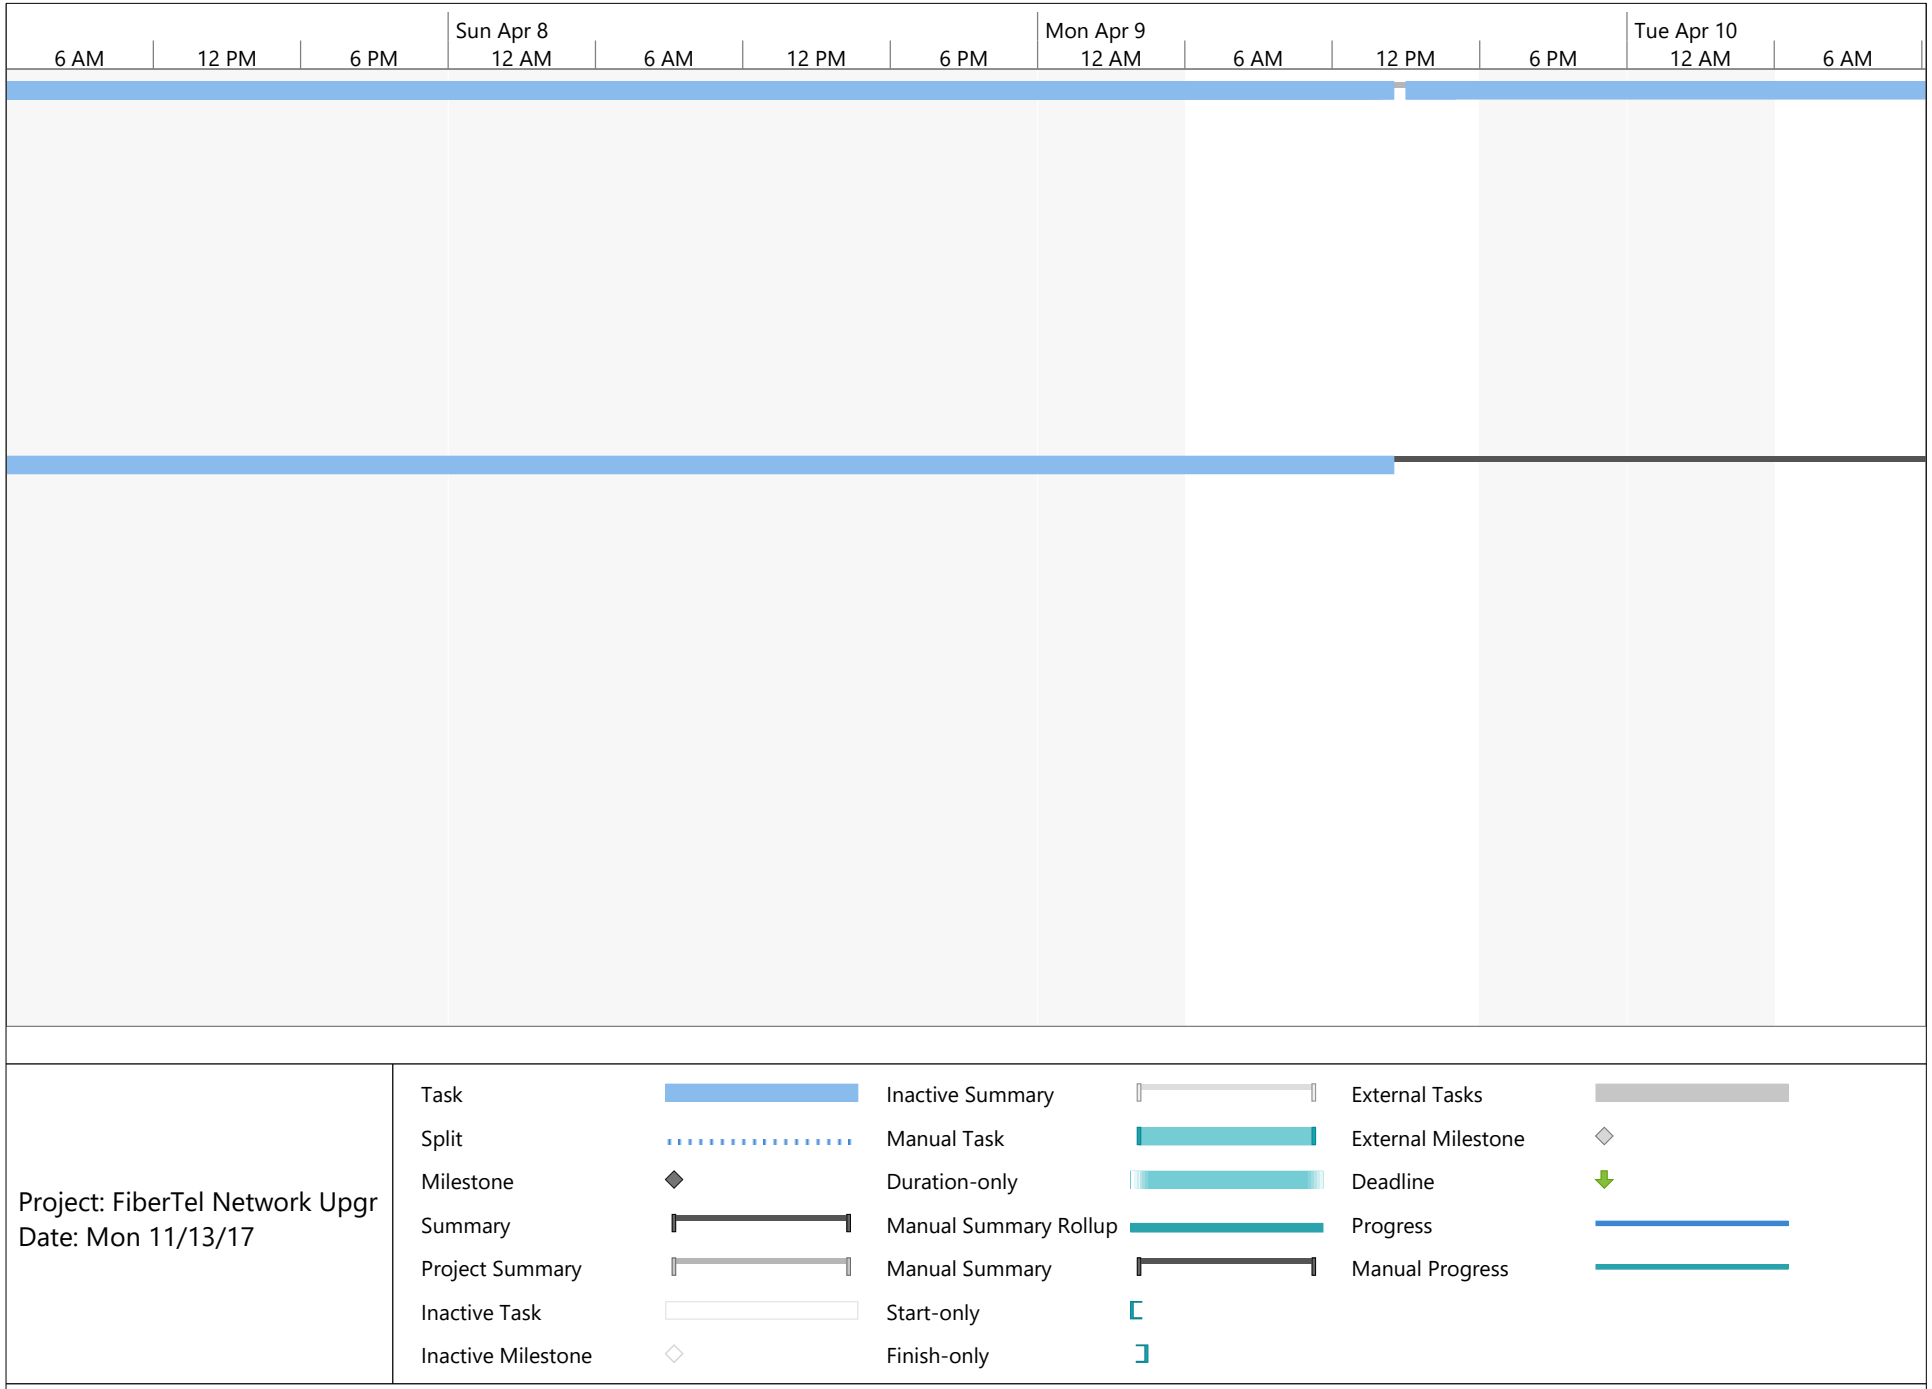

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

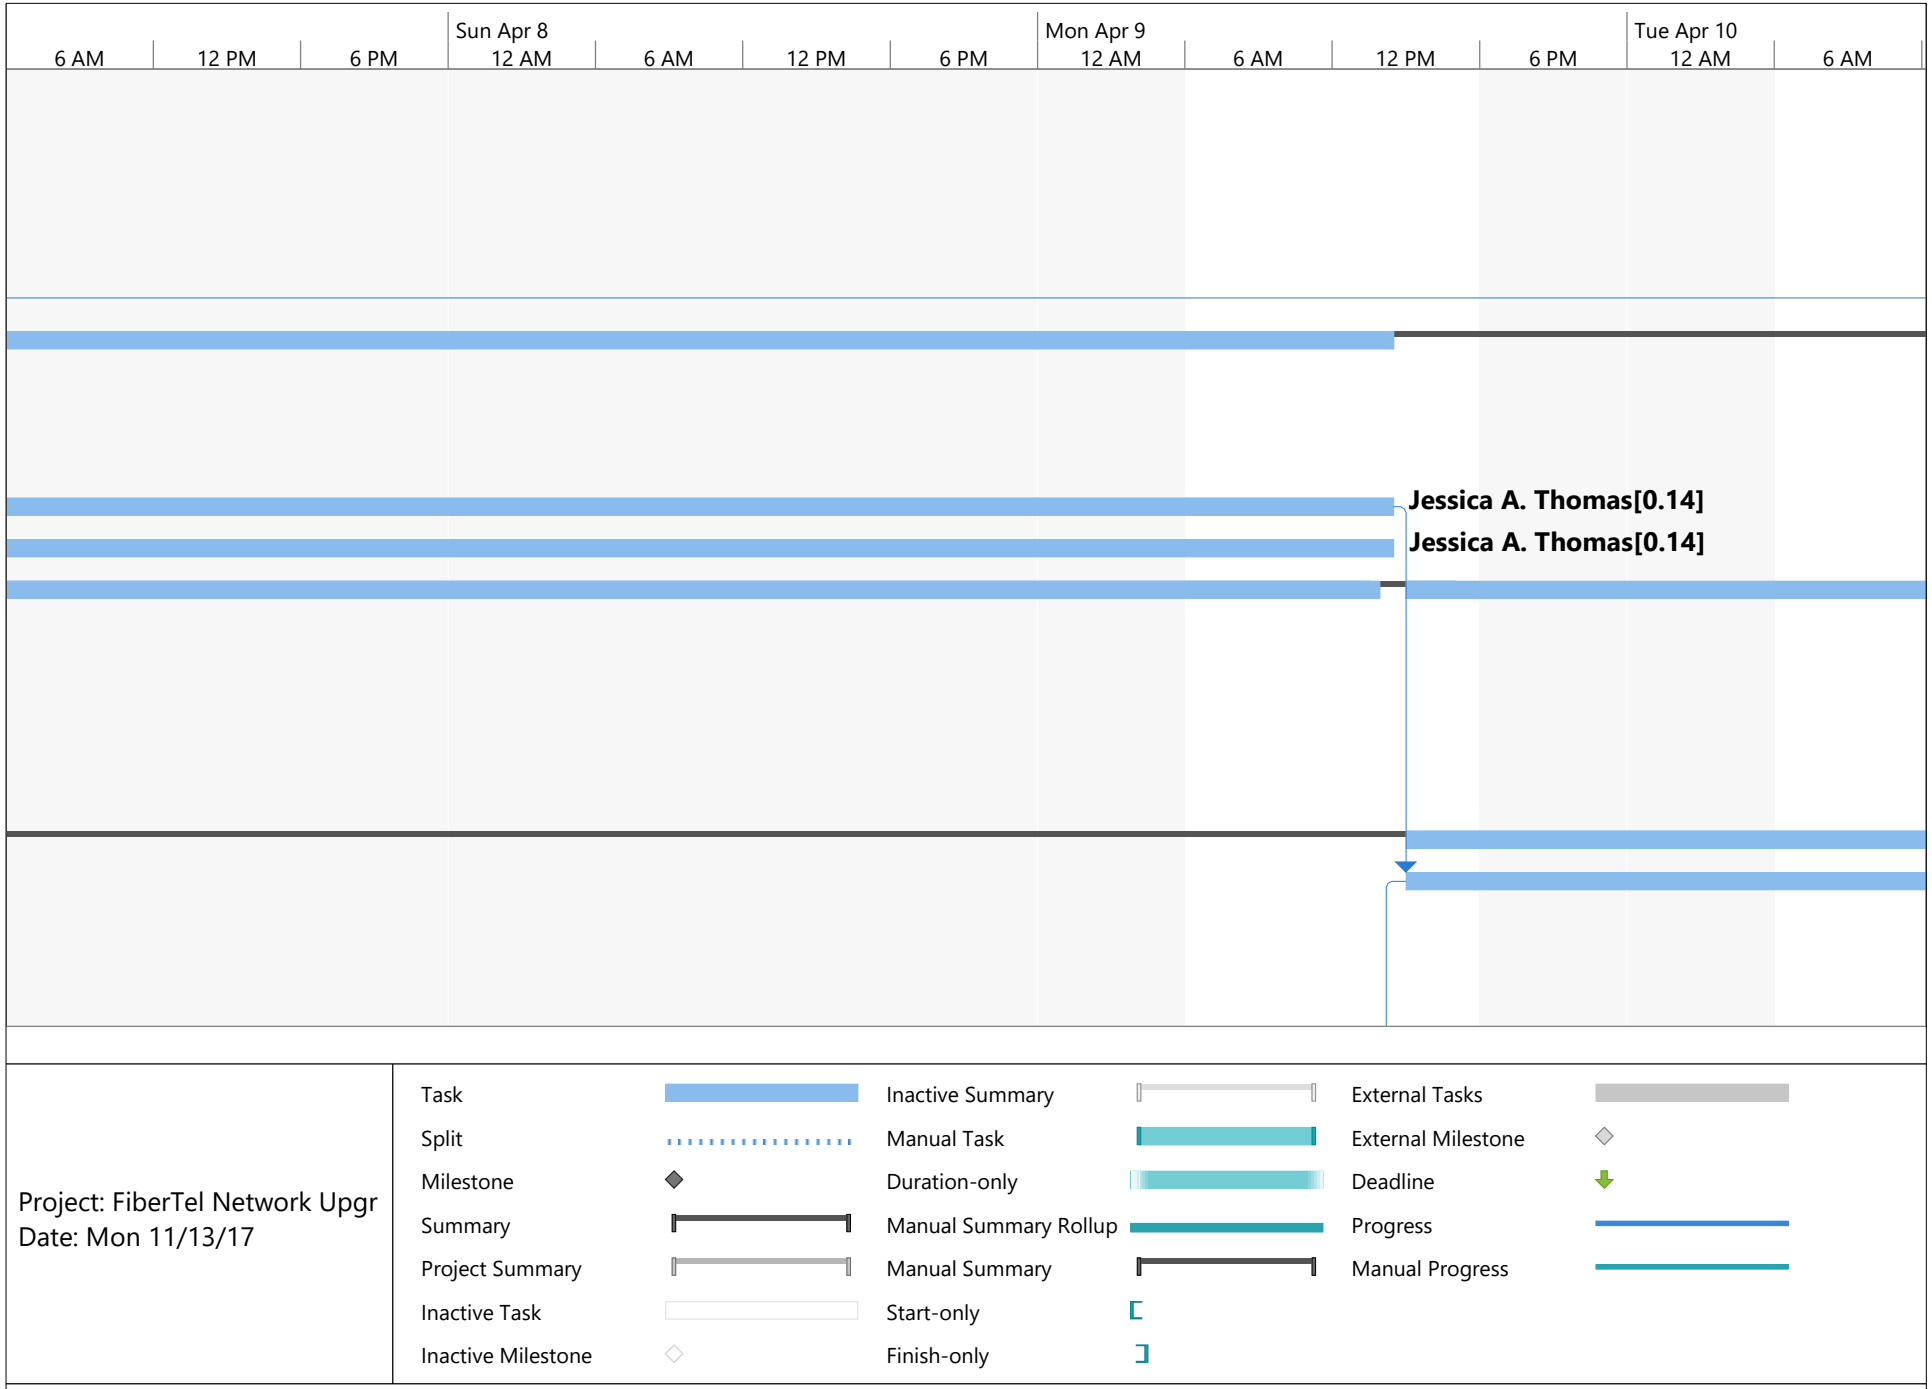

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

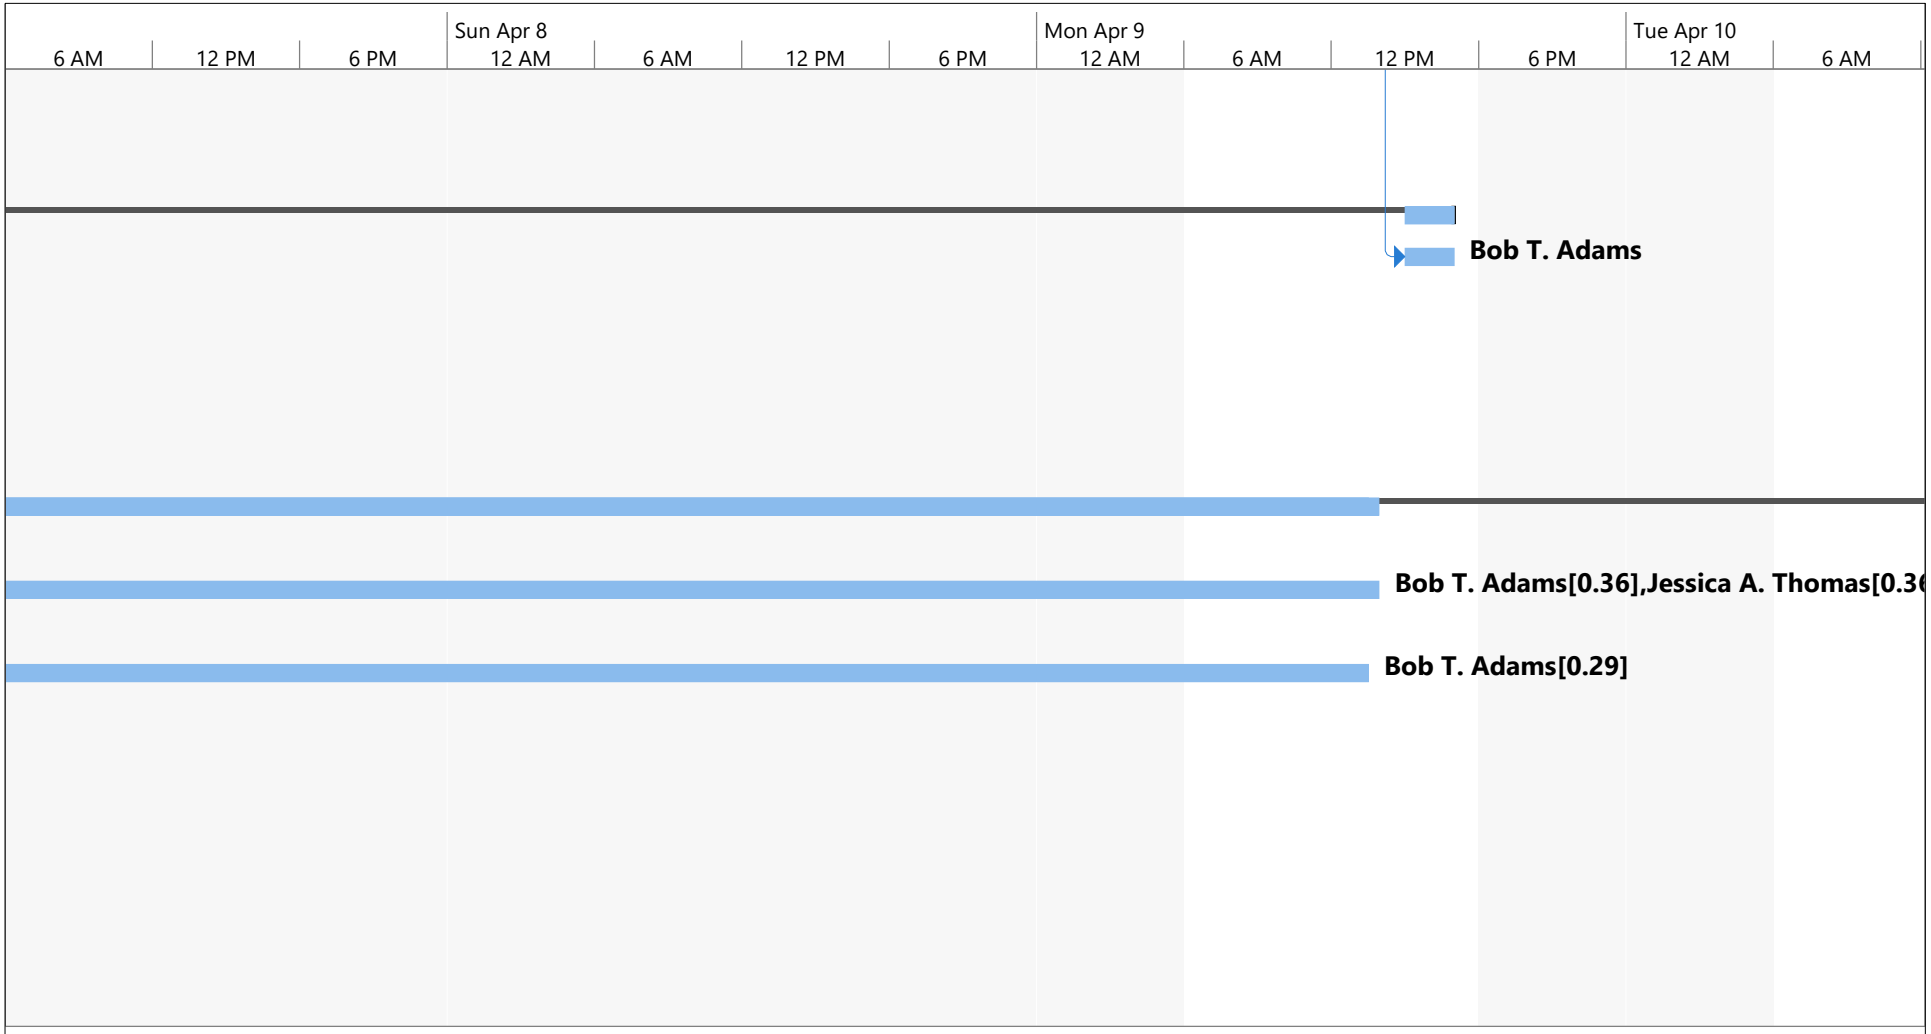

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

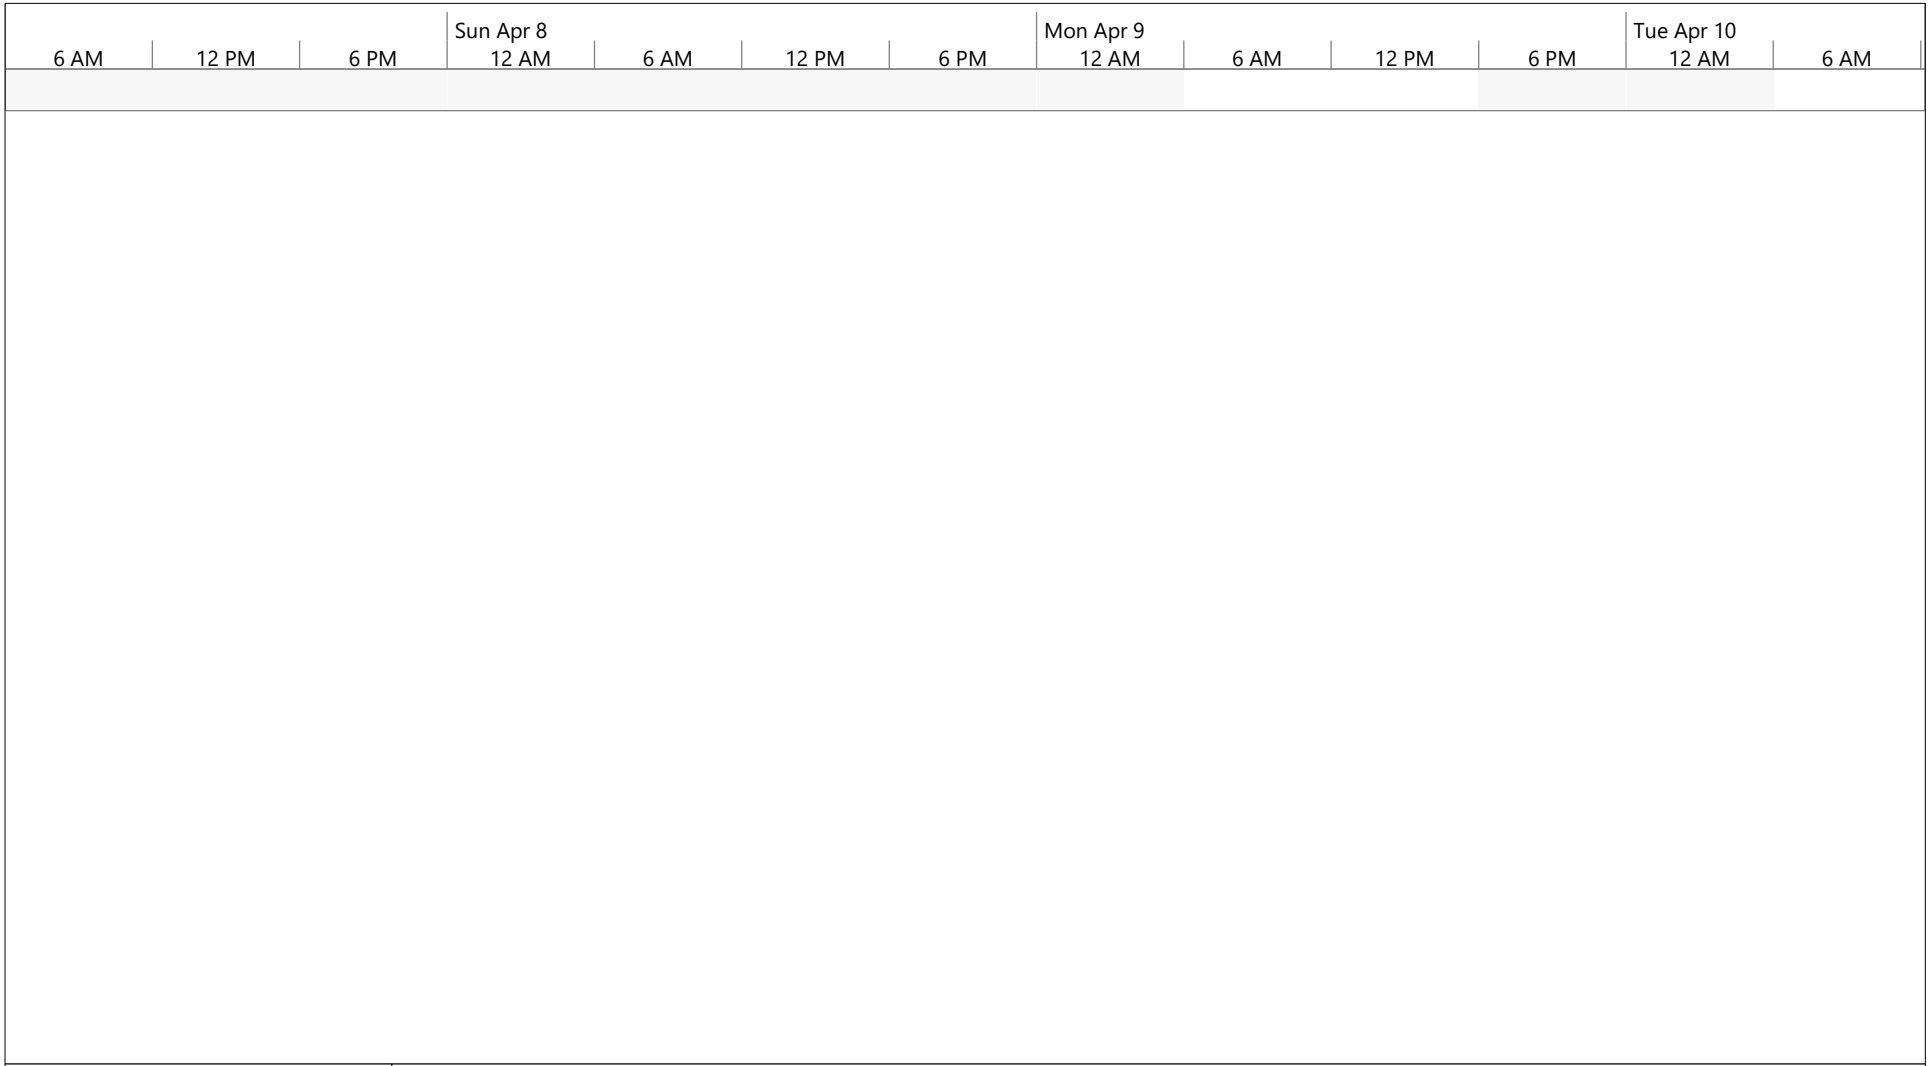

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

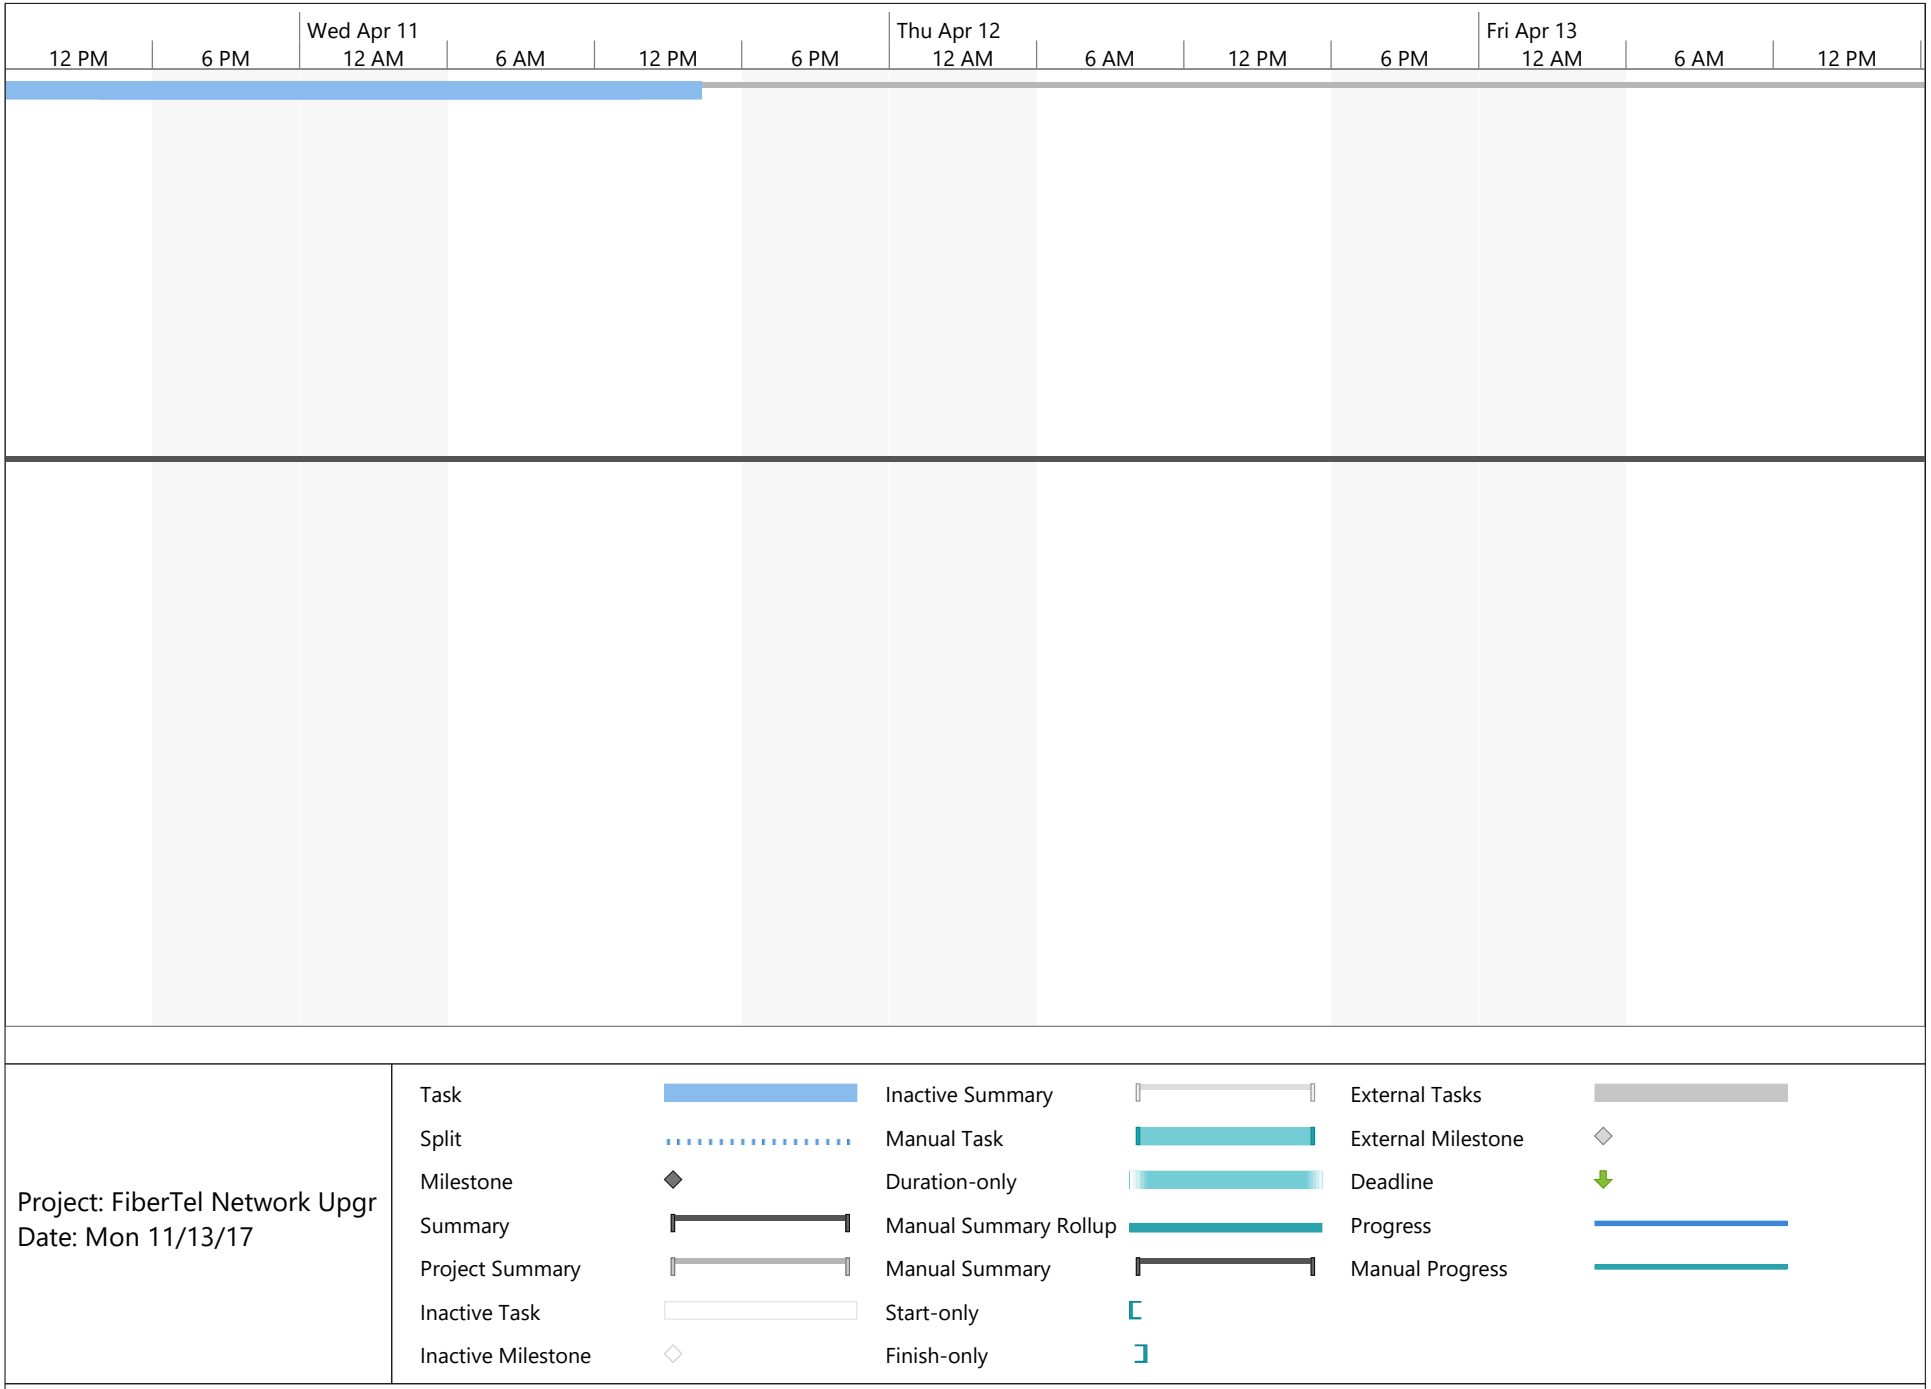

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

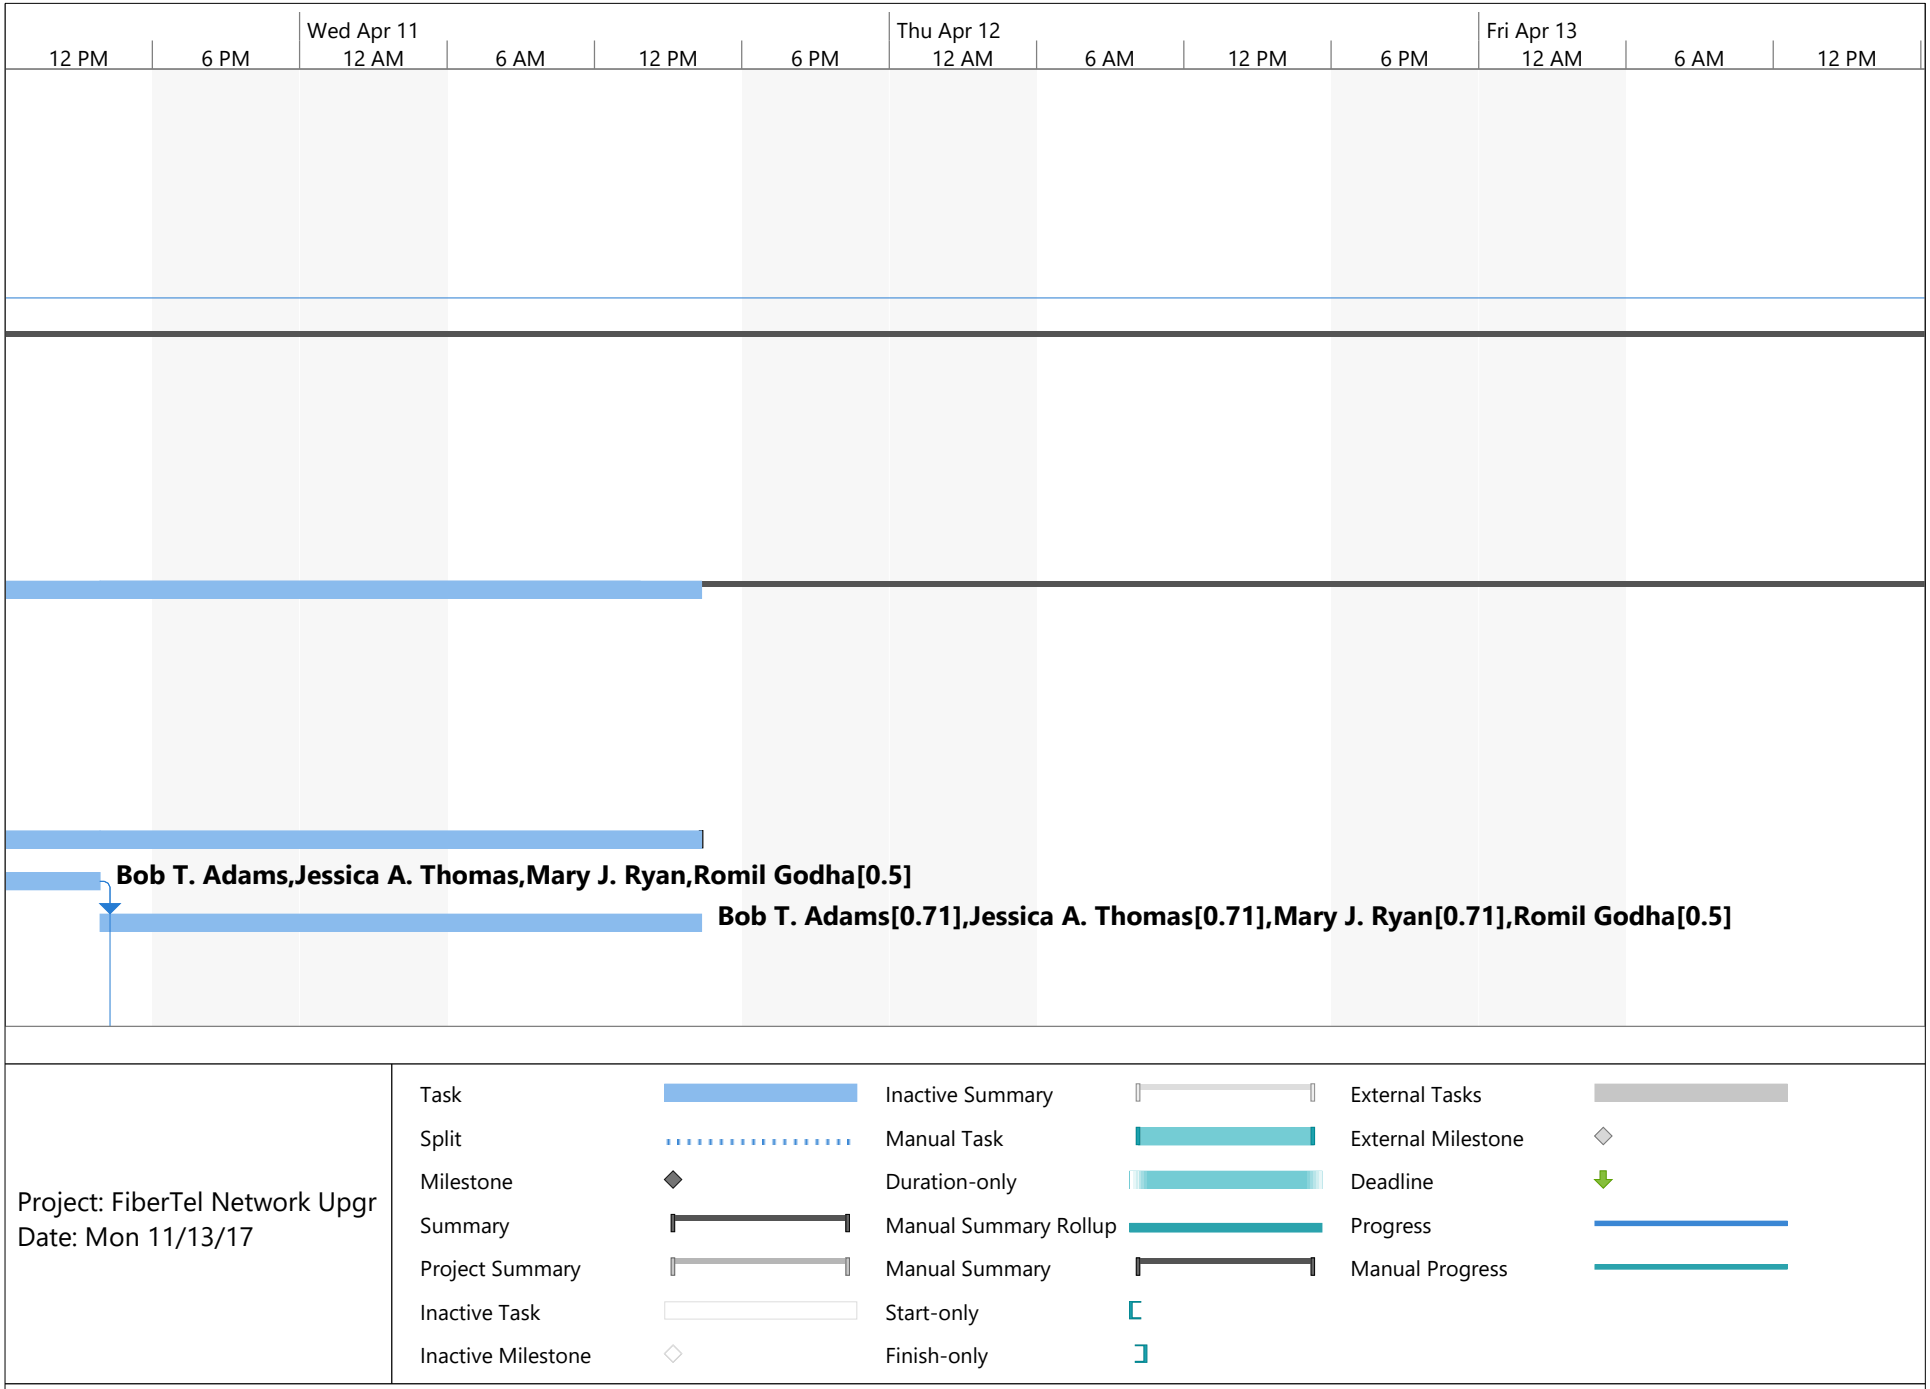

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

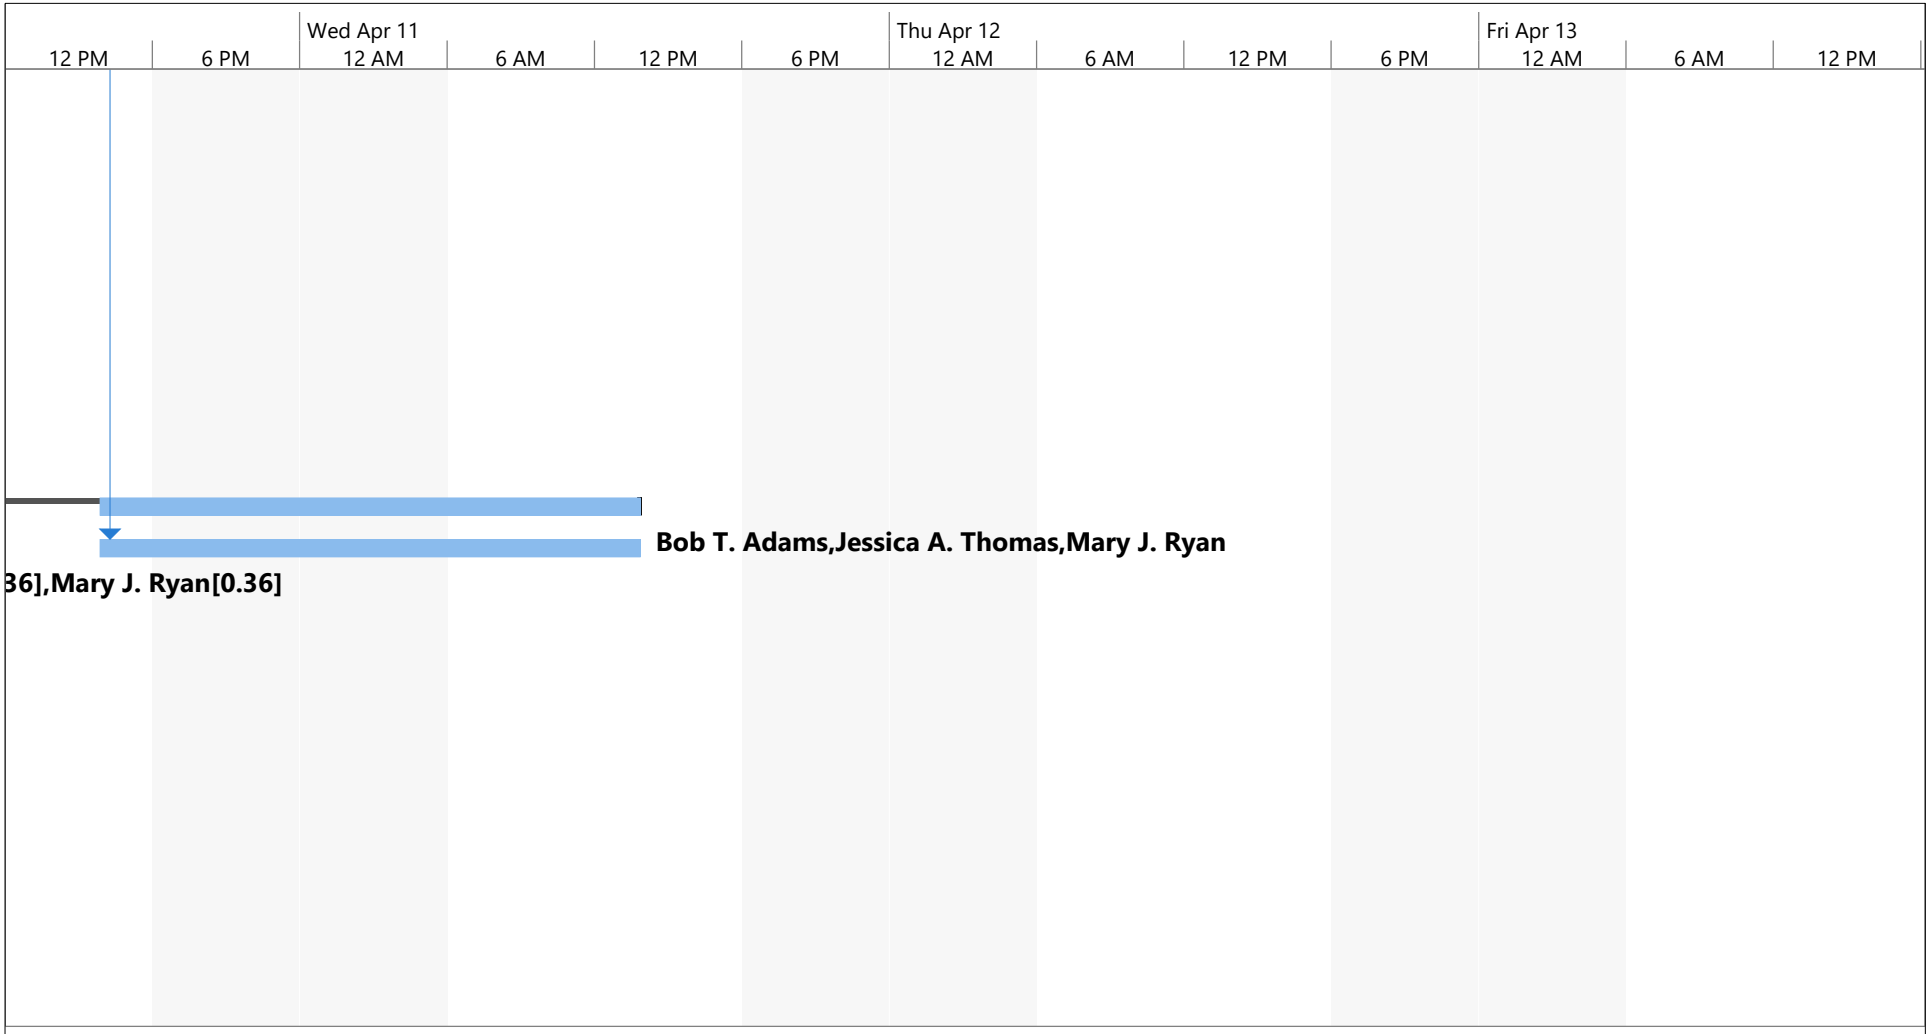

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

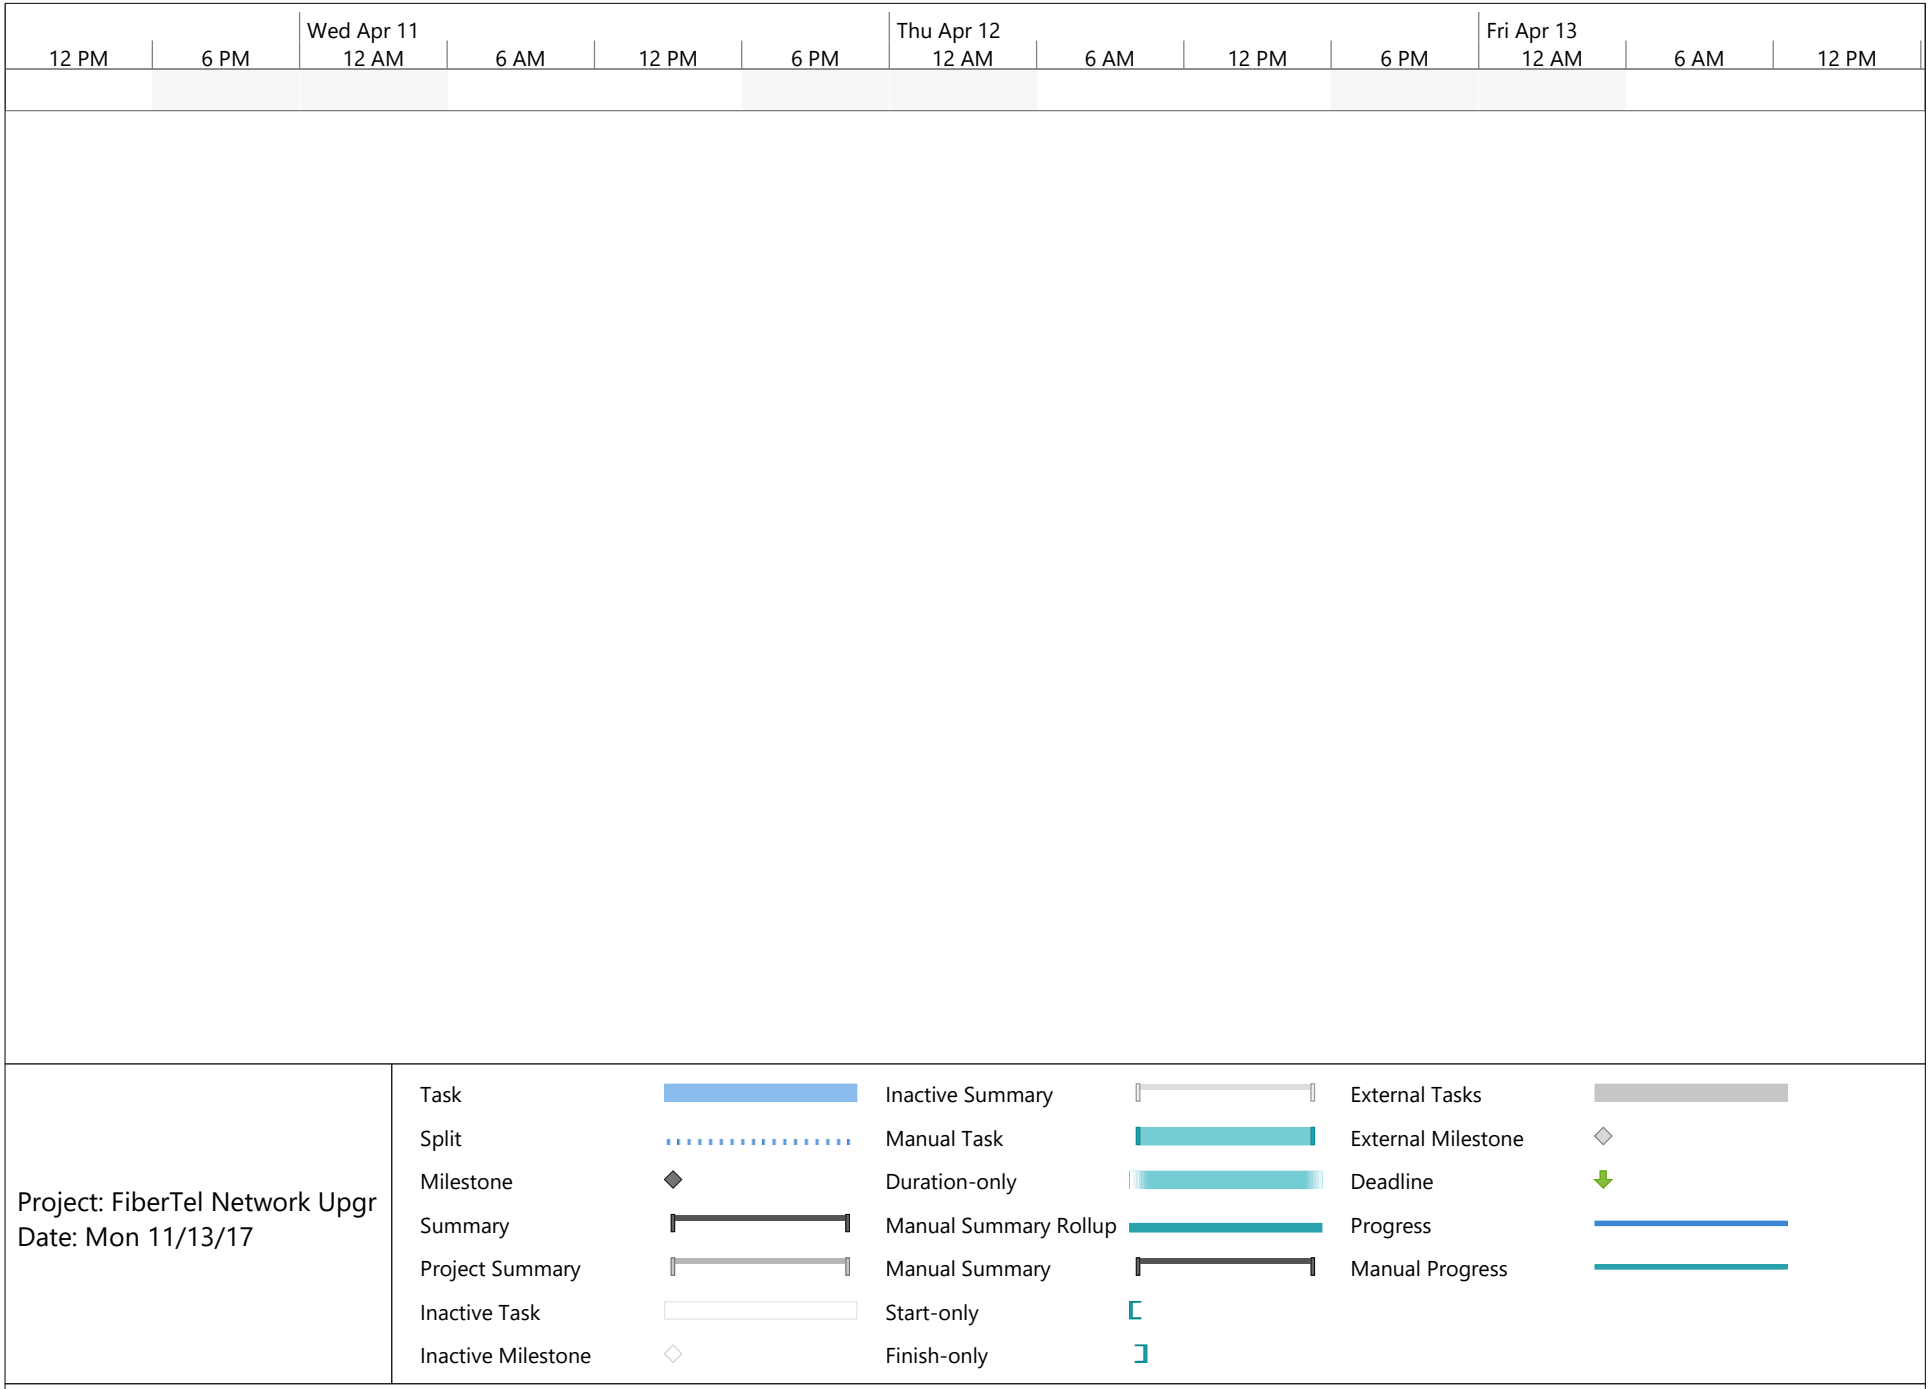
12 PM
6 PM
Wed Apr 11
12 AM
6 AM
12 PM
6 PM
Thu Apr 12
12 AM
6 AM
12 PM
6 PM
Fri Apr 13
12 AM
6 AM
12 PM
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

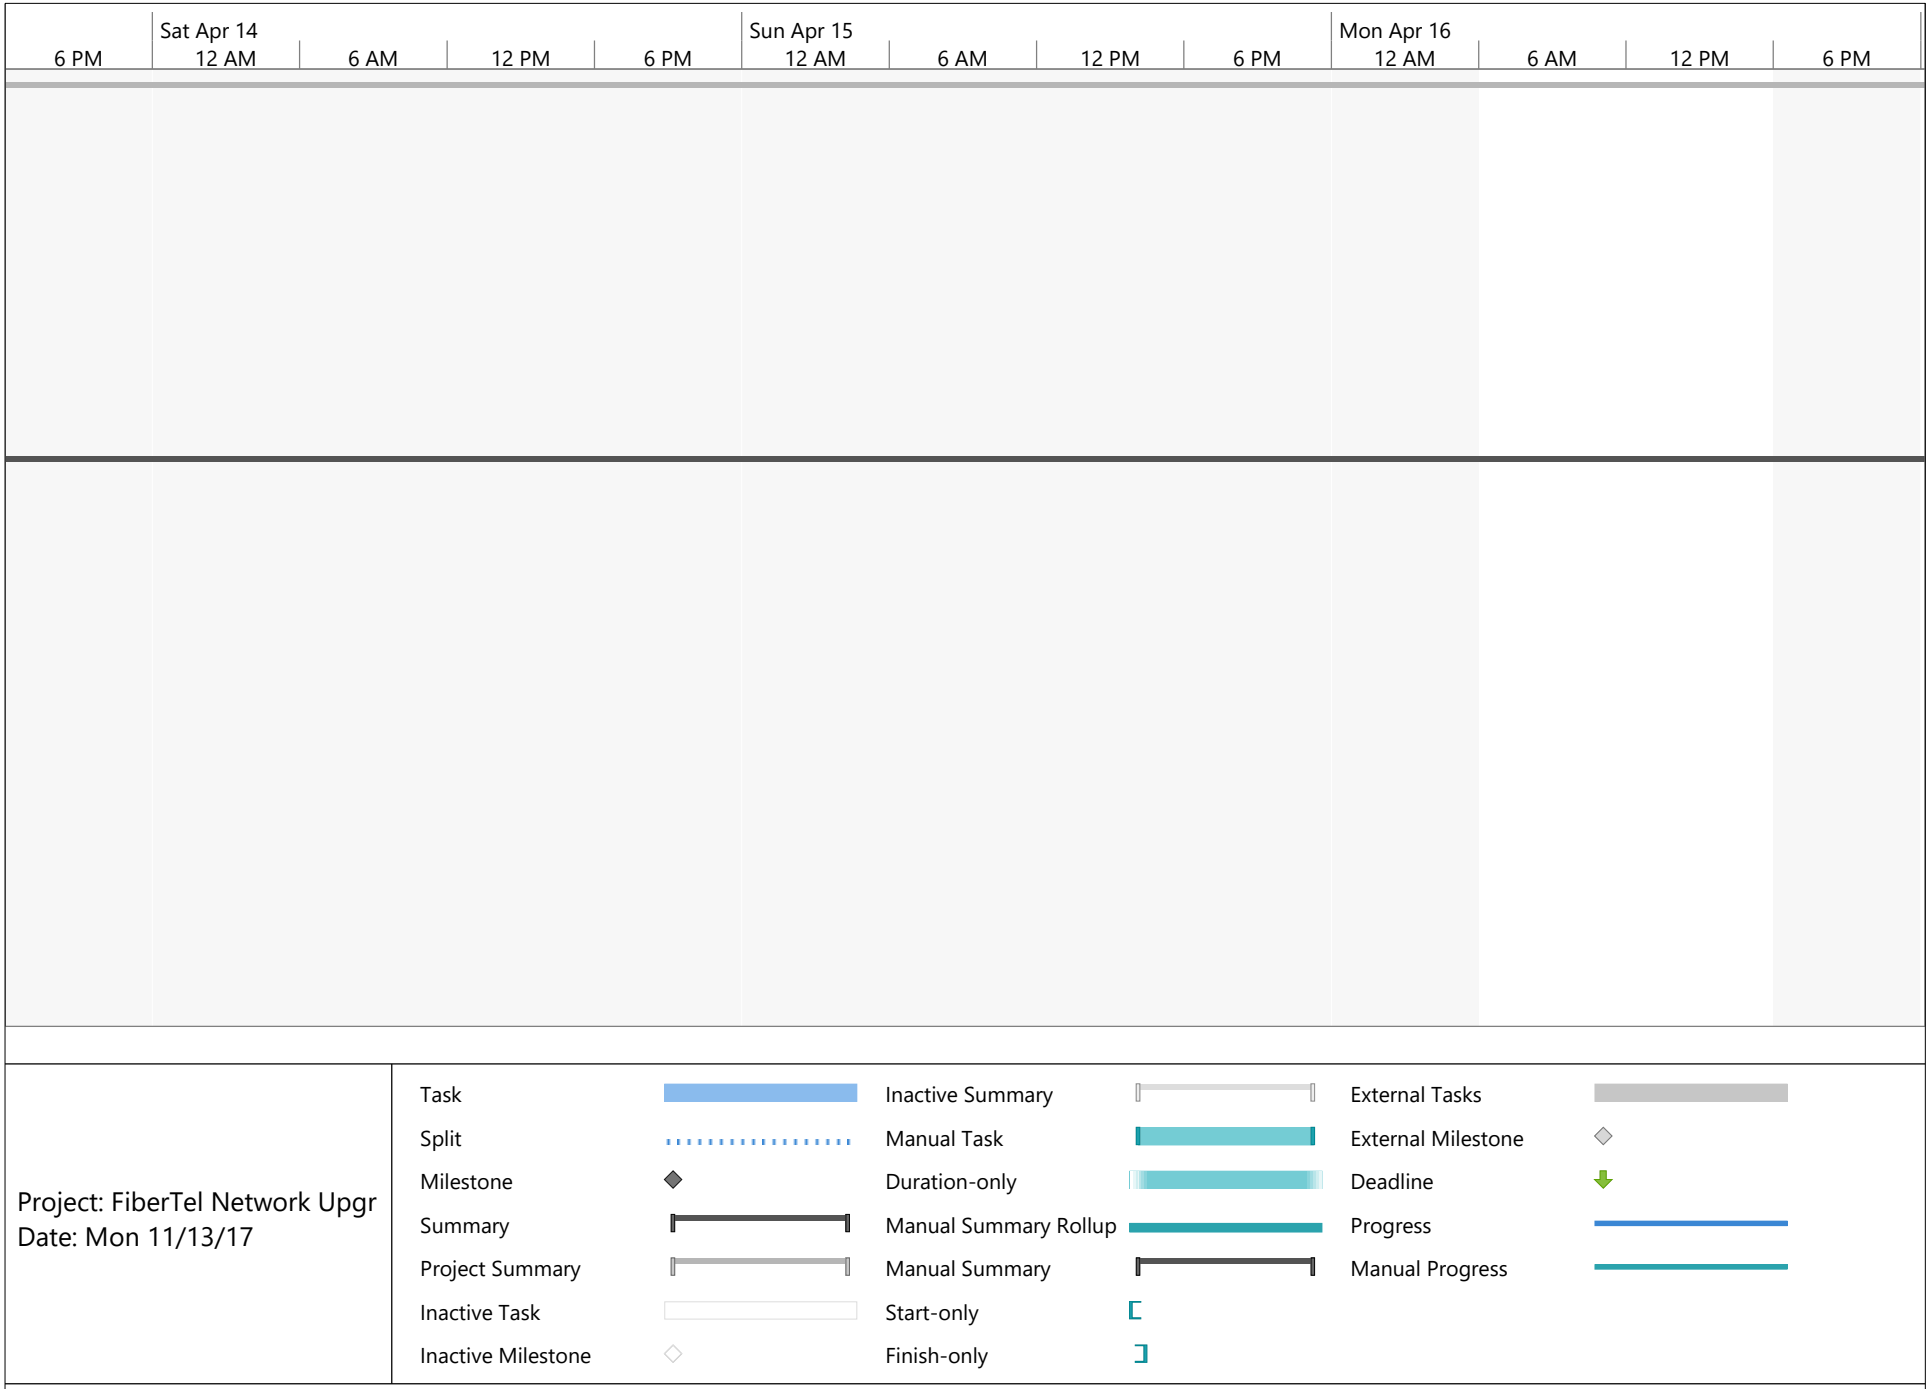

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

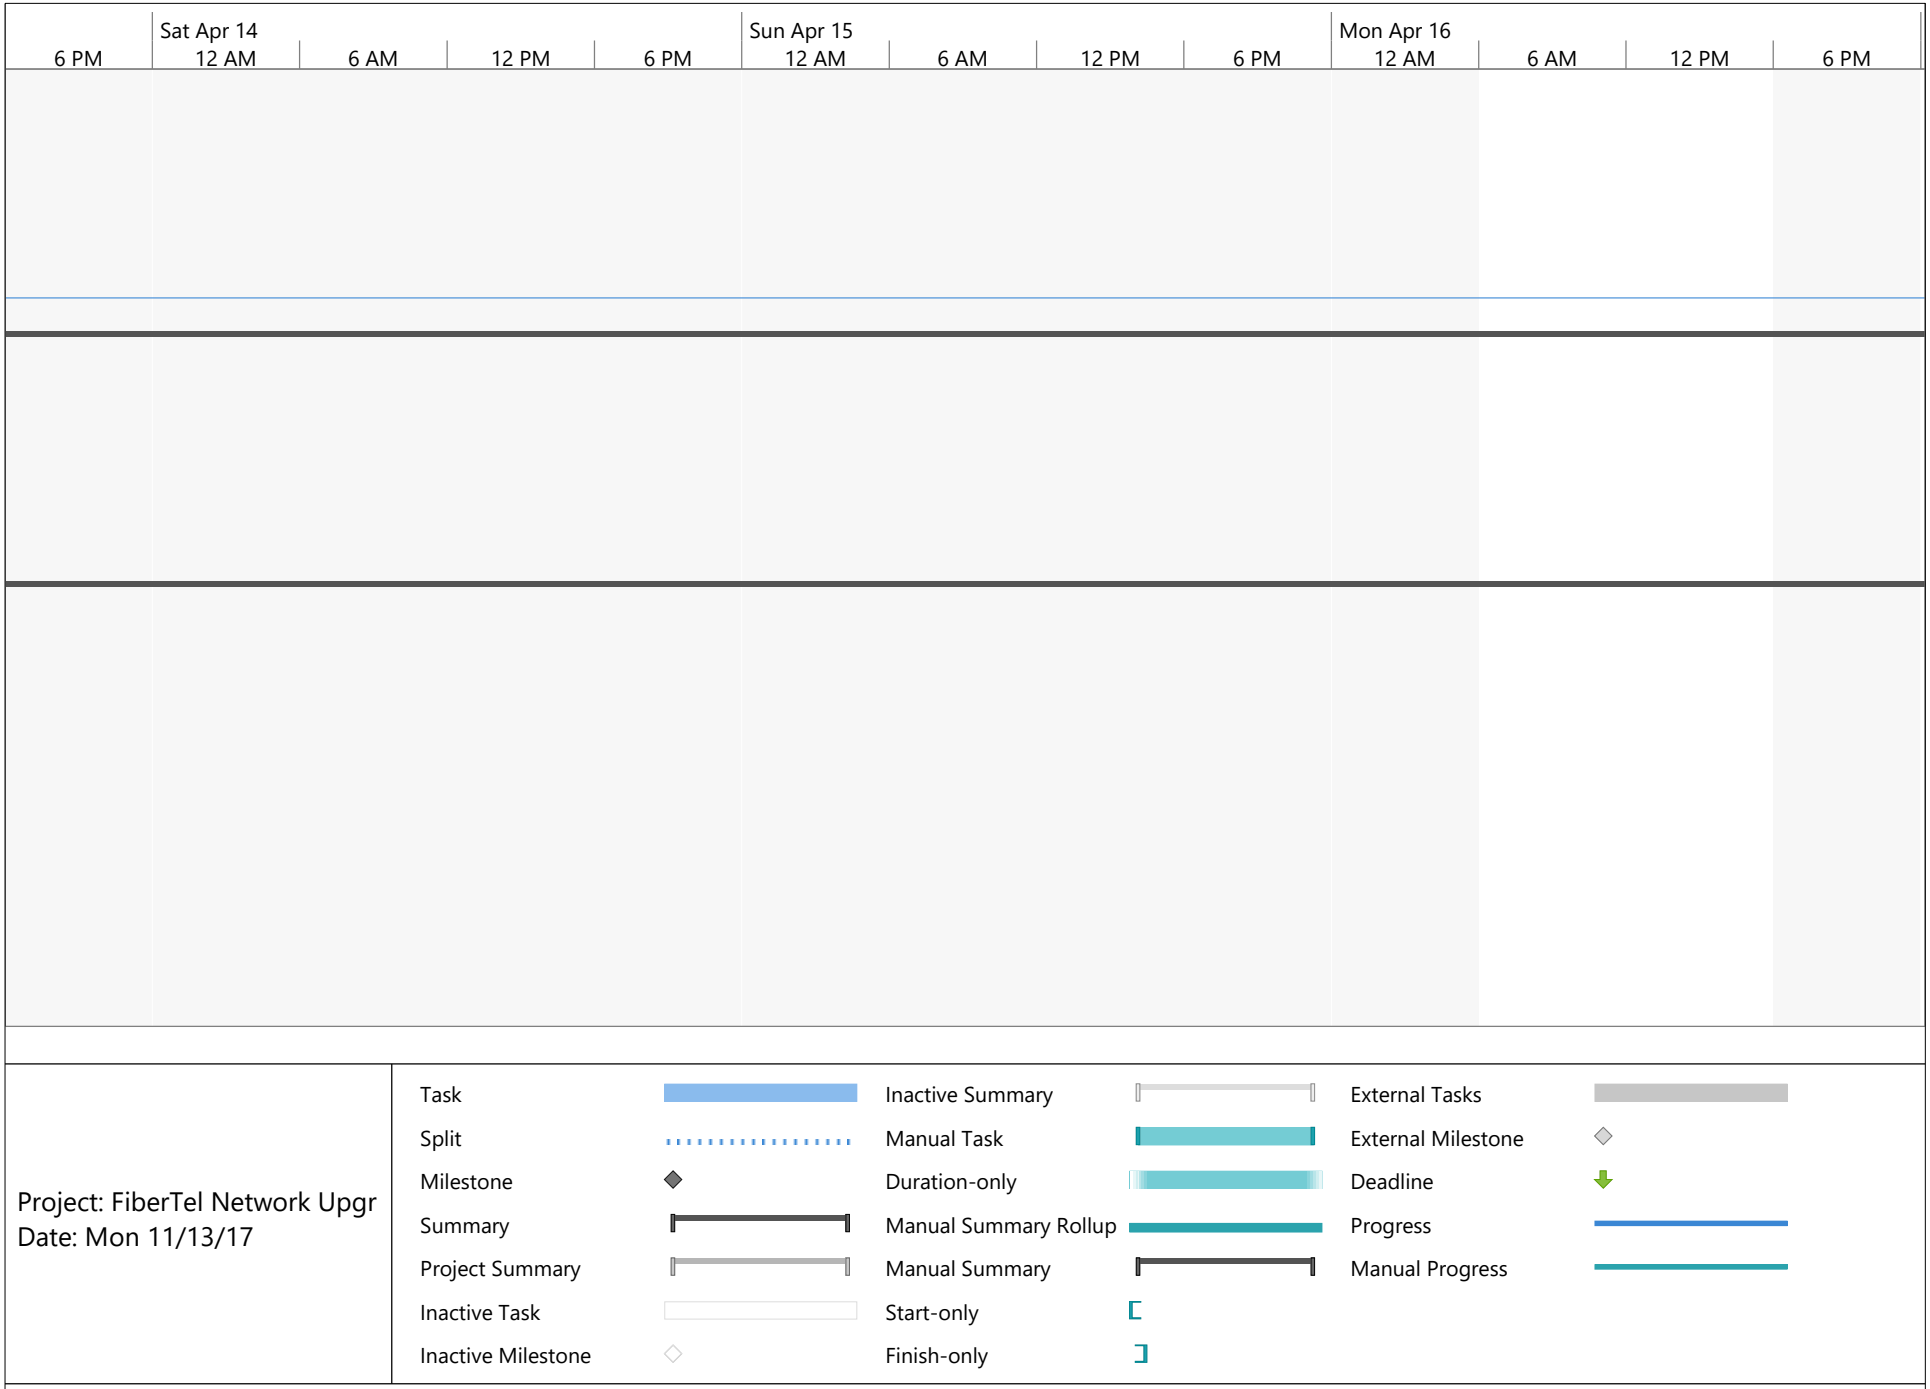

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

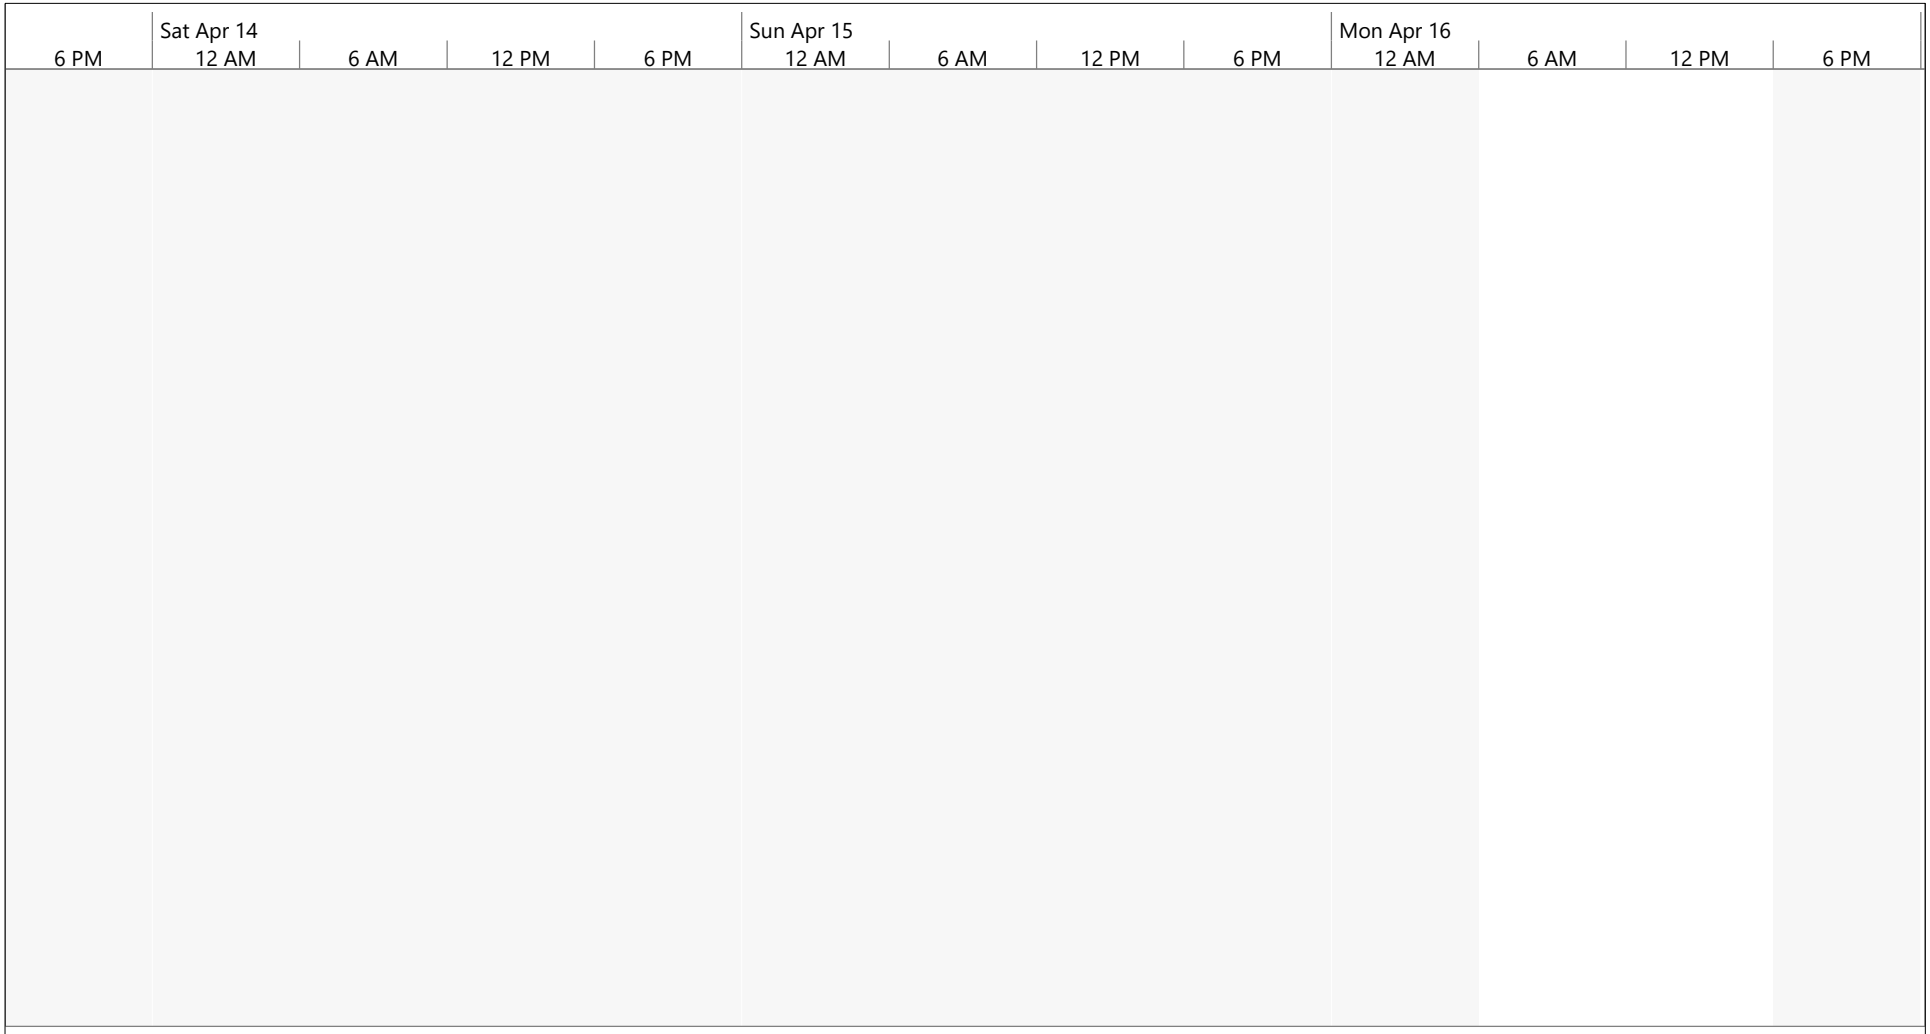

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

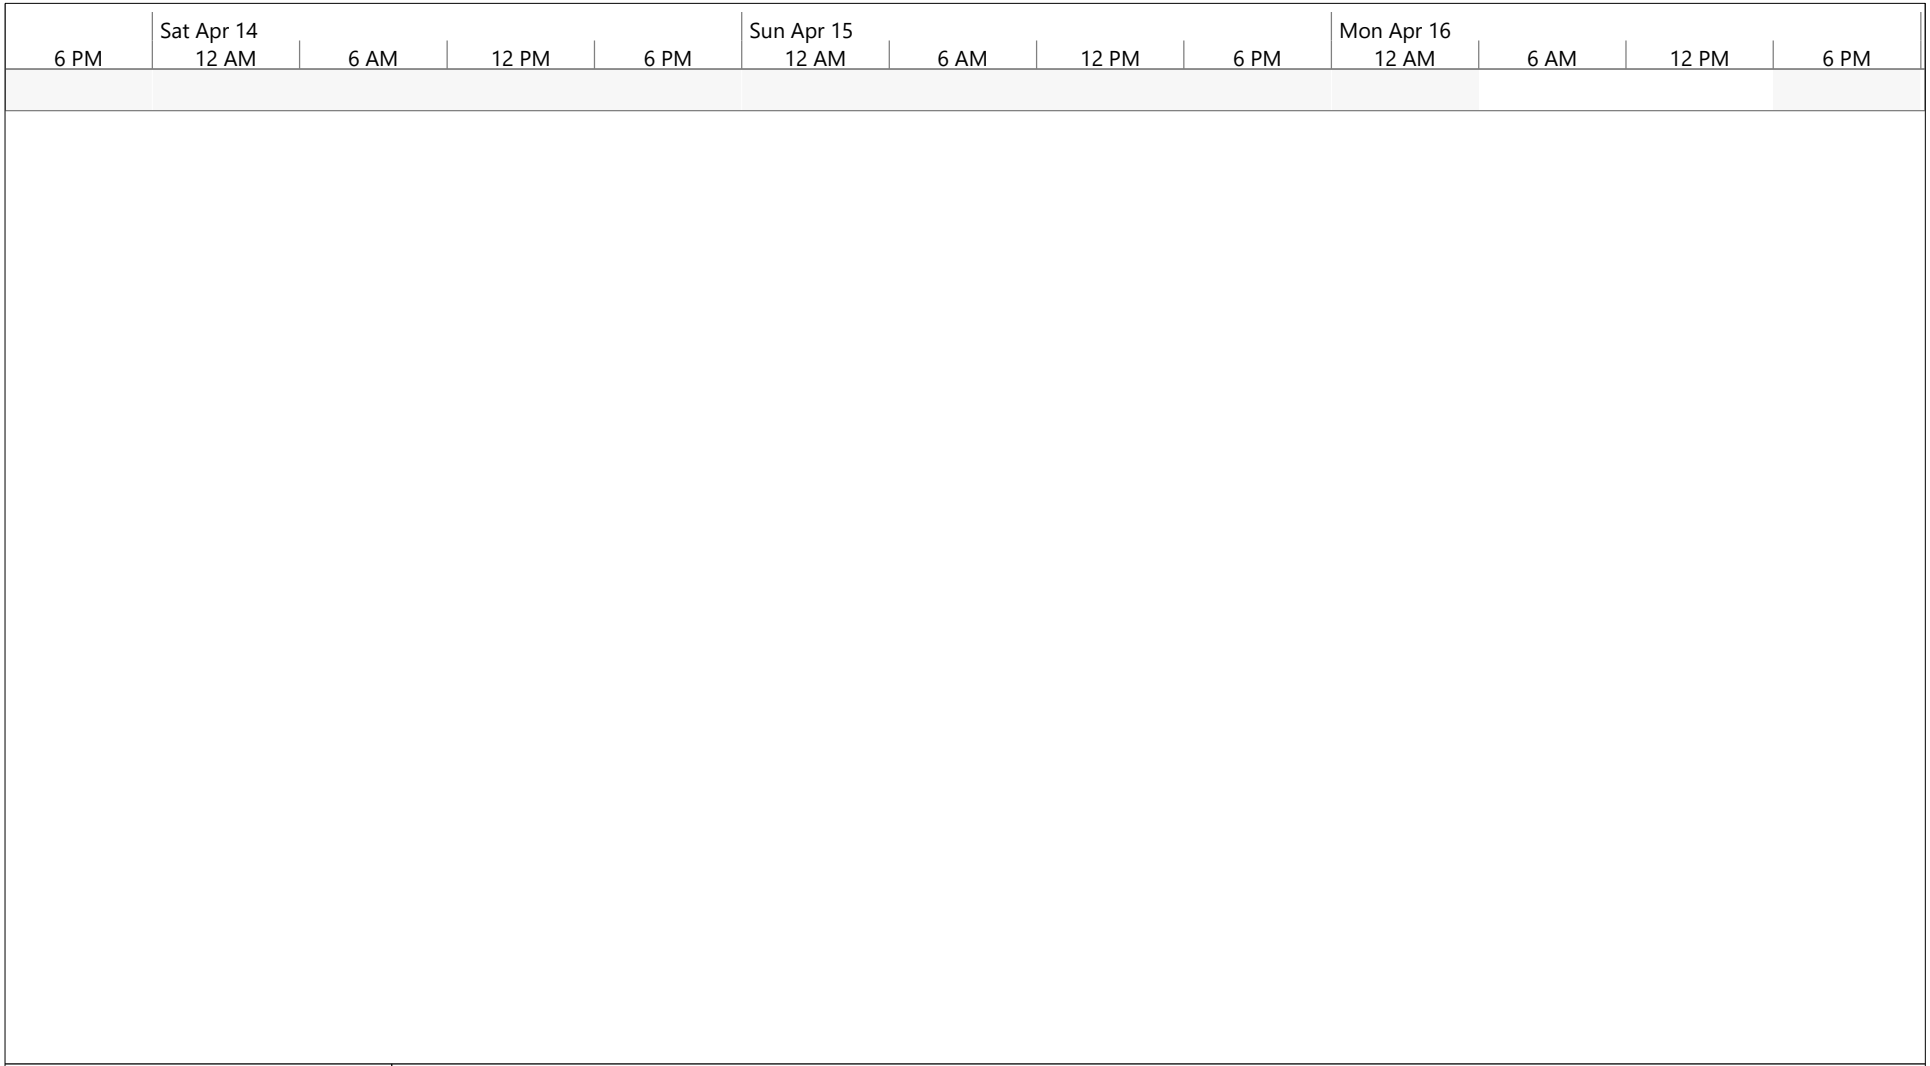

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

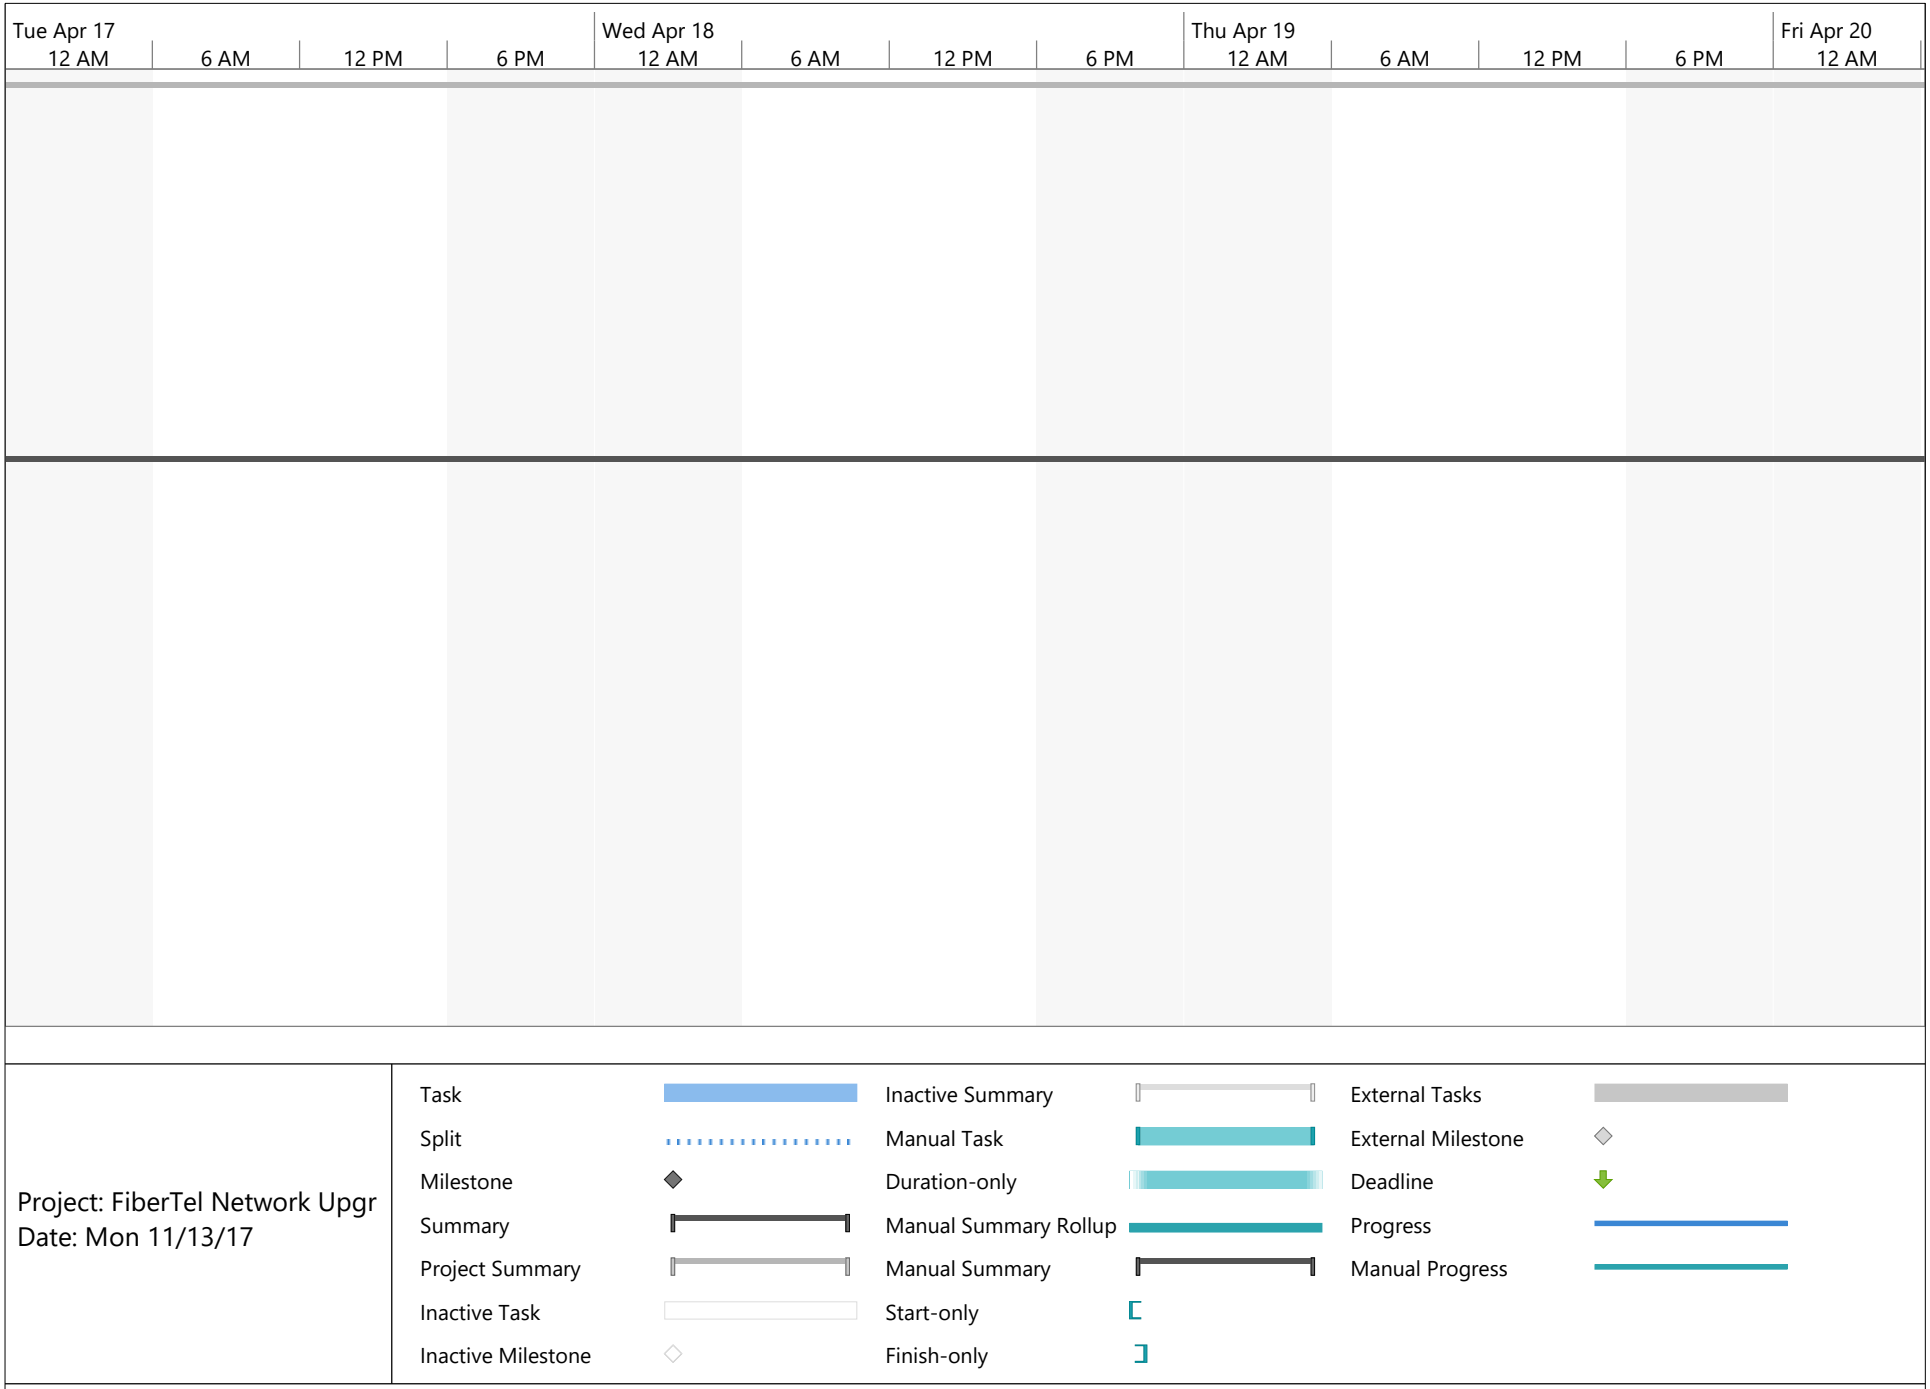

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

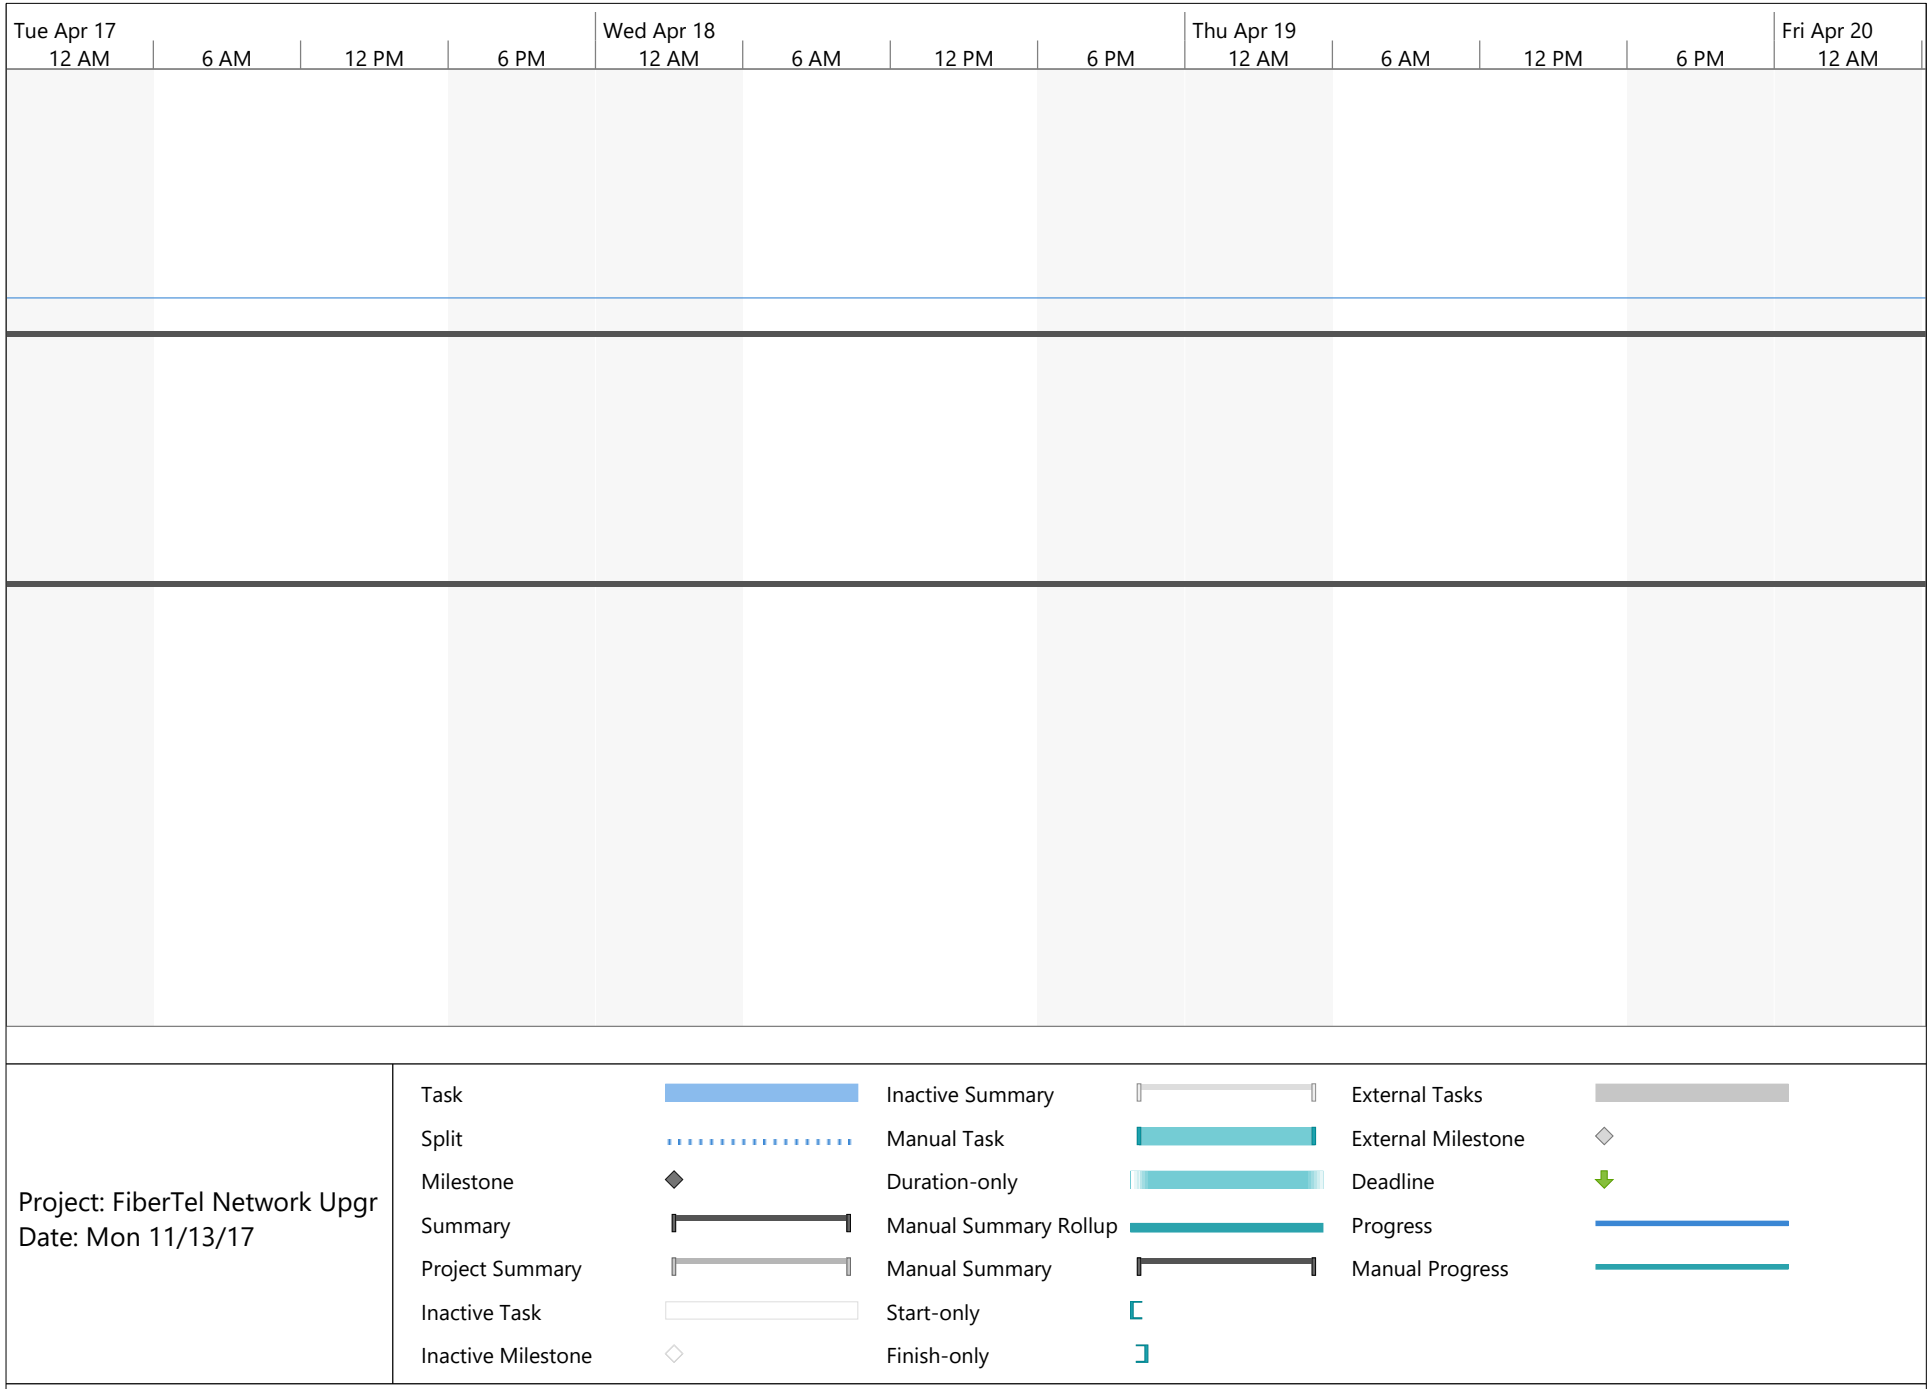

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

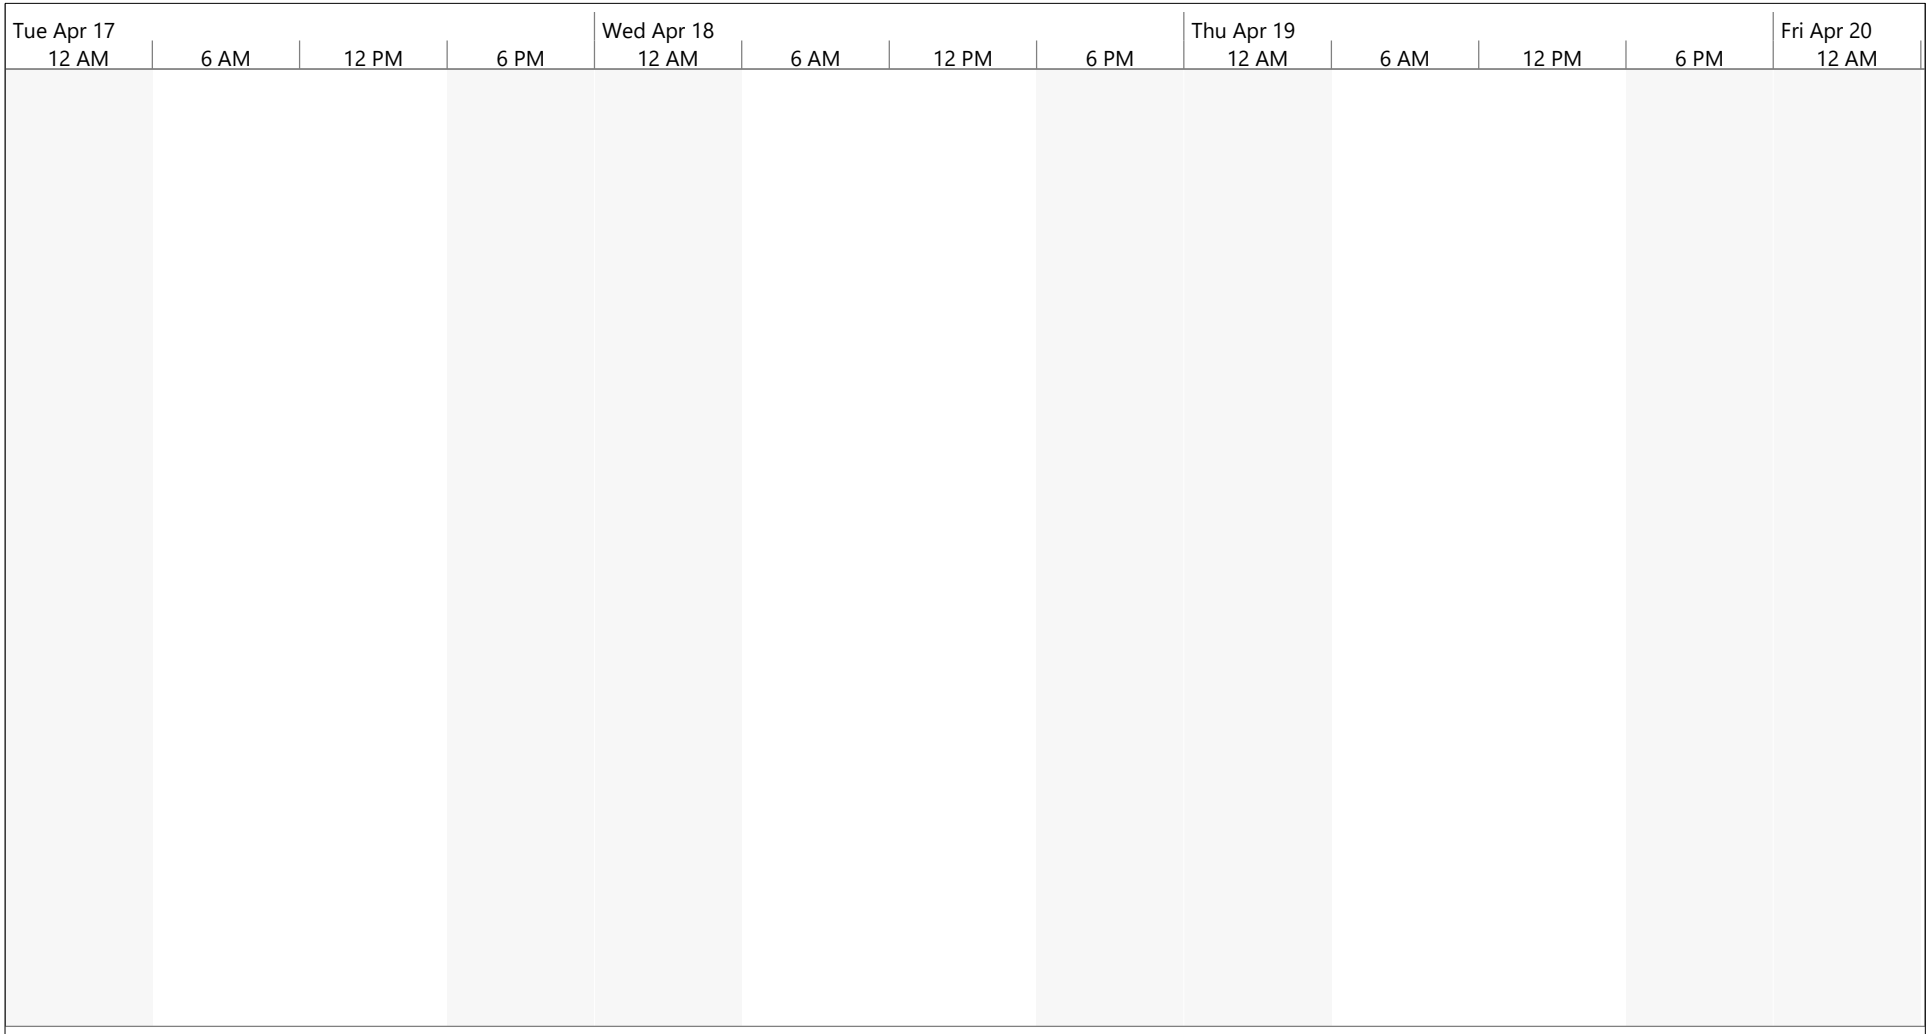

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

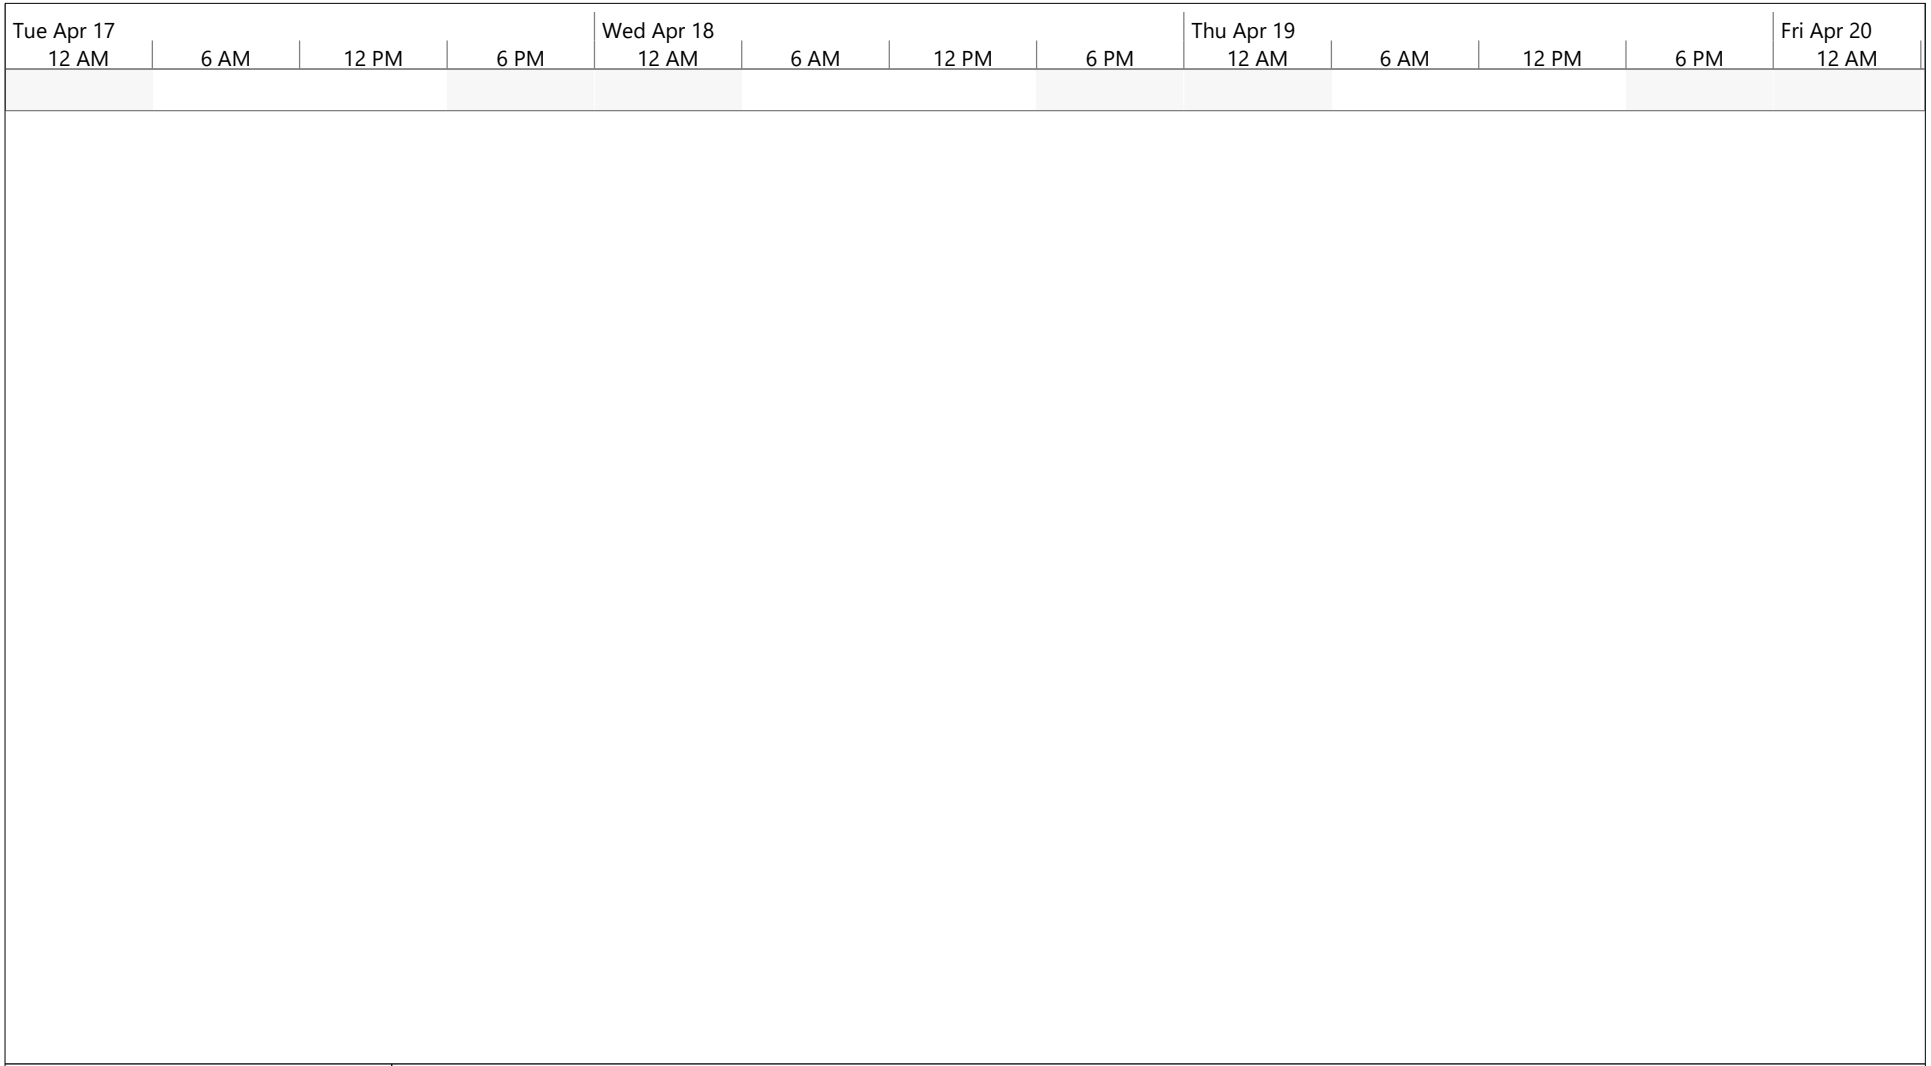

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

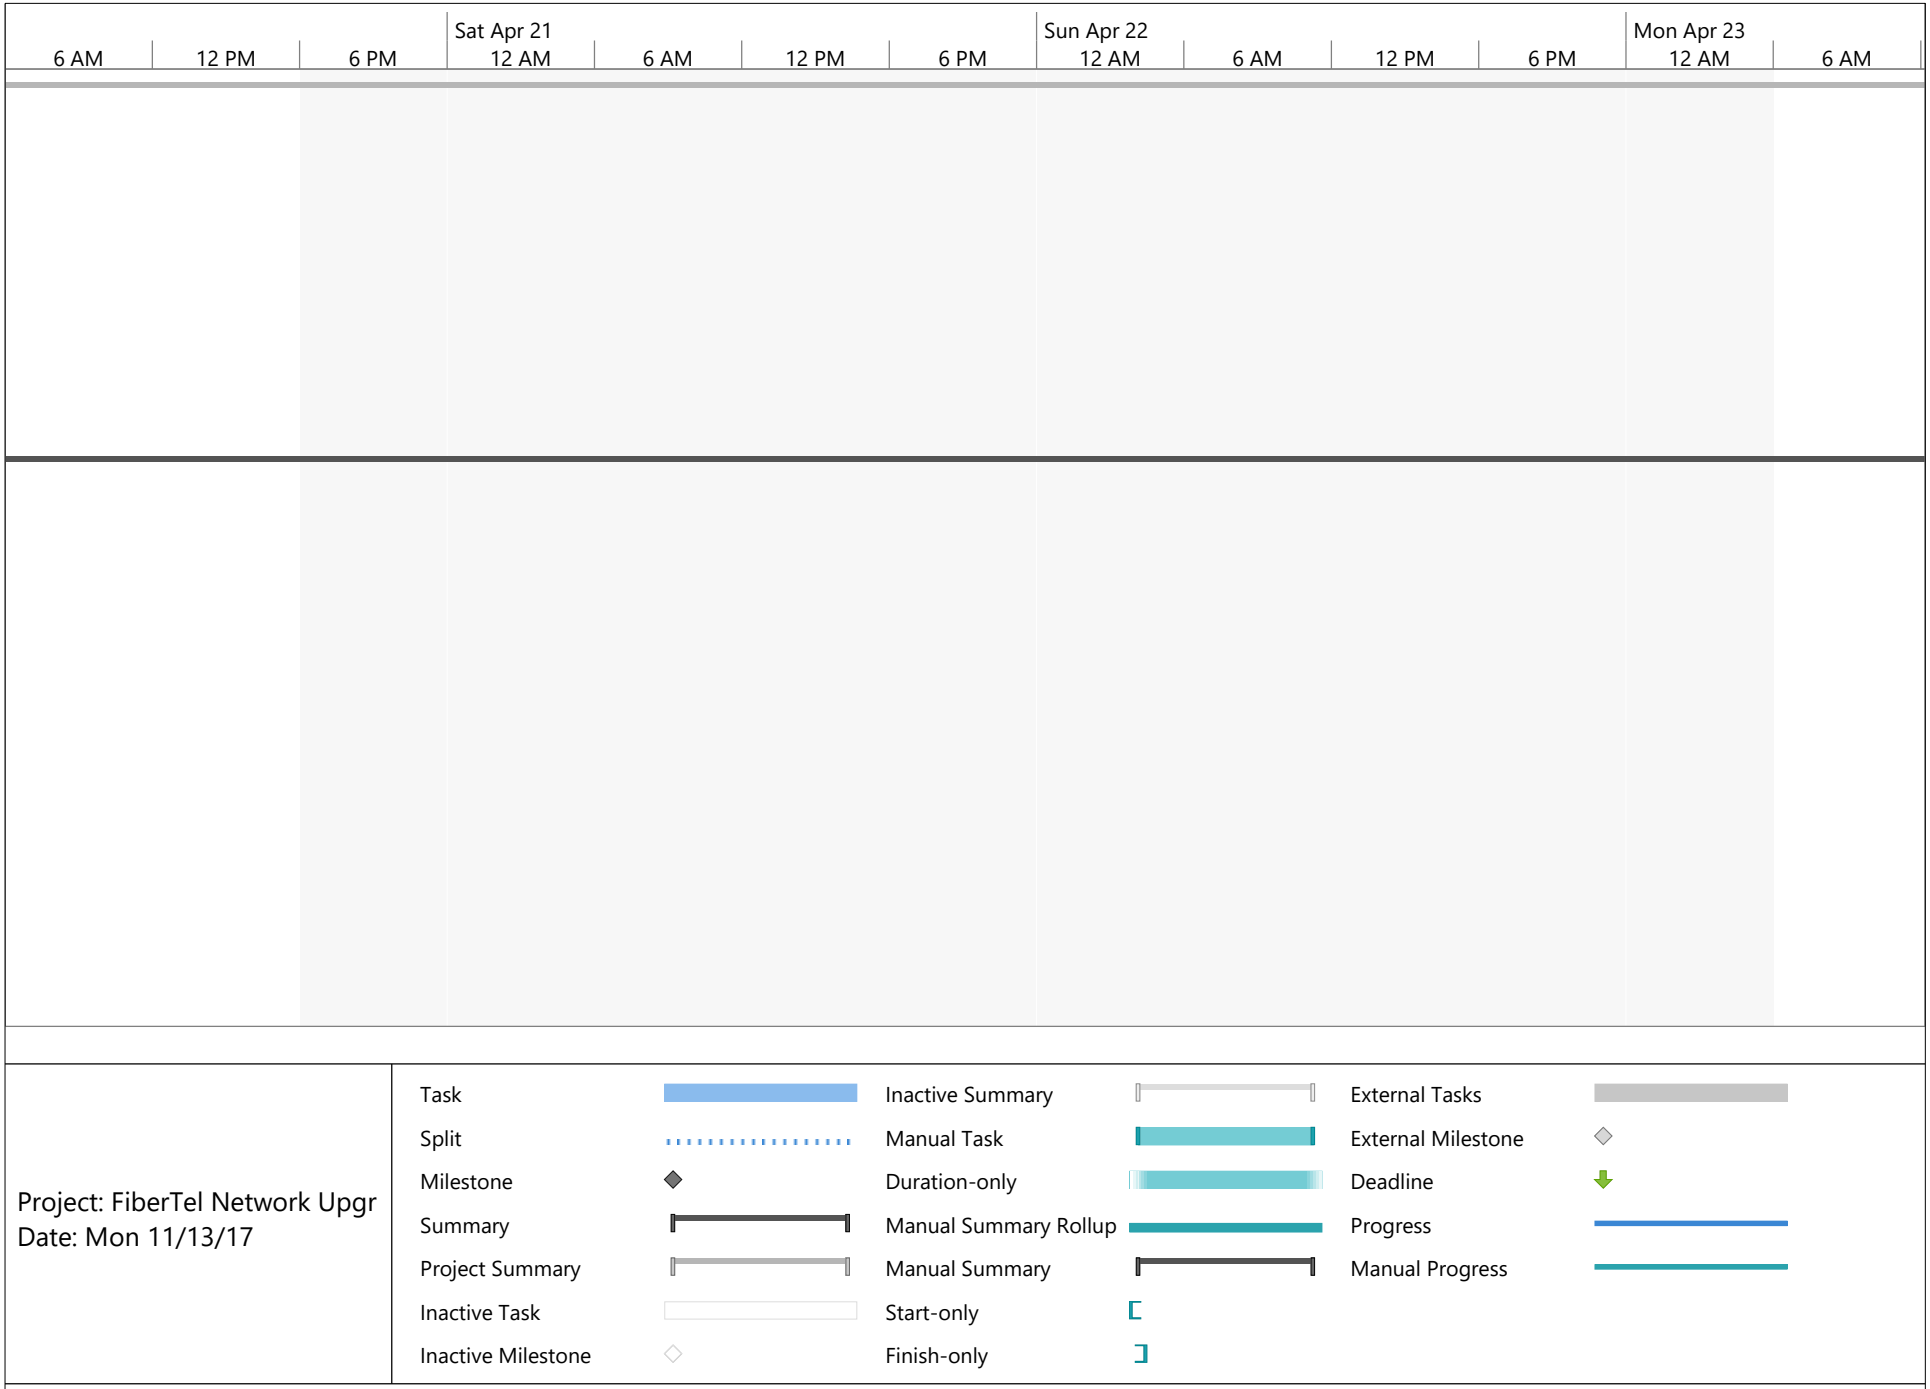

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

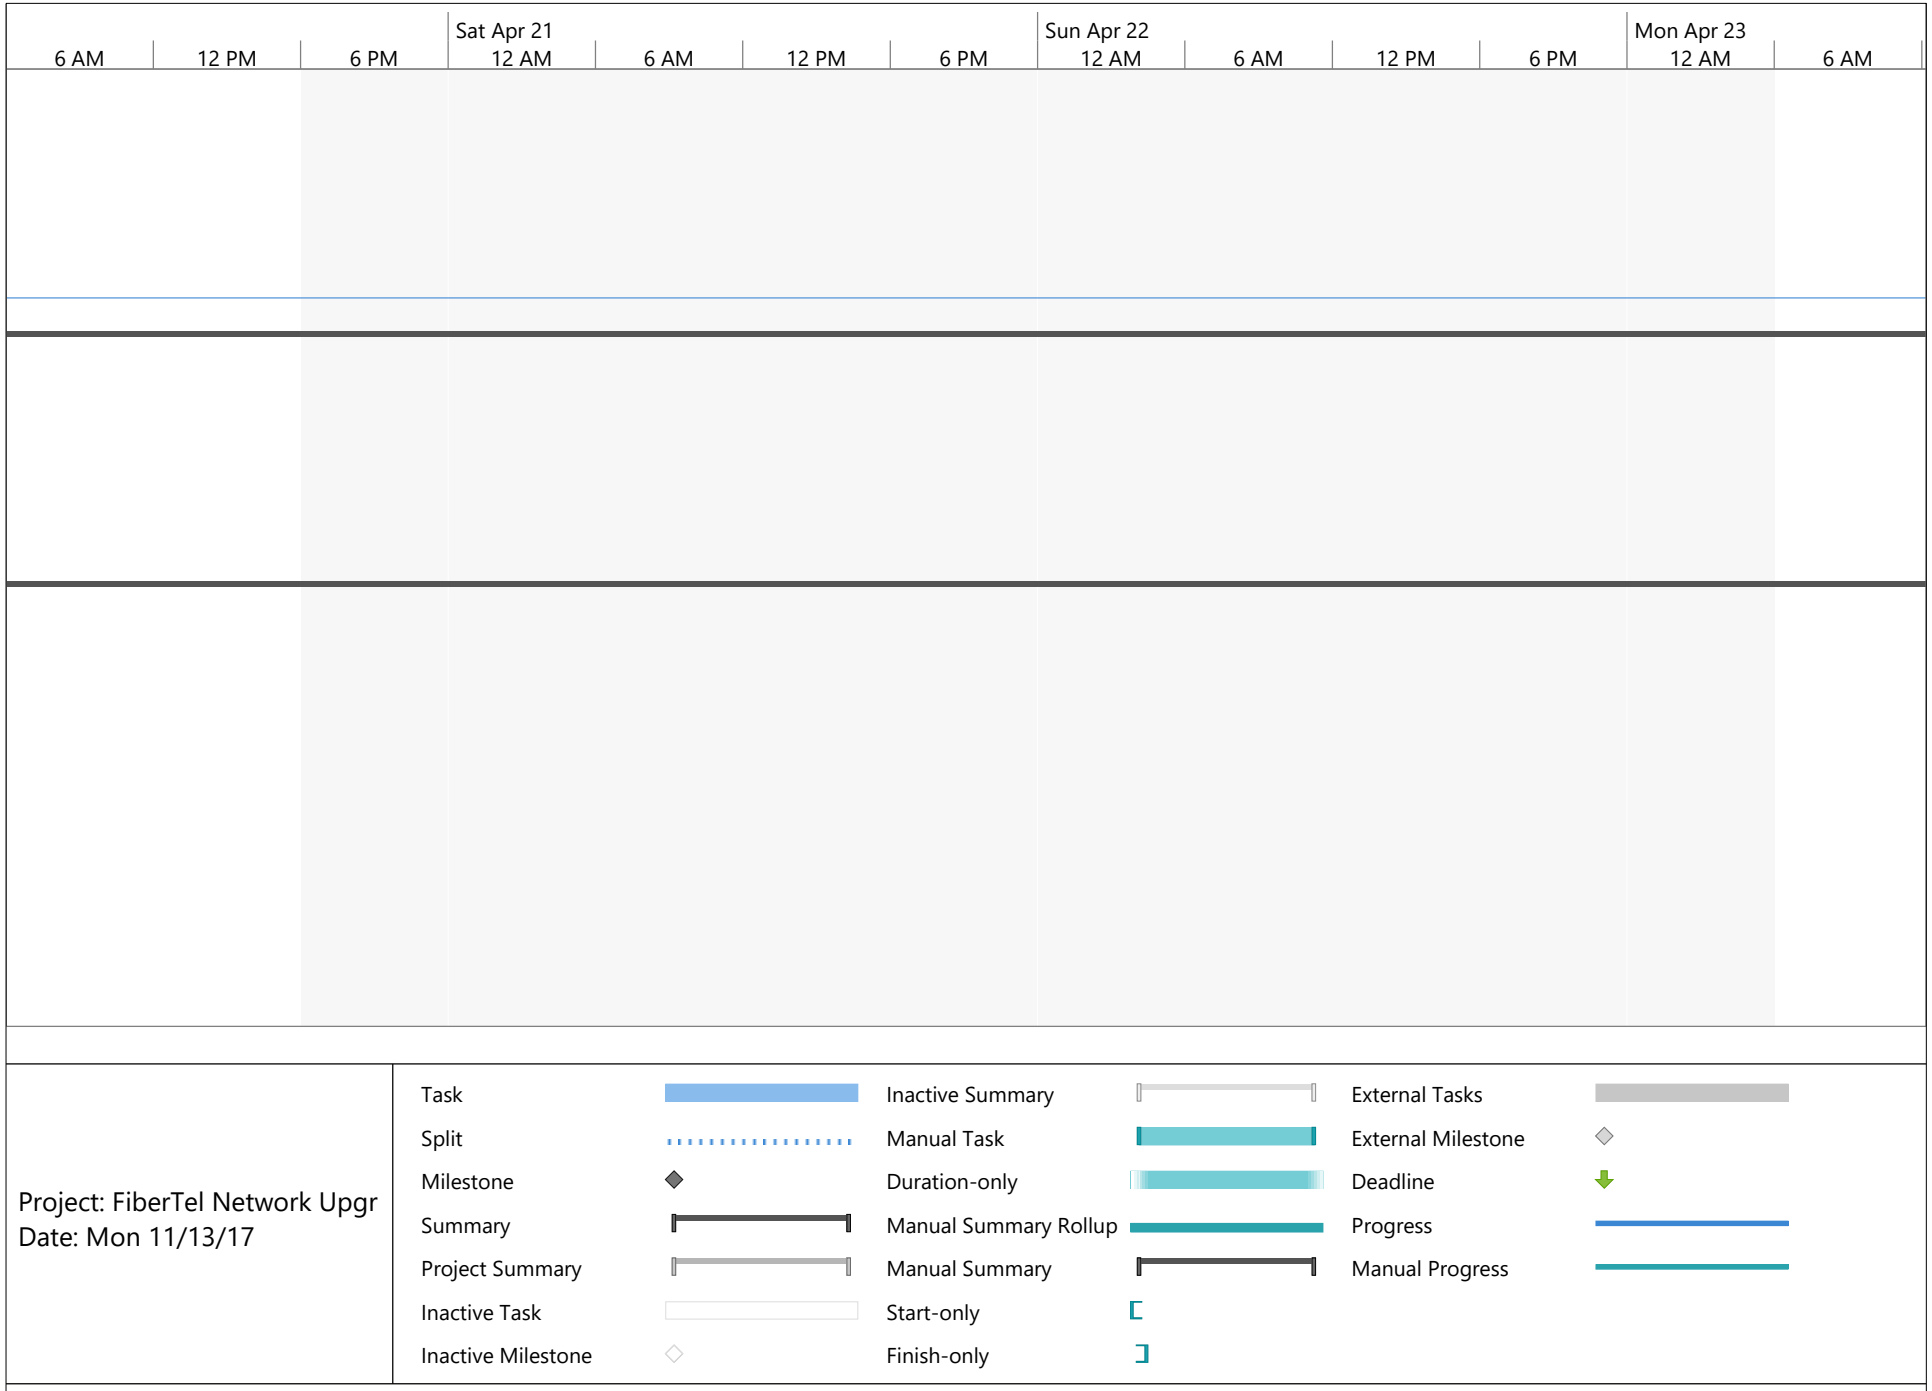
6 AM
12 PM
6 PM
Sat Apr 21
12 AM
6 AM
12 PM
6 PM
Sun Apr 22
12 AM
6 AM
12 PM
6 PM
Mon Apr 23
12 AM
6 AM
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

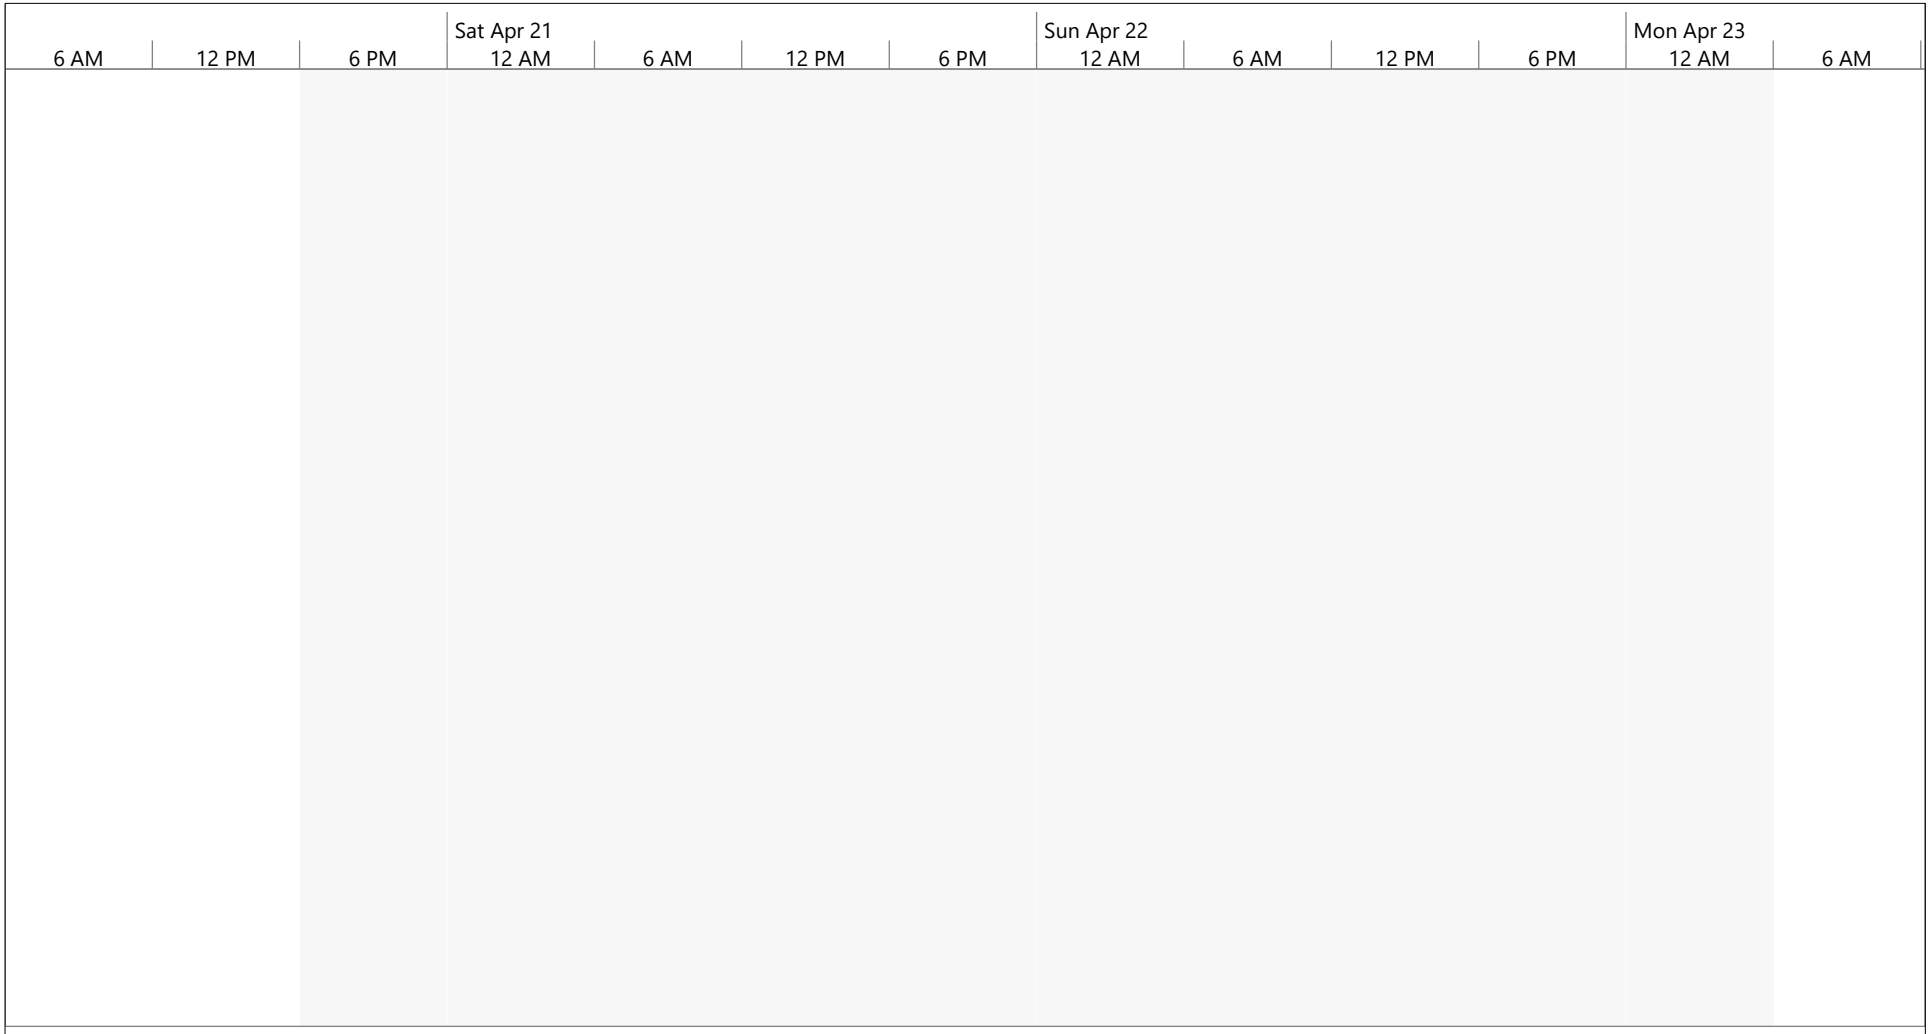

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

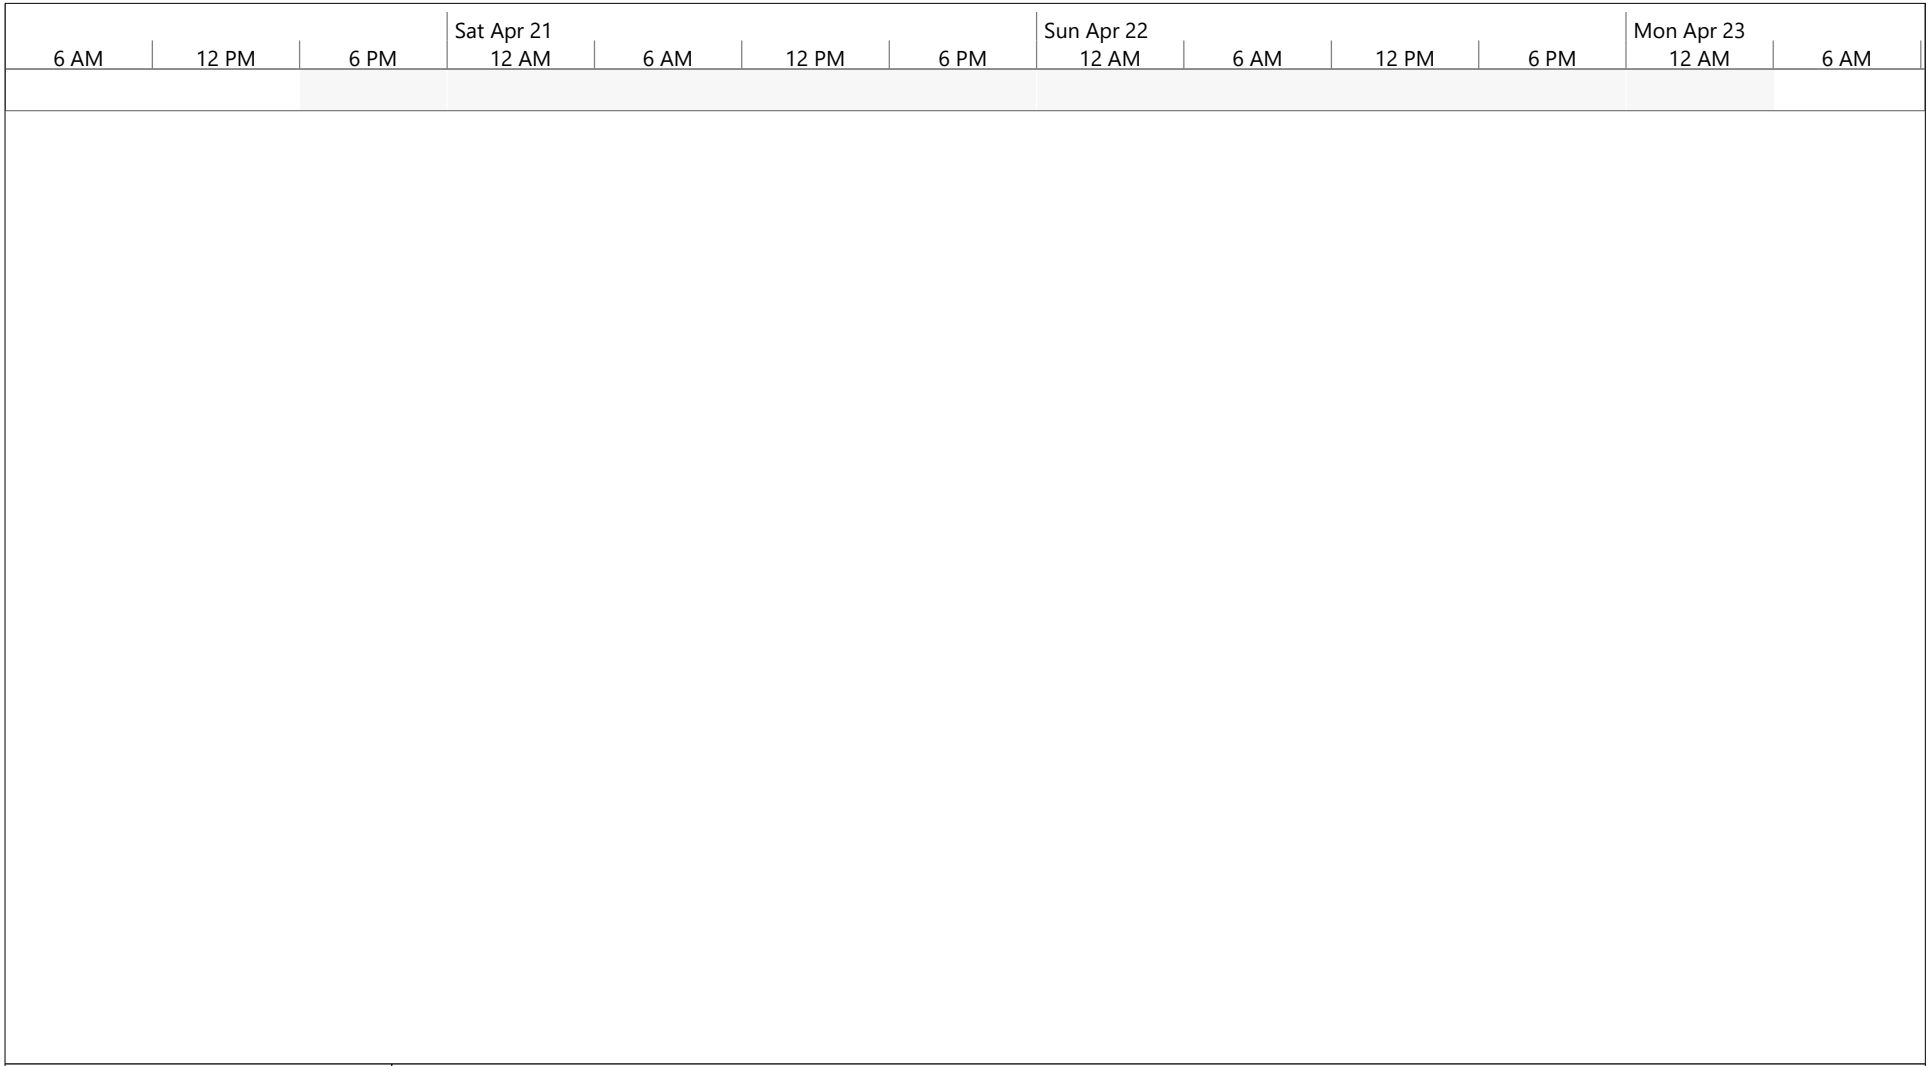

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

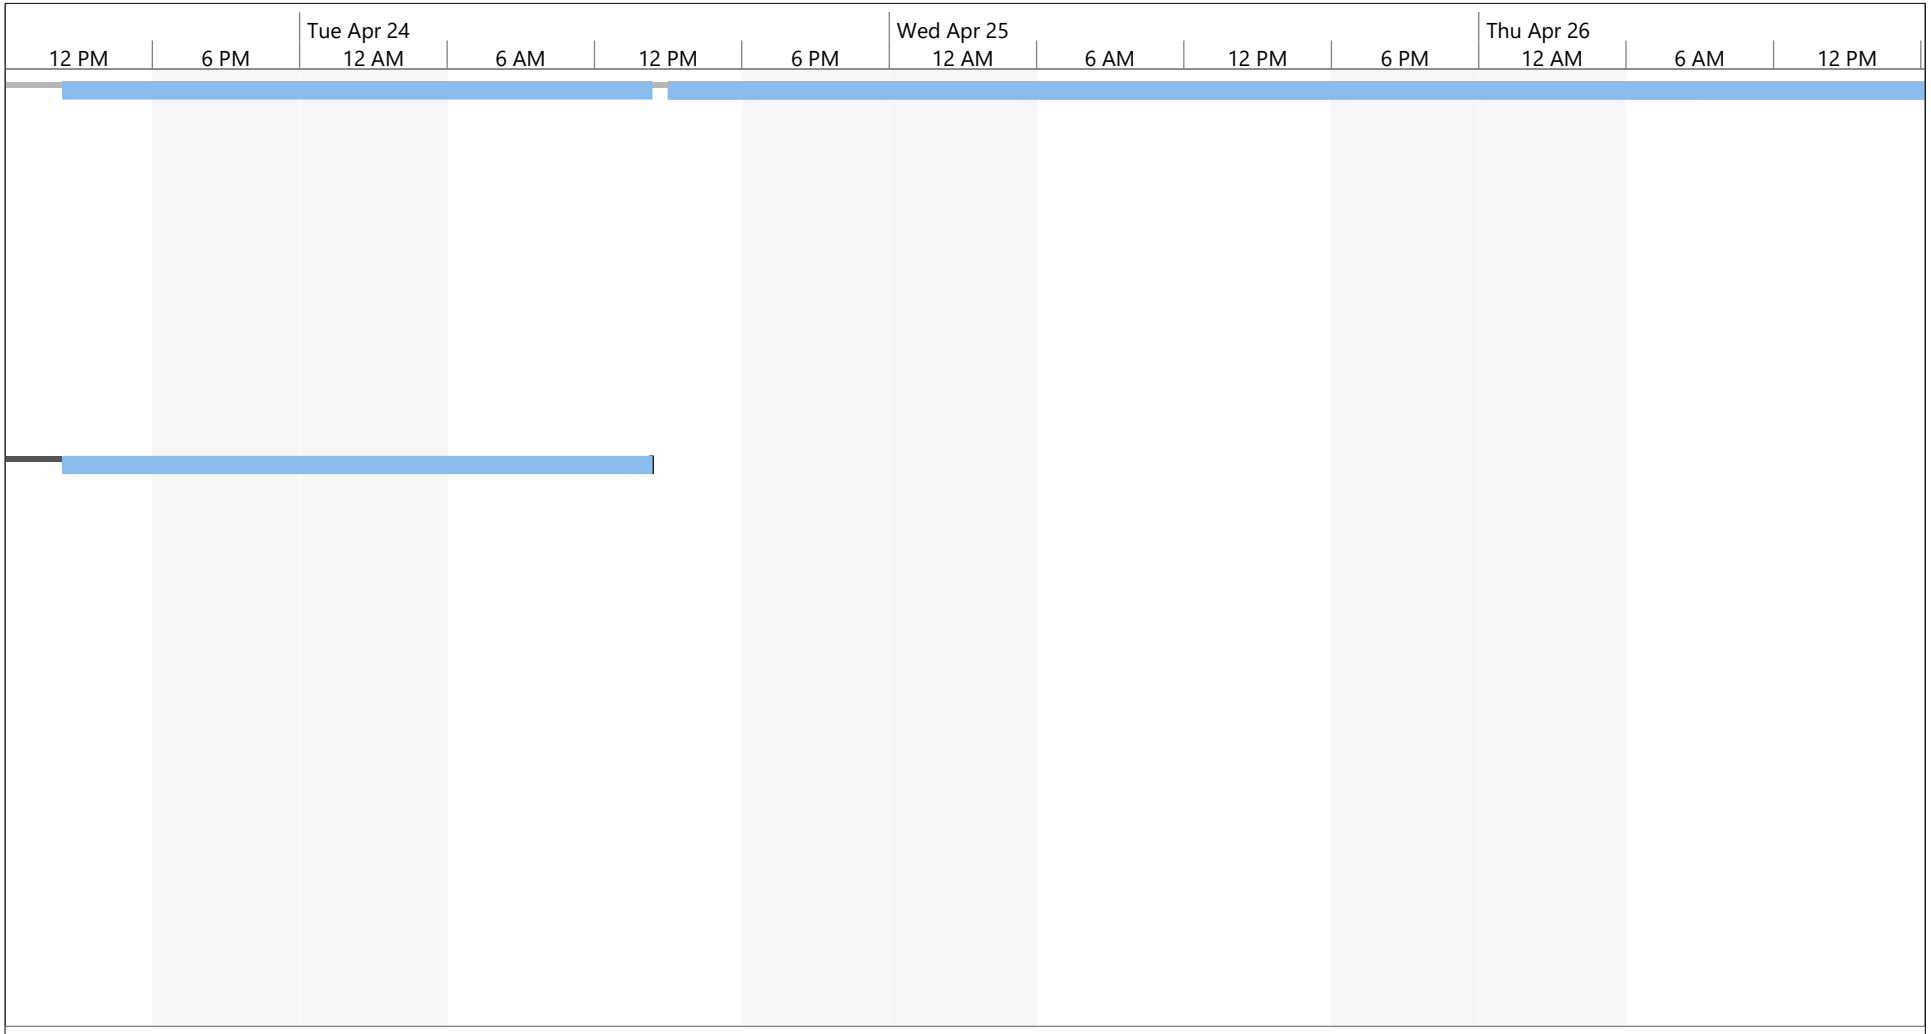

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

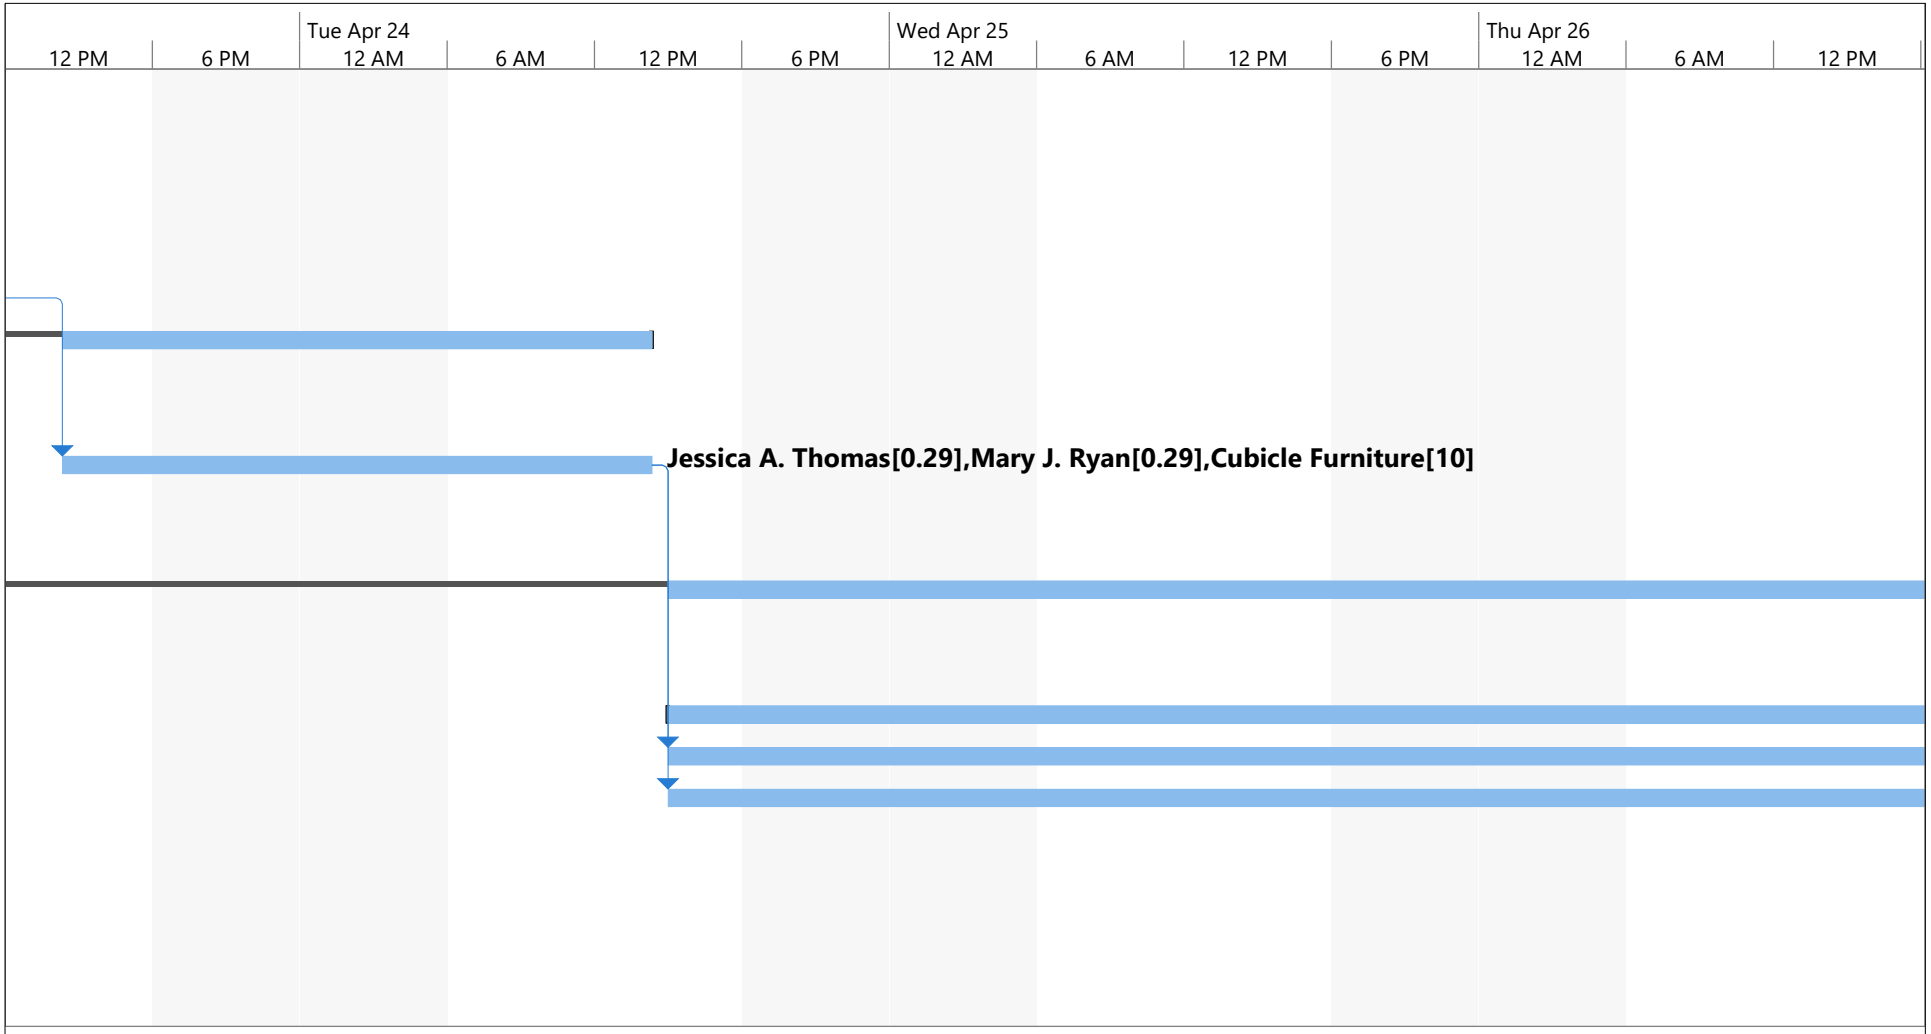

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

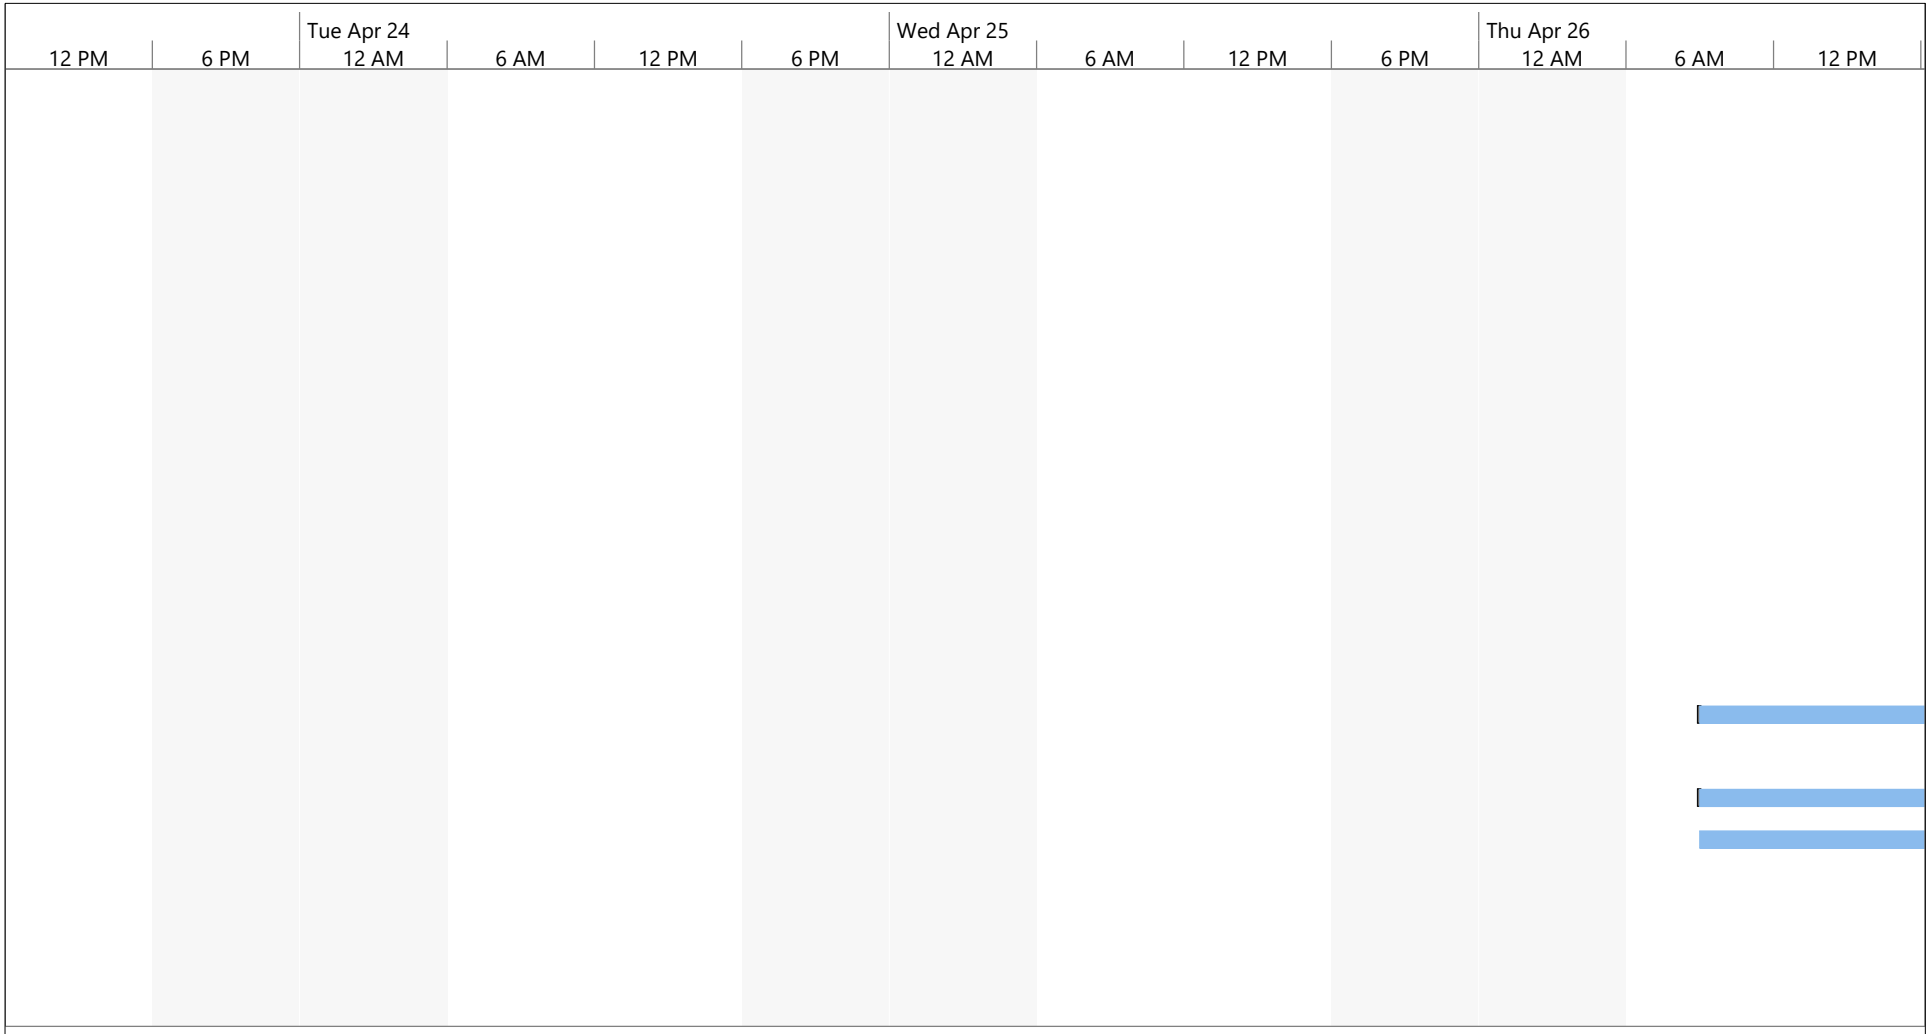

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

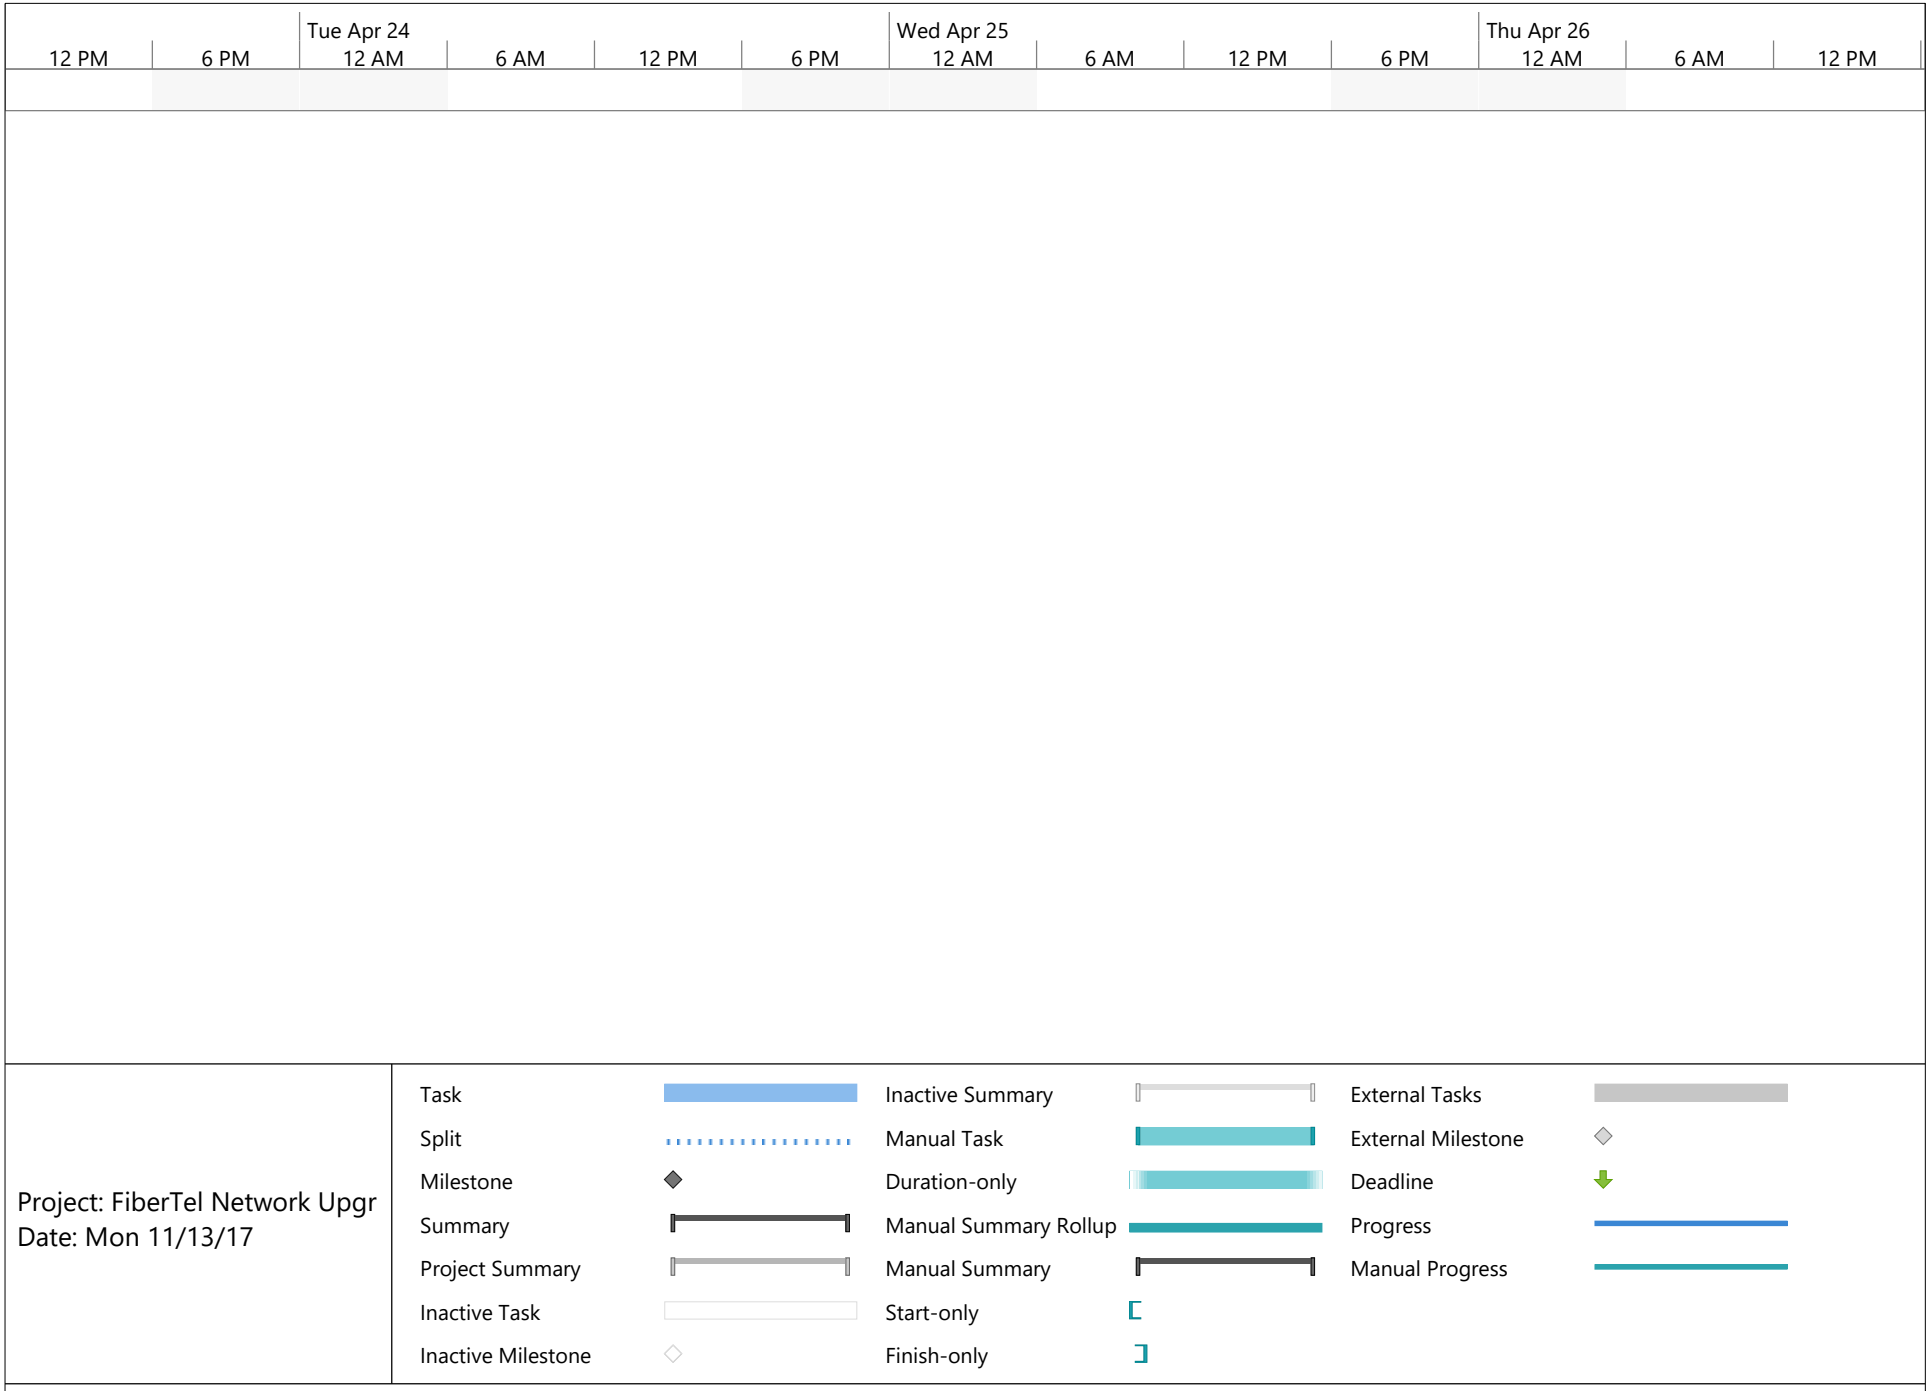
12 PM
6 PM
Tue Apr 24
12 AM
6 AM
12 PM
6 PM
Wed Apr 25
12 AM
6 AM
12 PM
6 PM
Thu Apr 26
12 AM
6 AM
12 PM
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

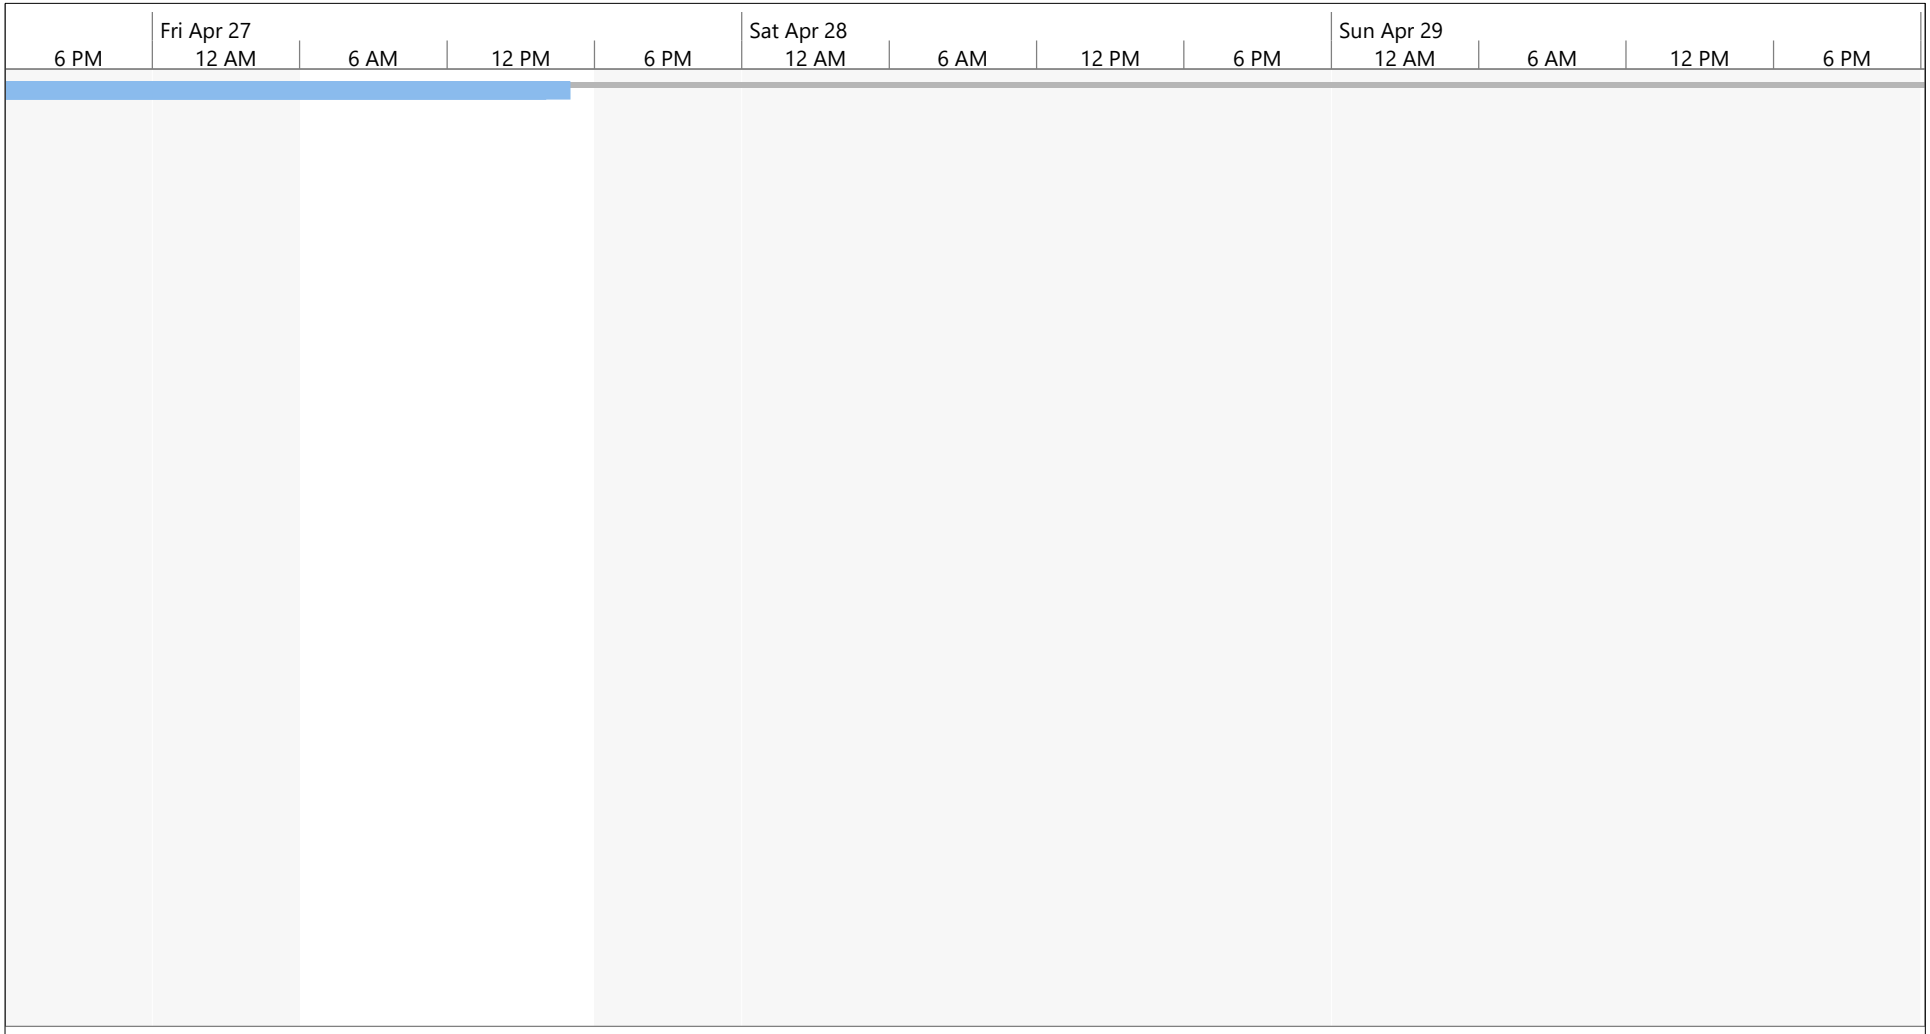

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

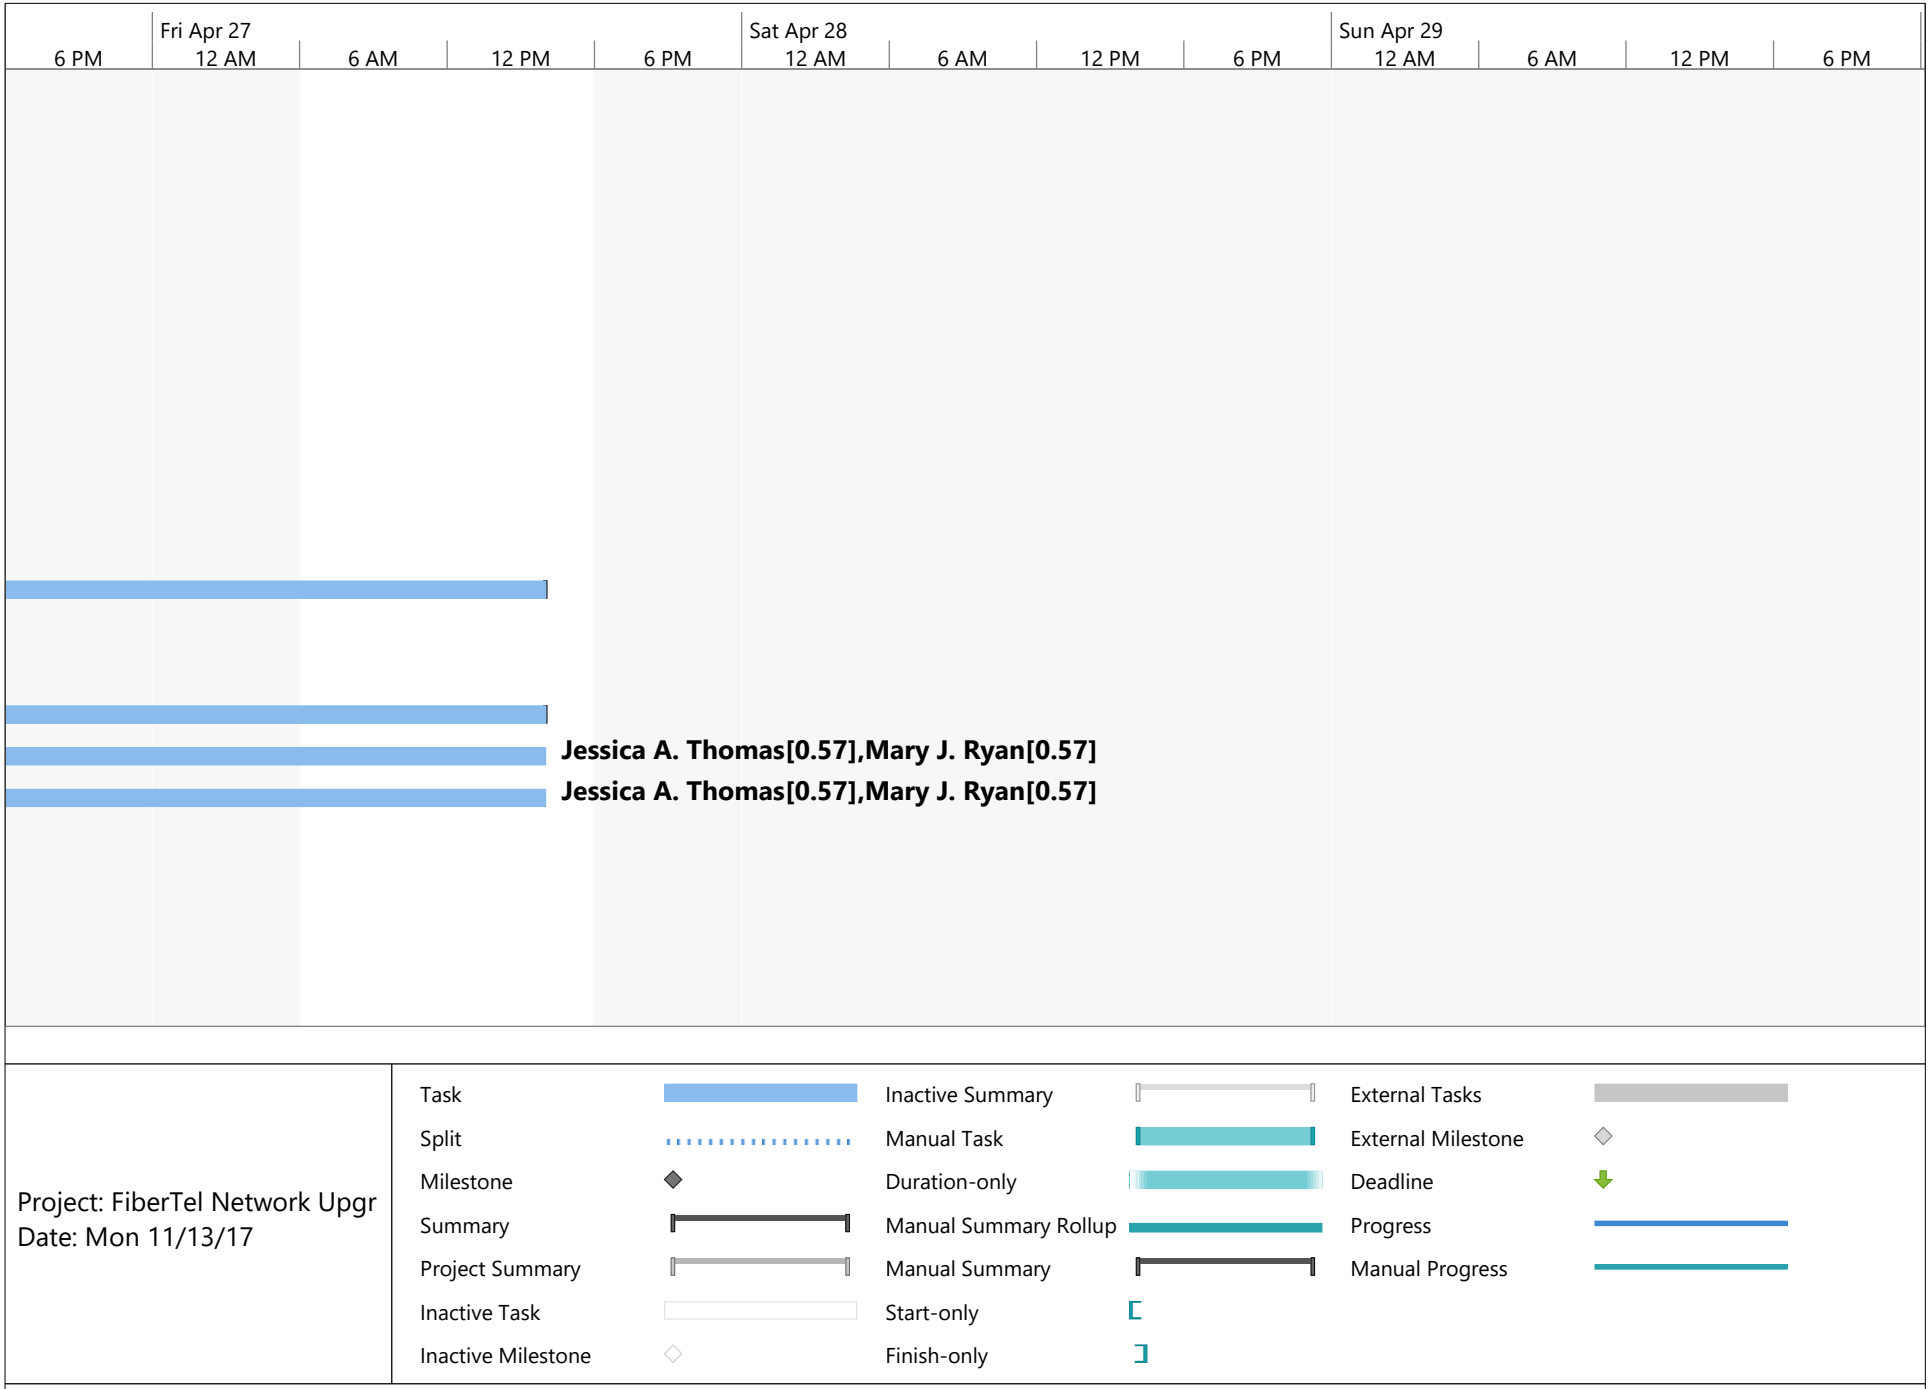

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

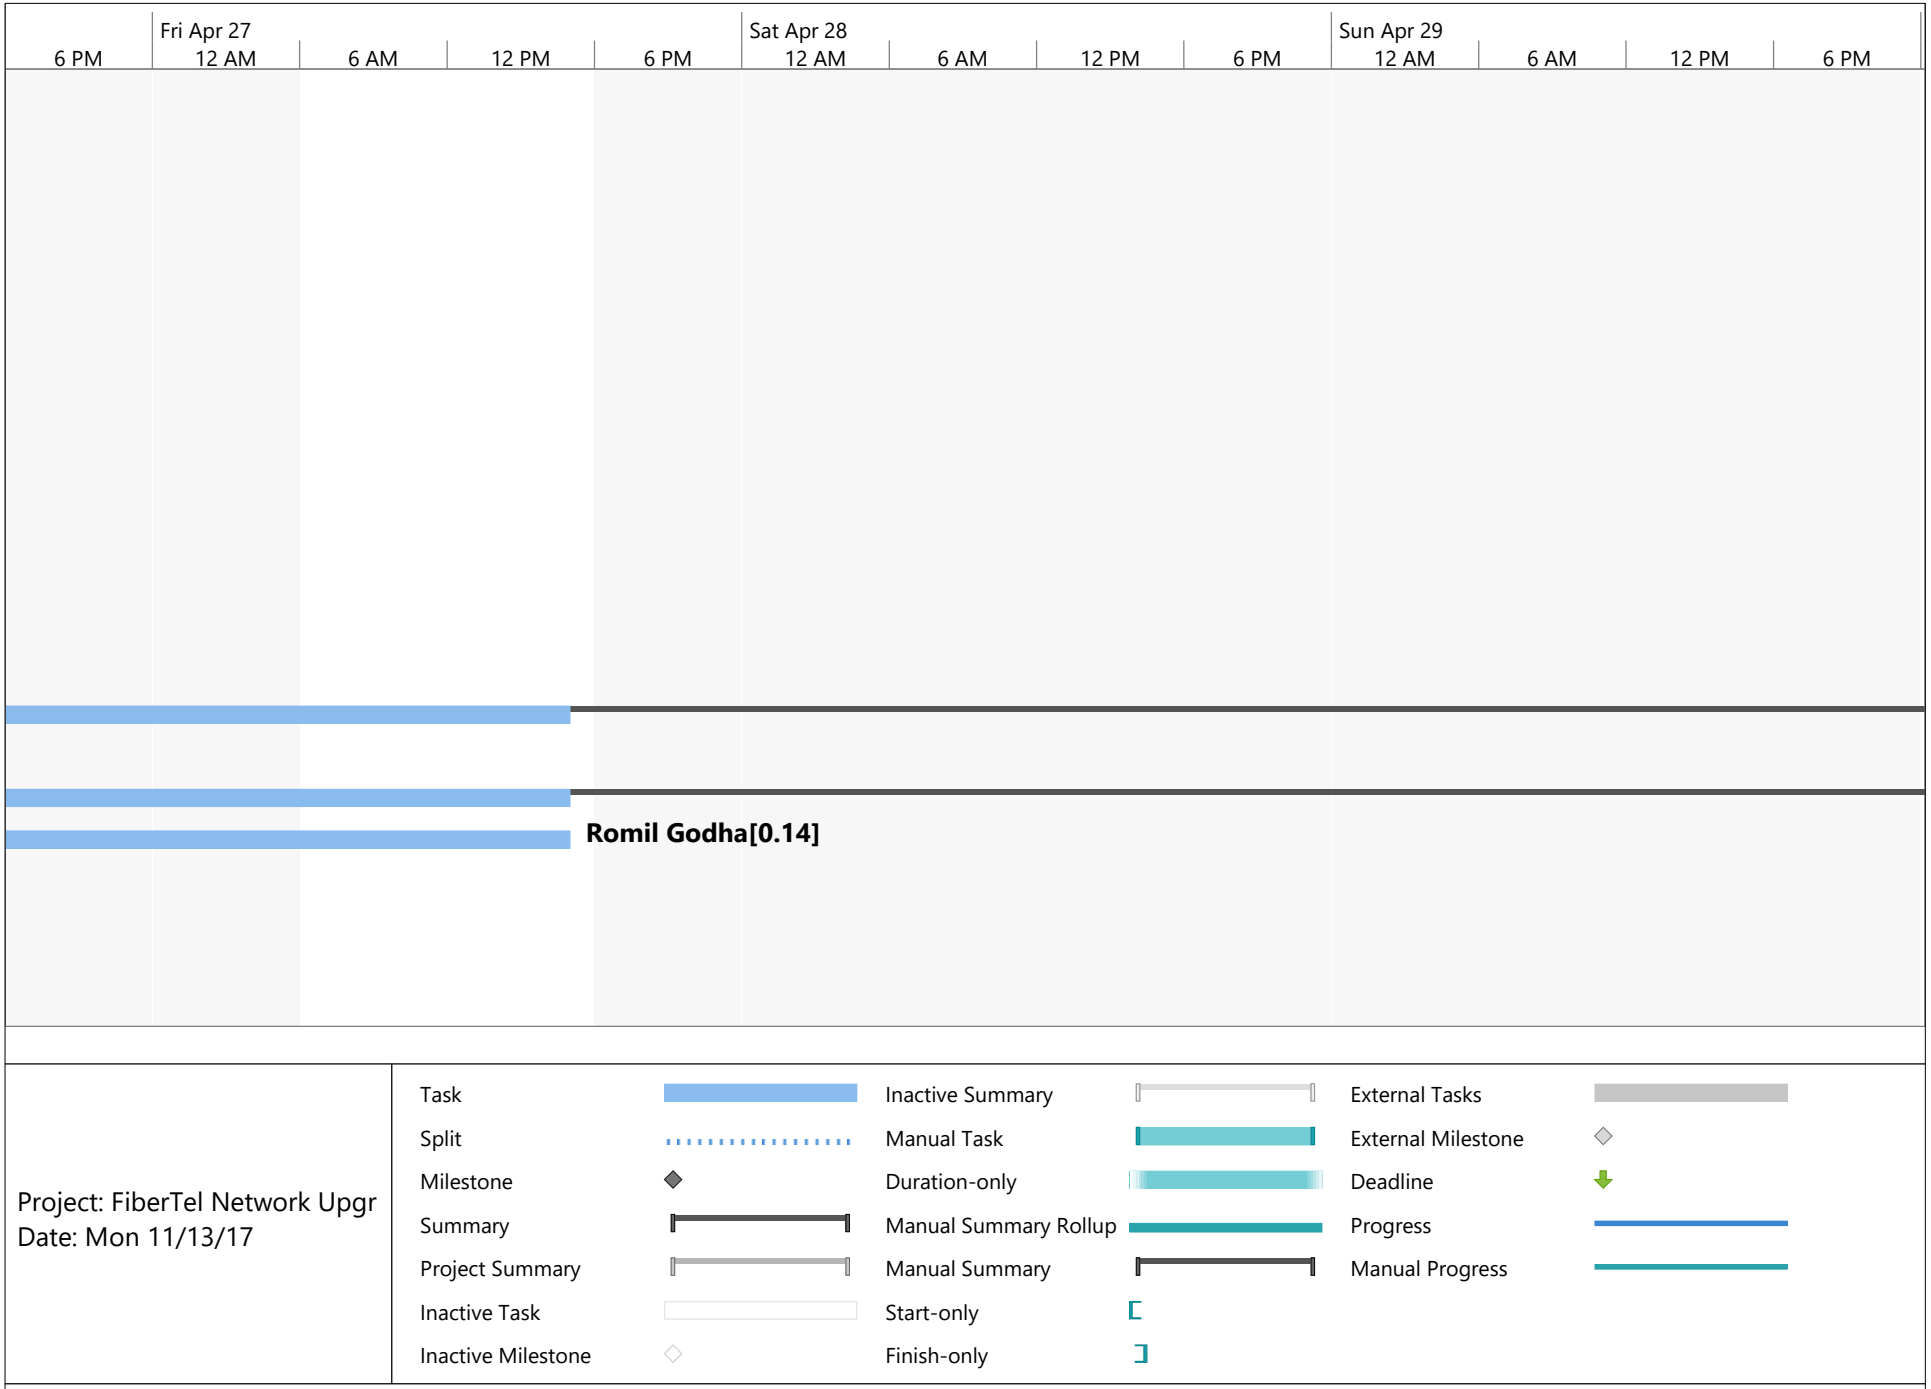

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

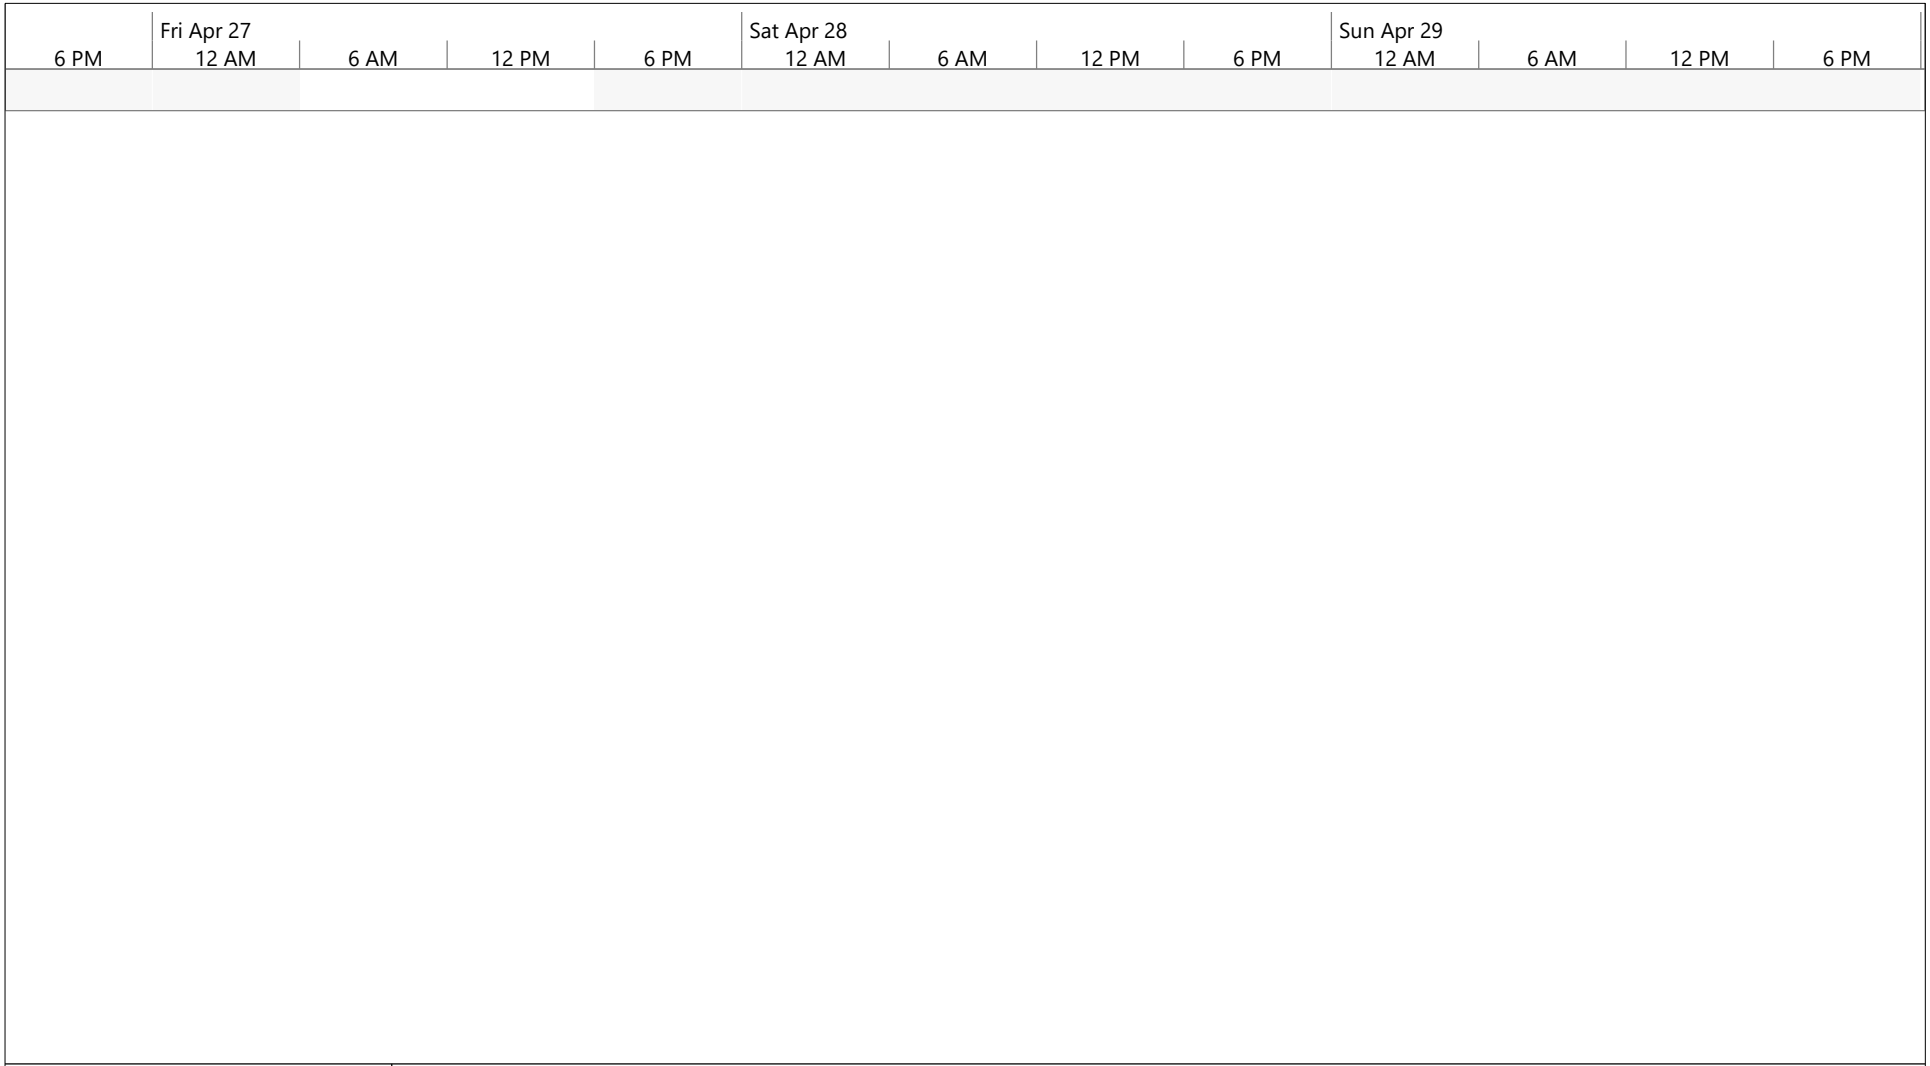

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

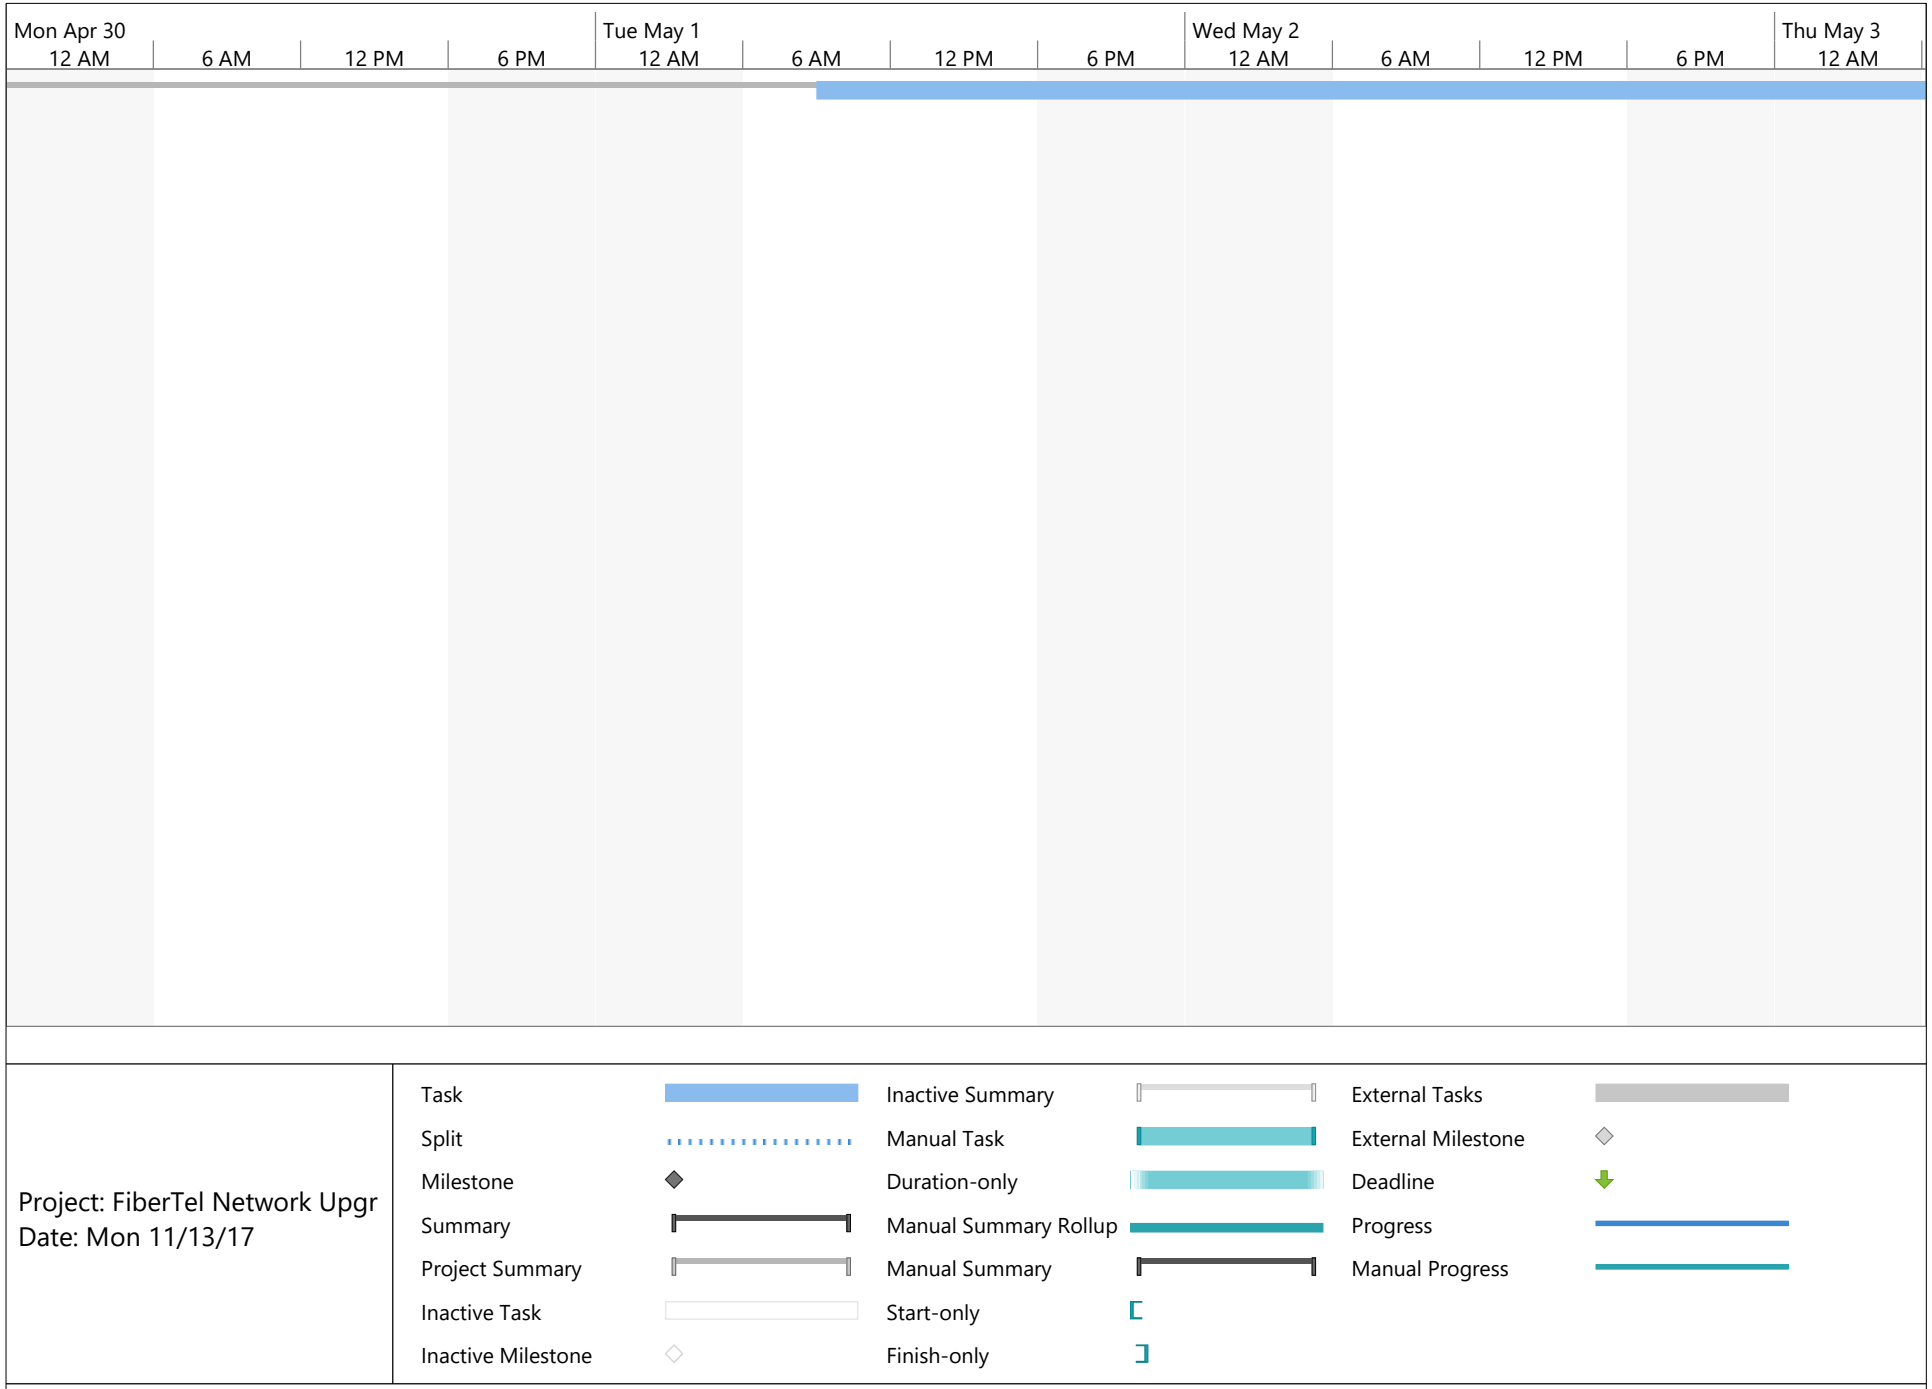

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

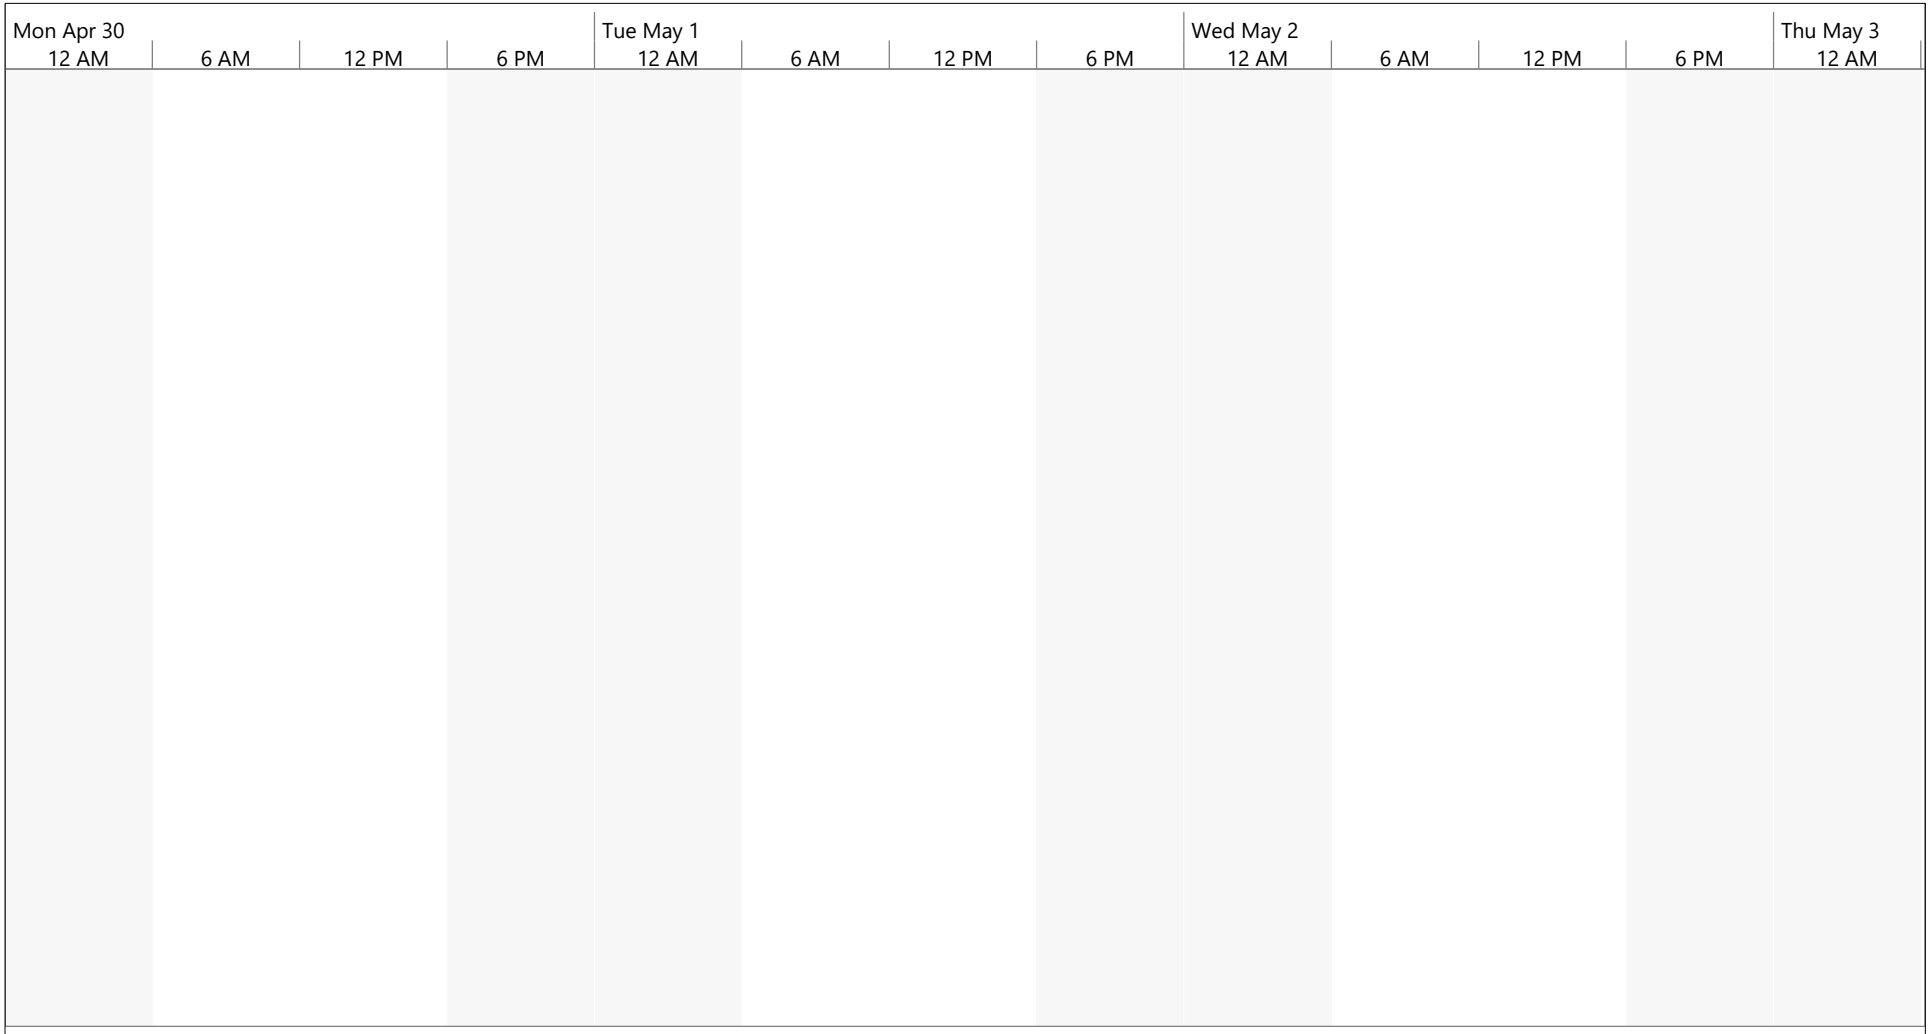

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

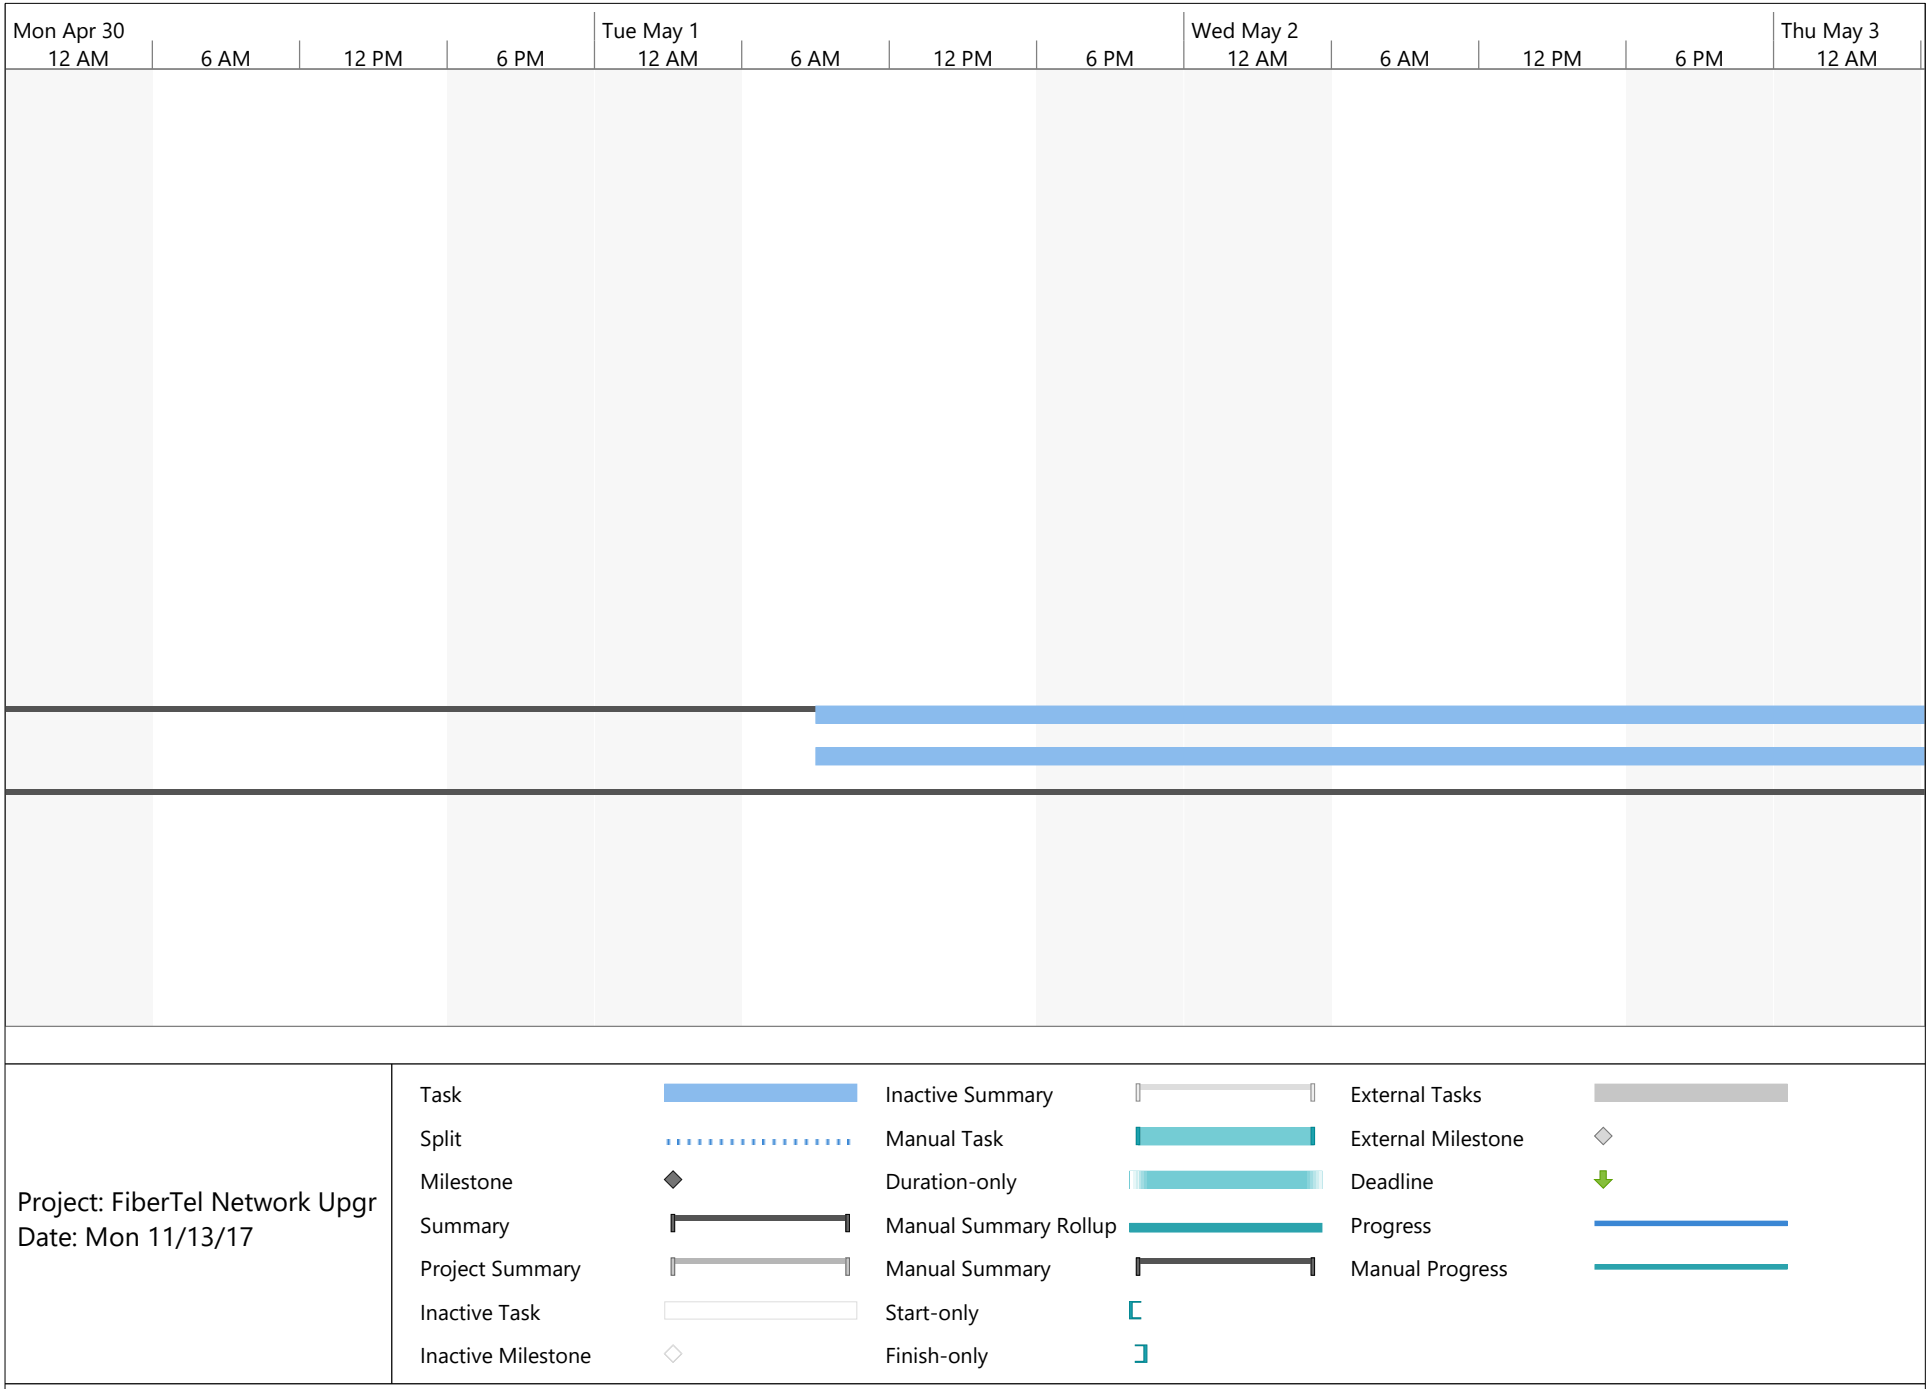

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

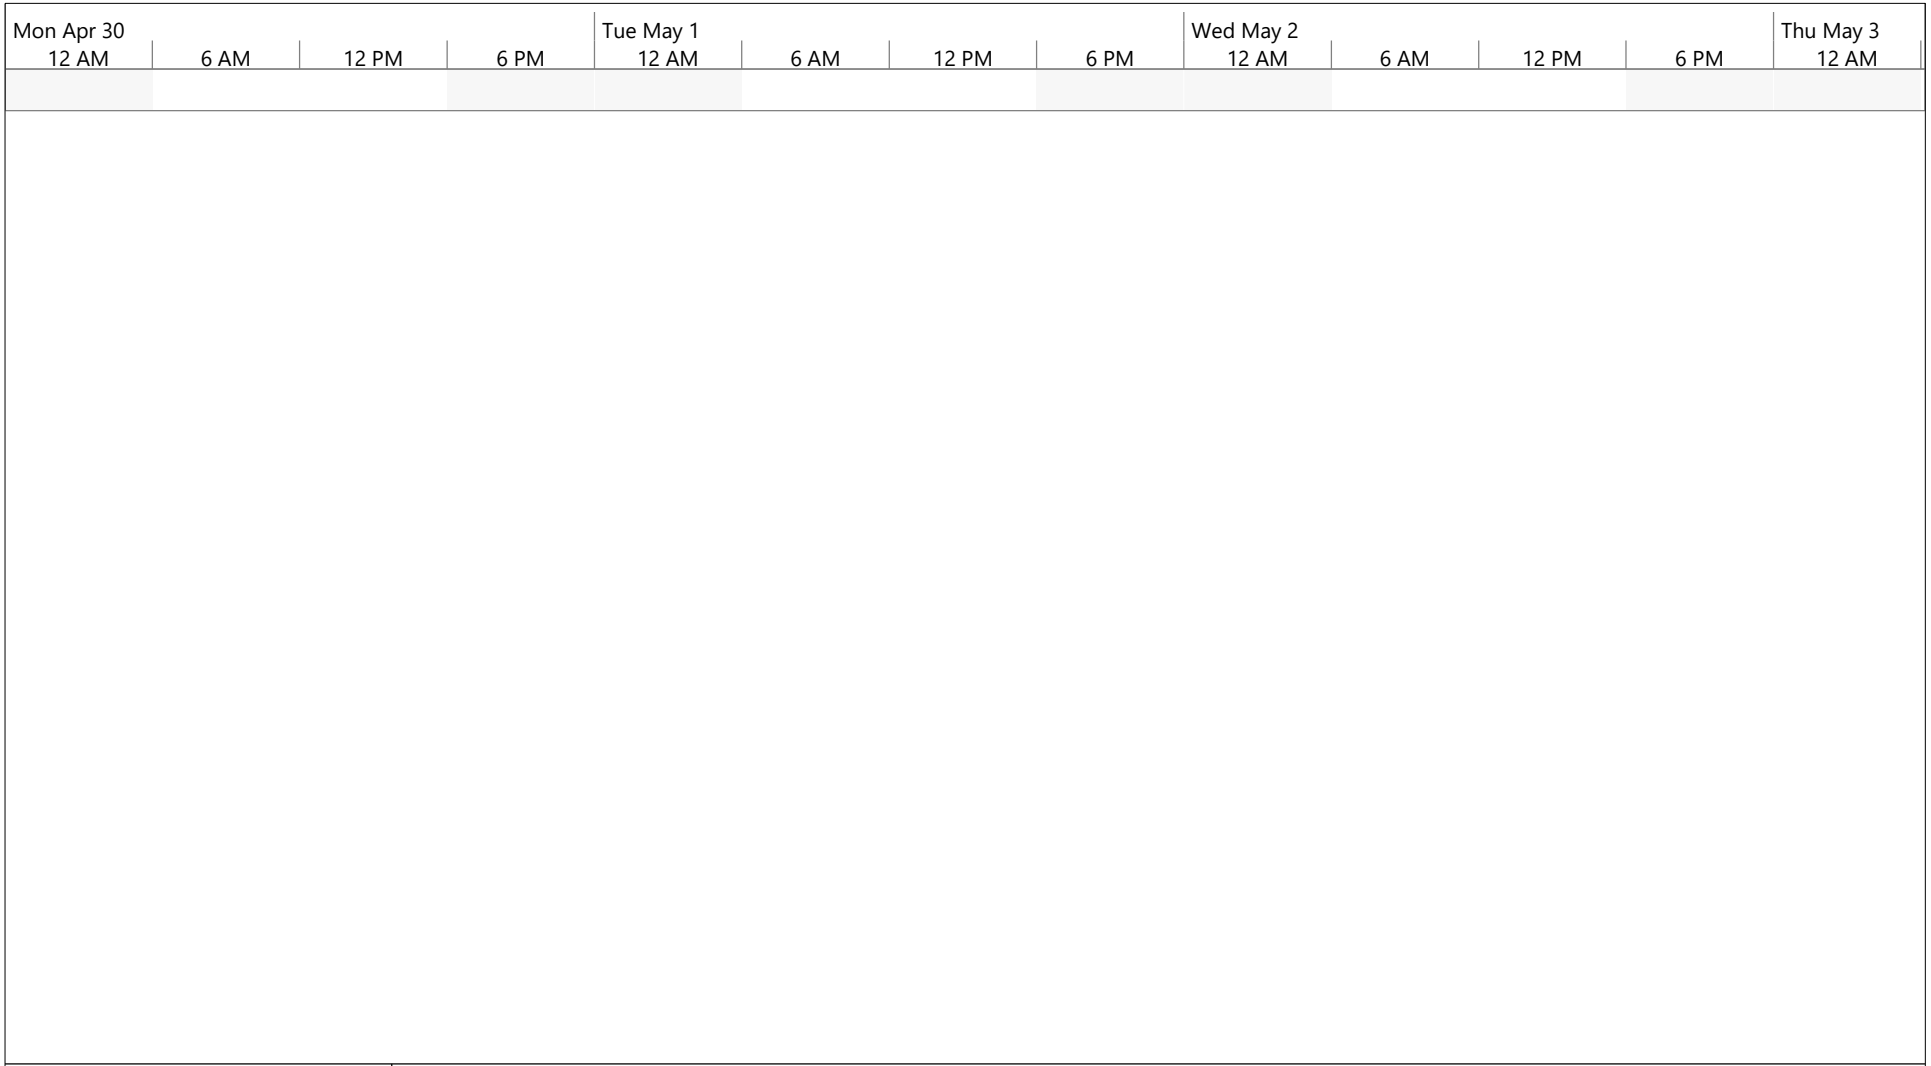

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

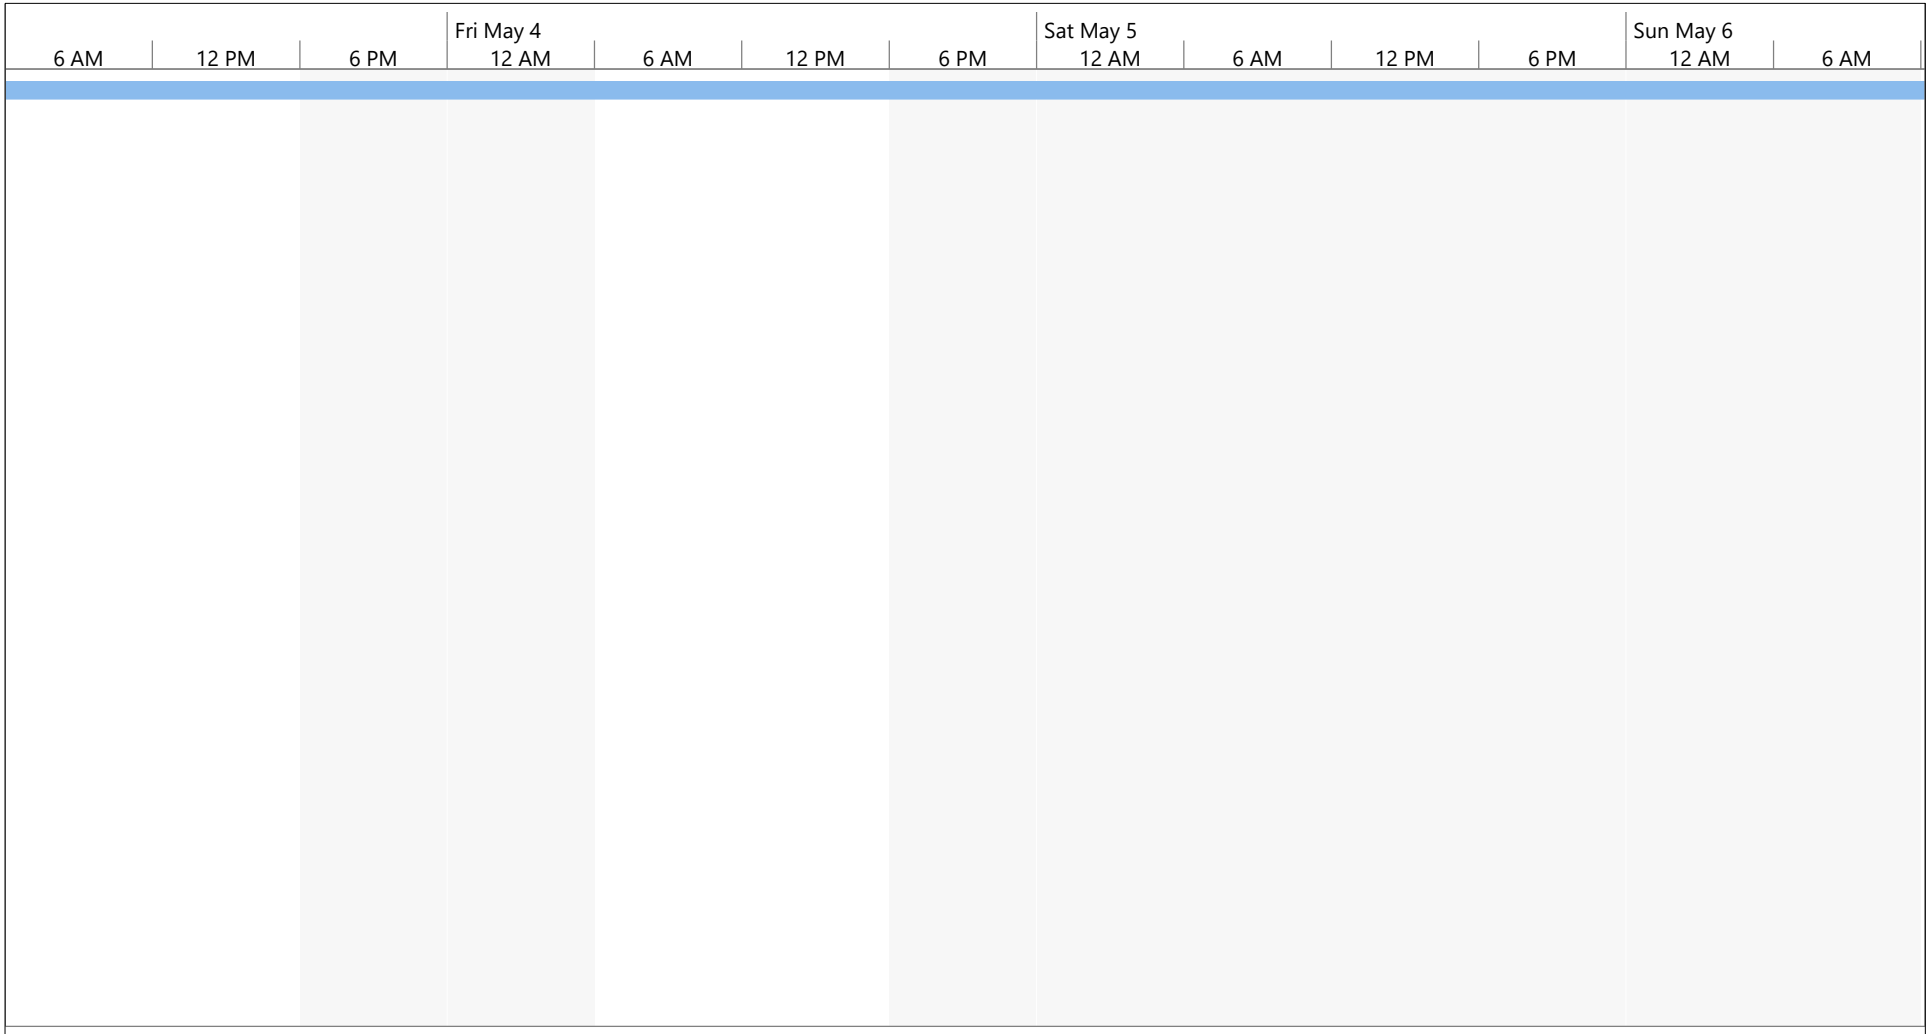

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

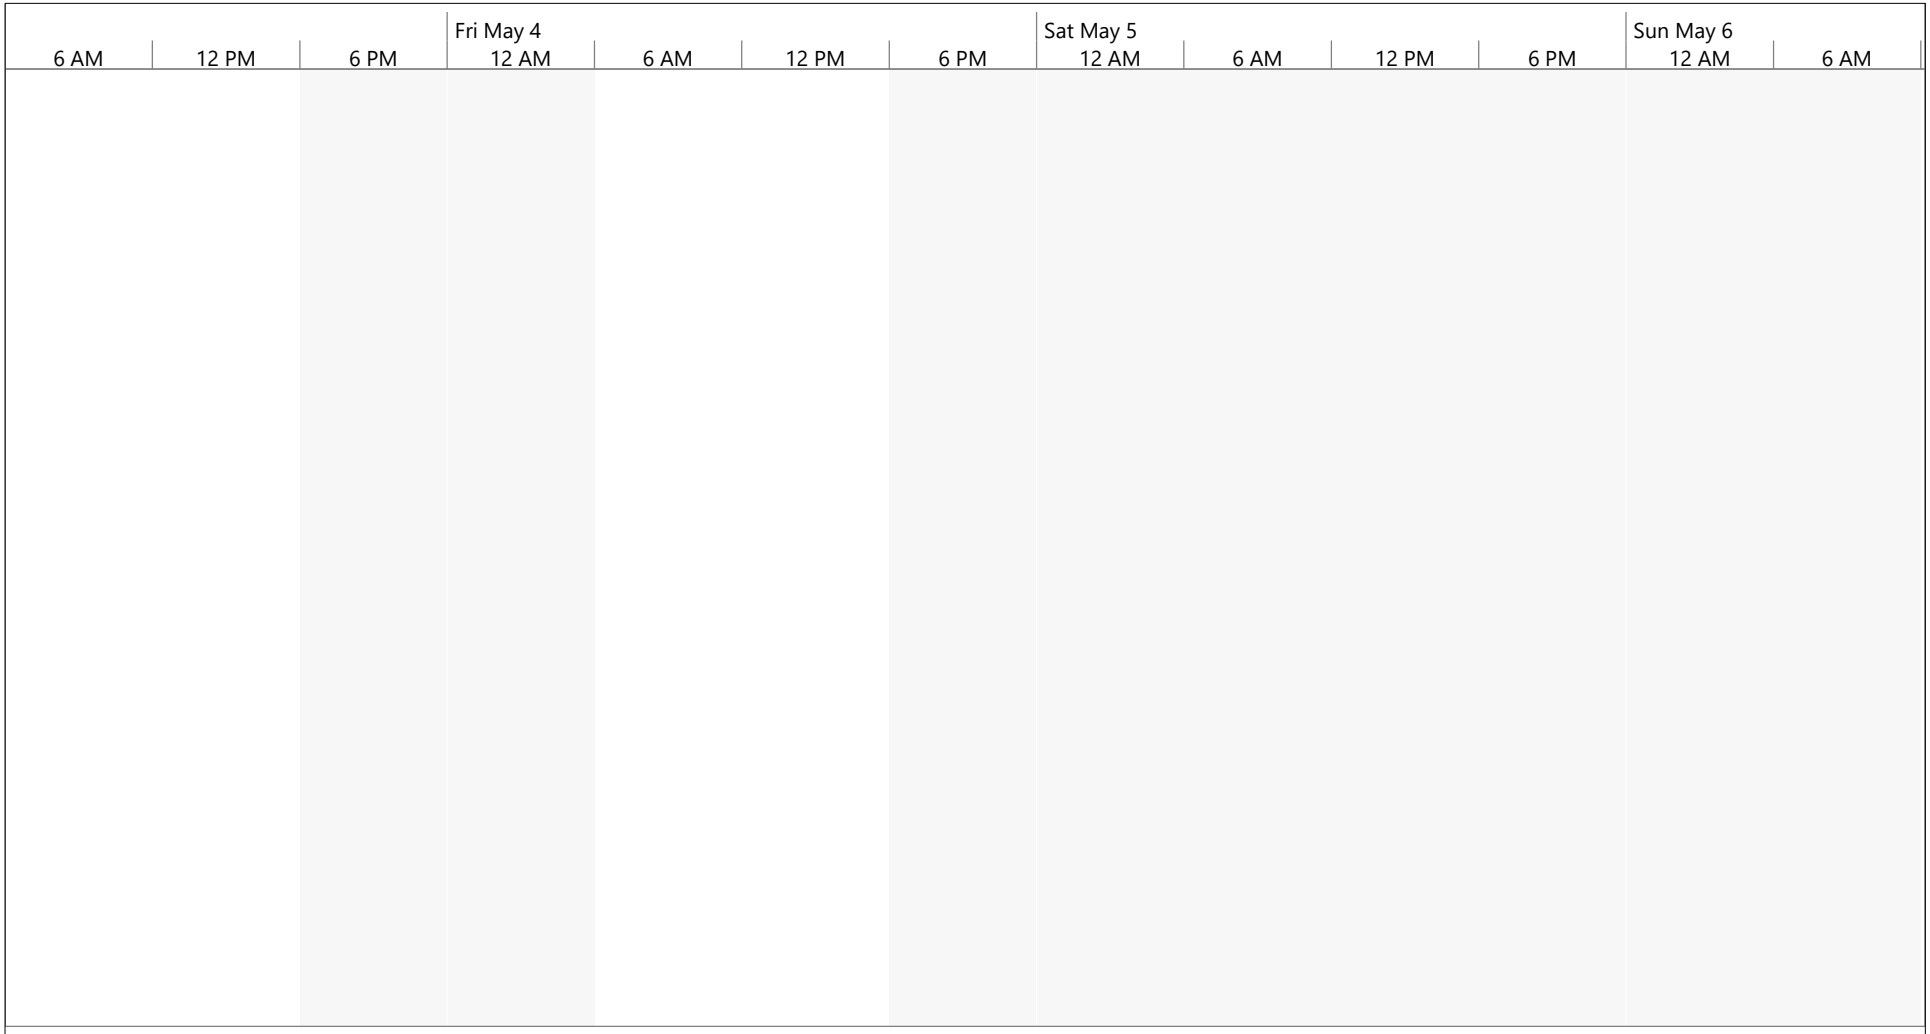

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

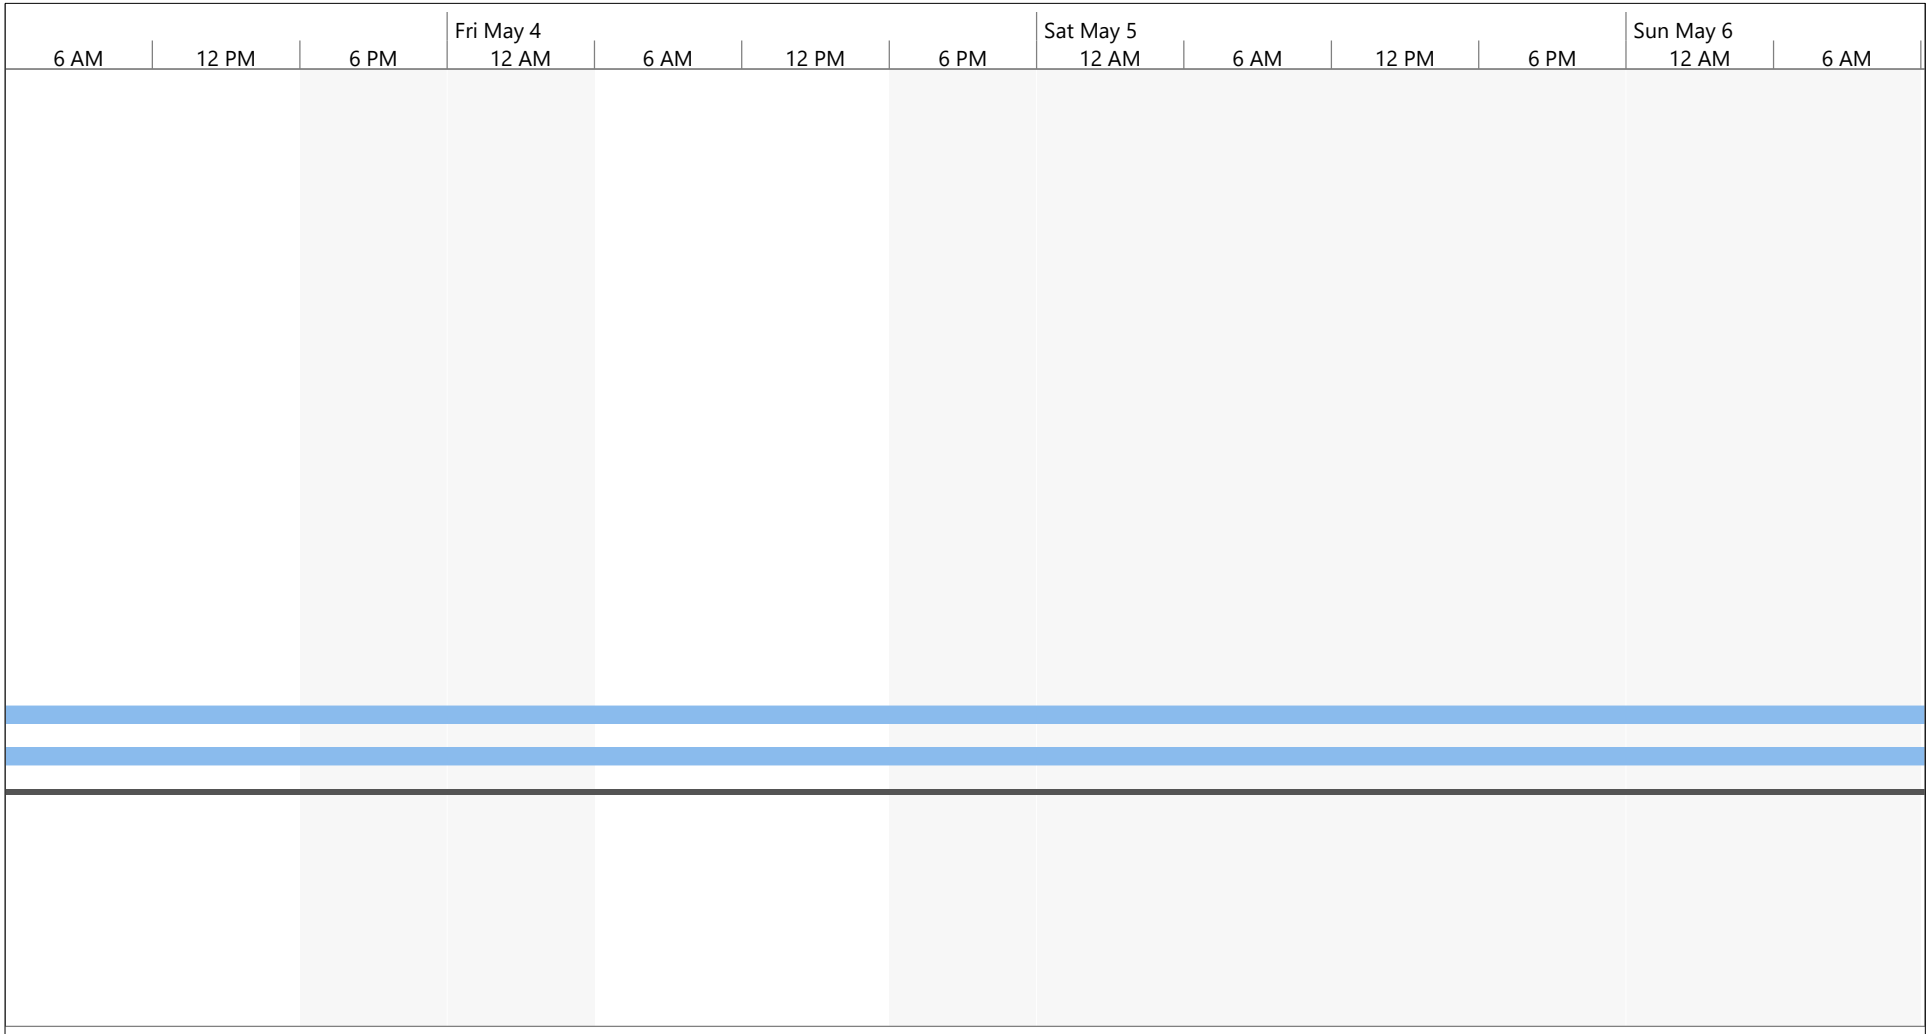

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	



Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

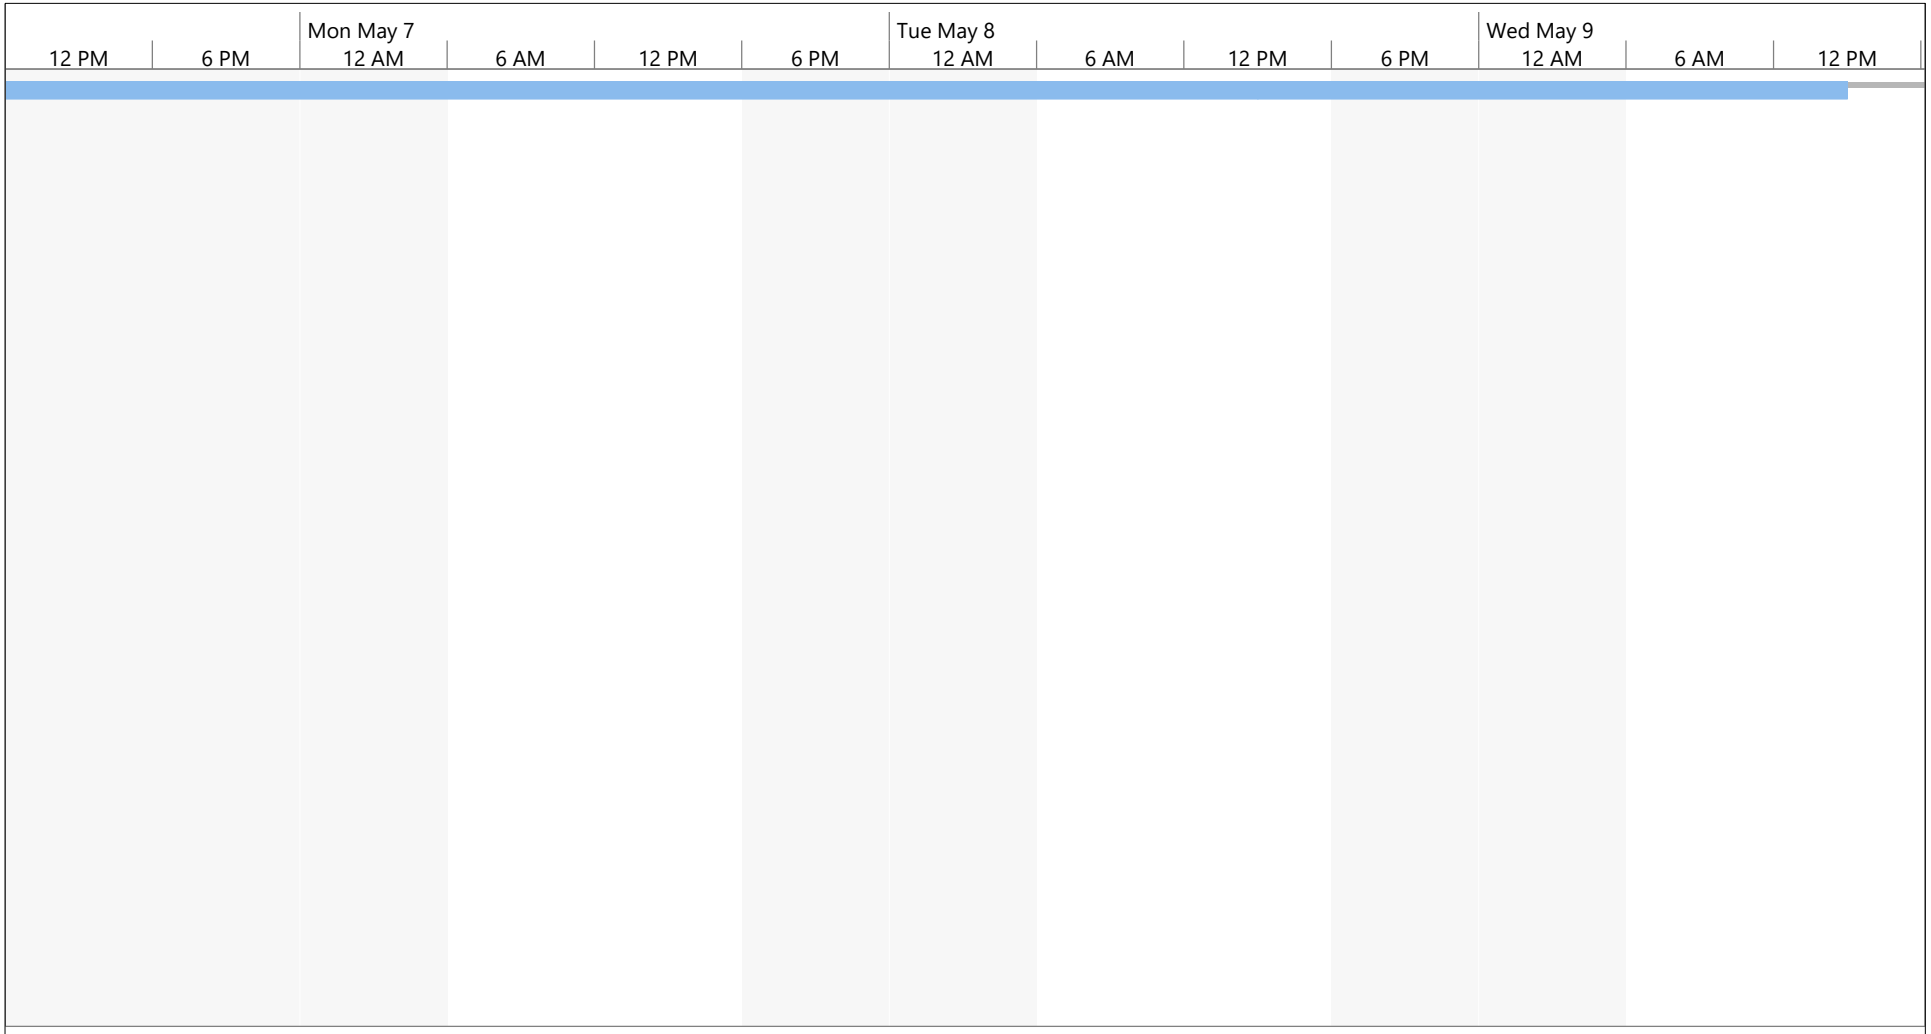

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

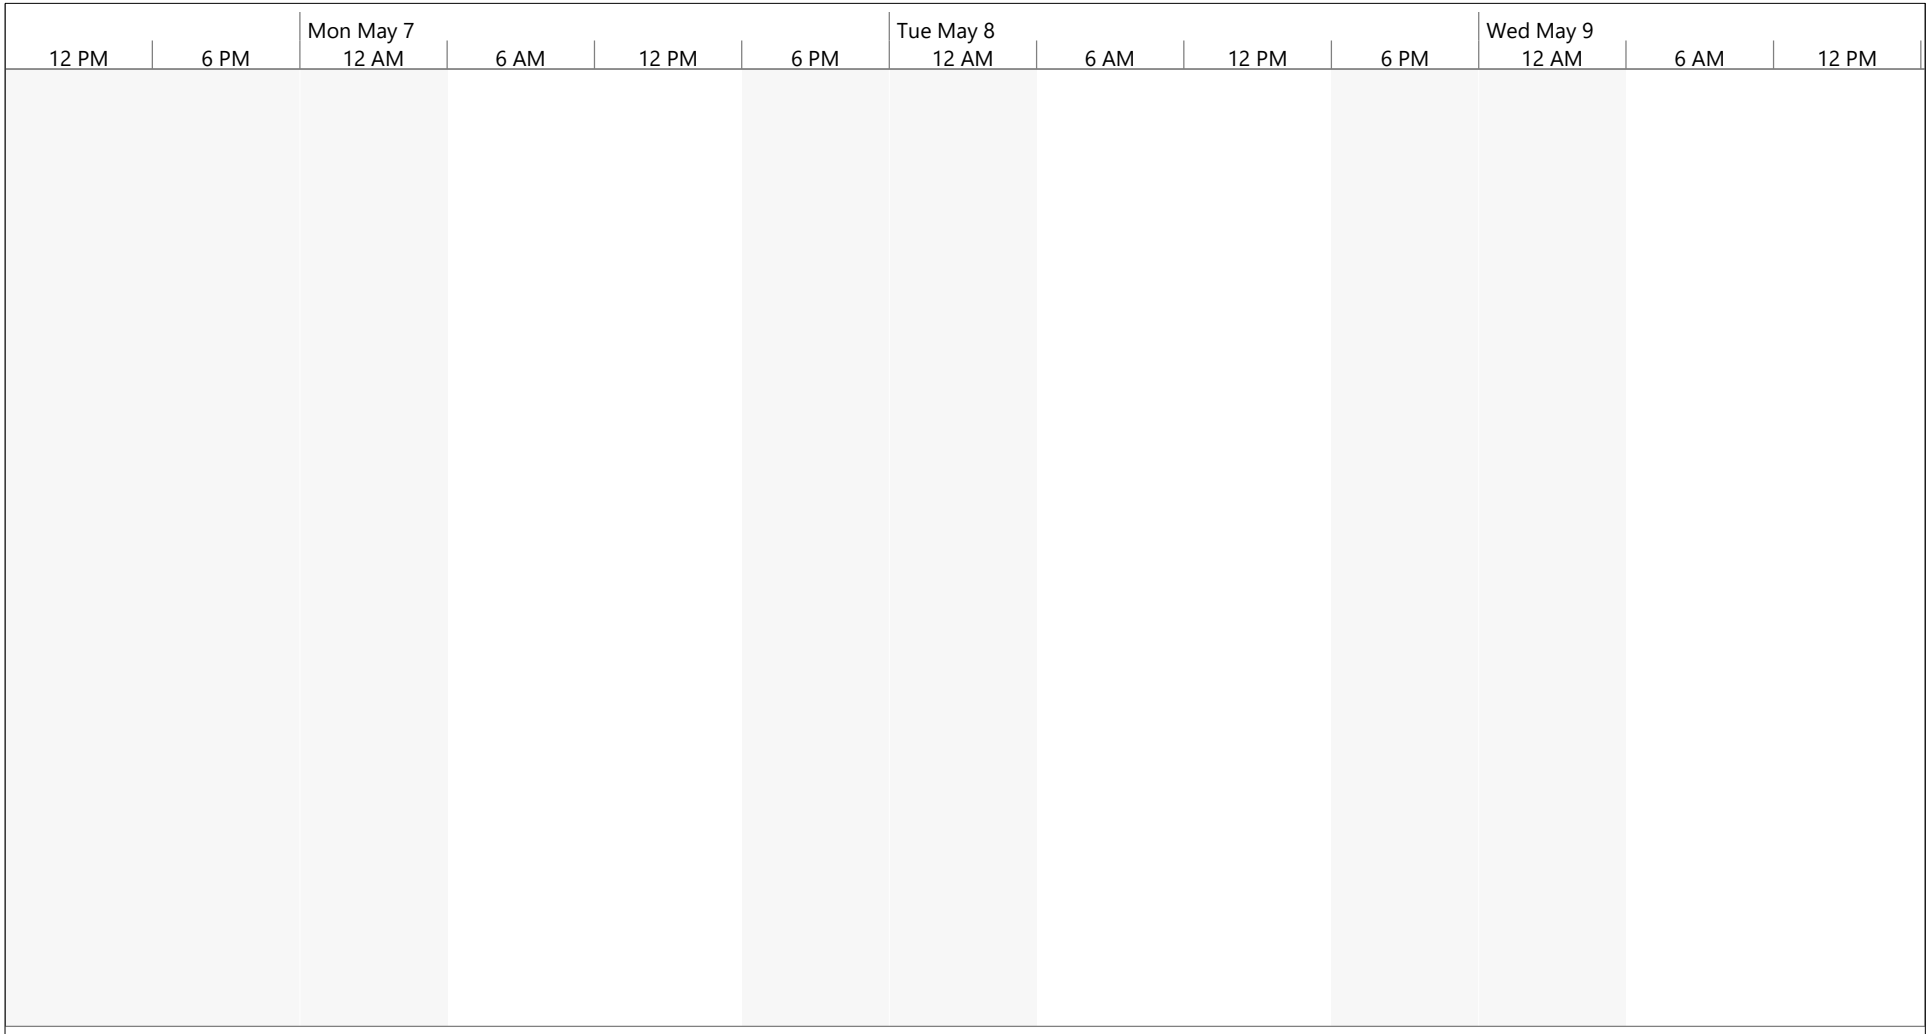

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

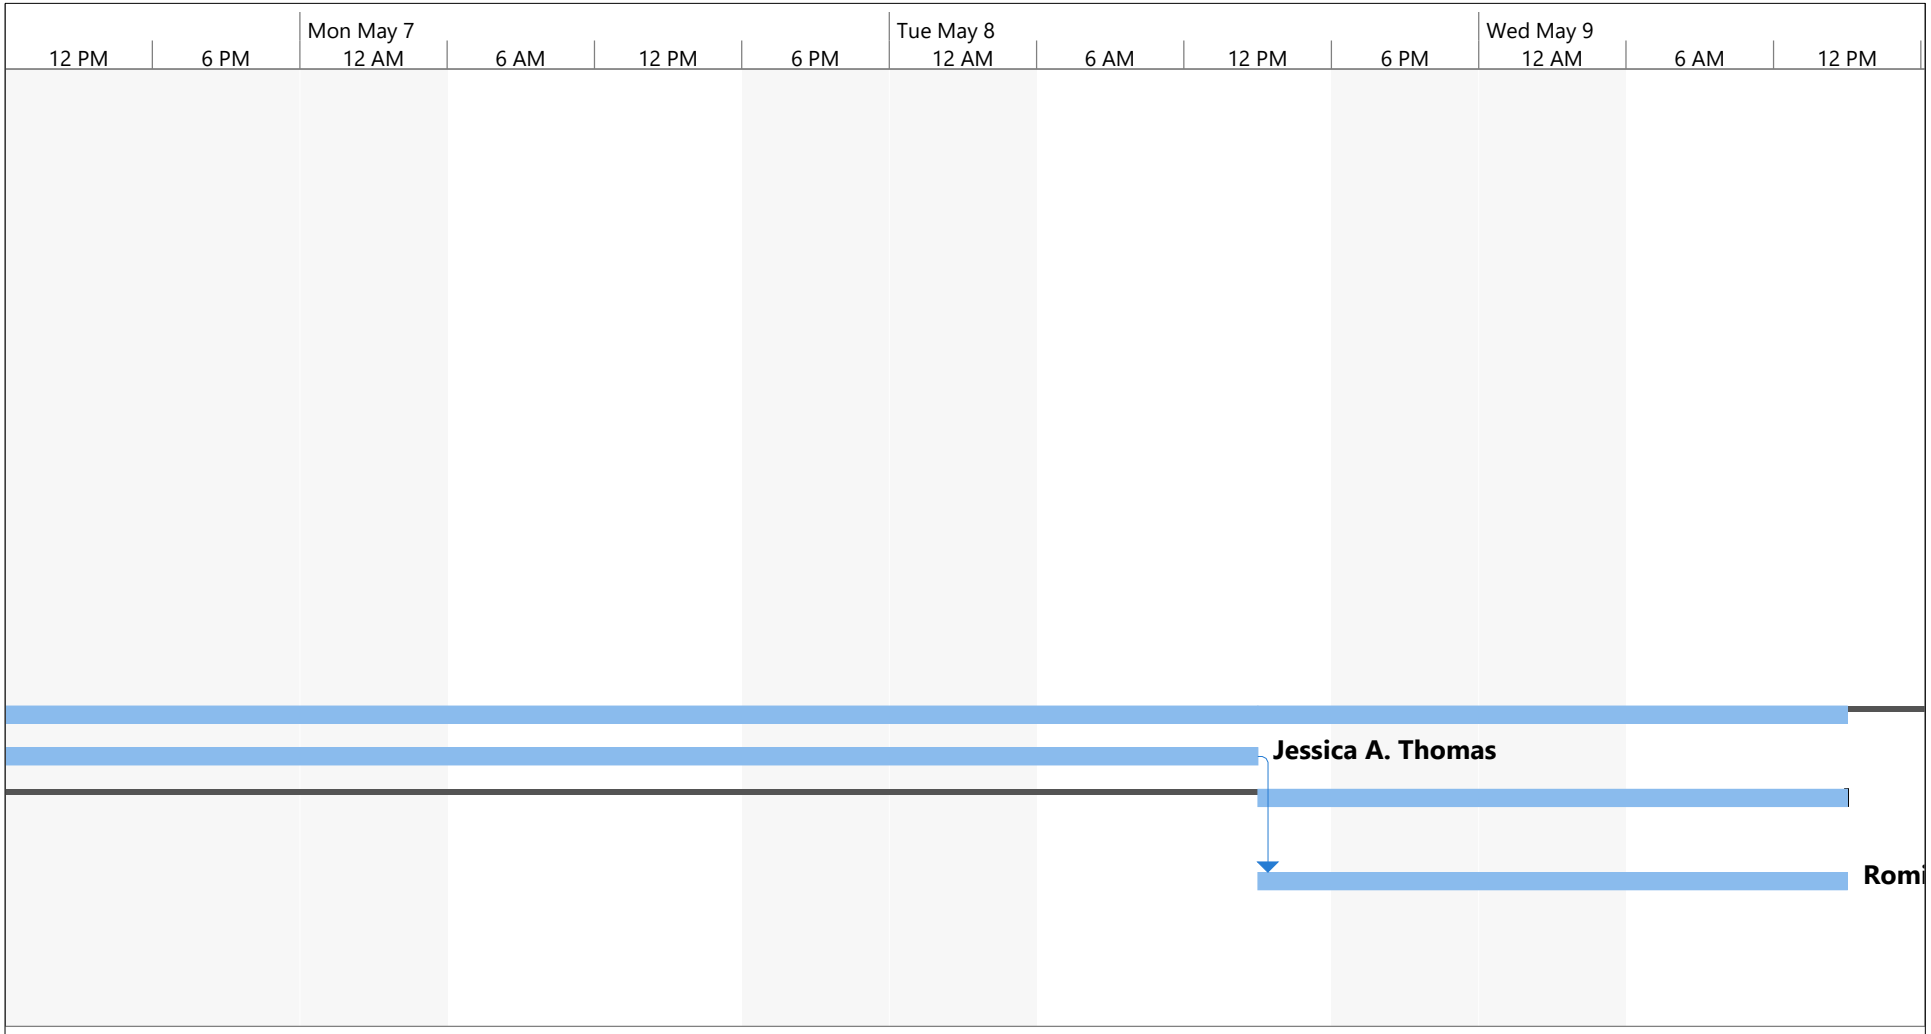

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

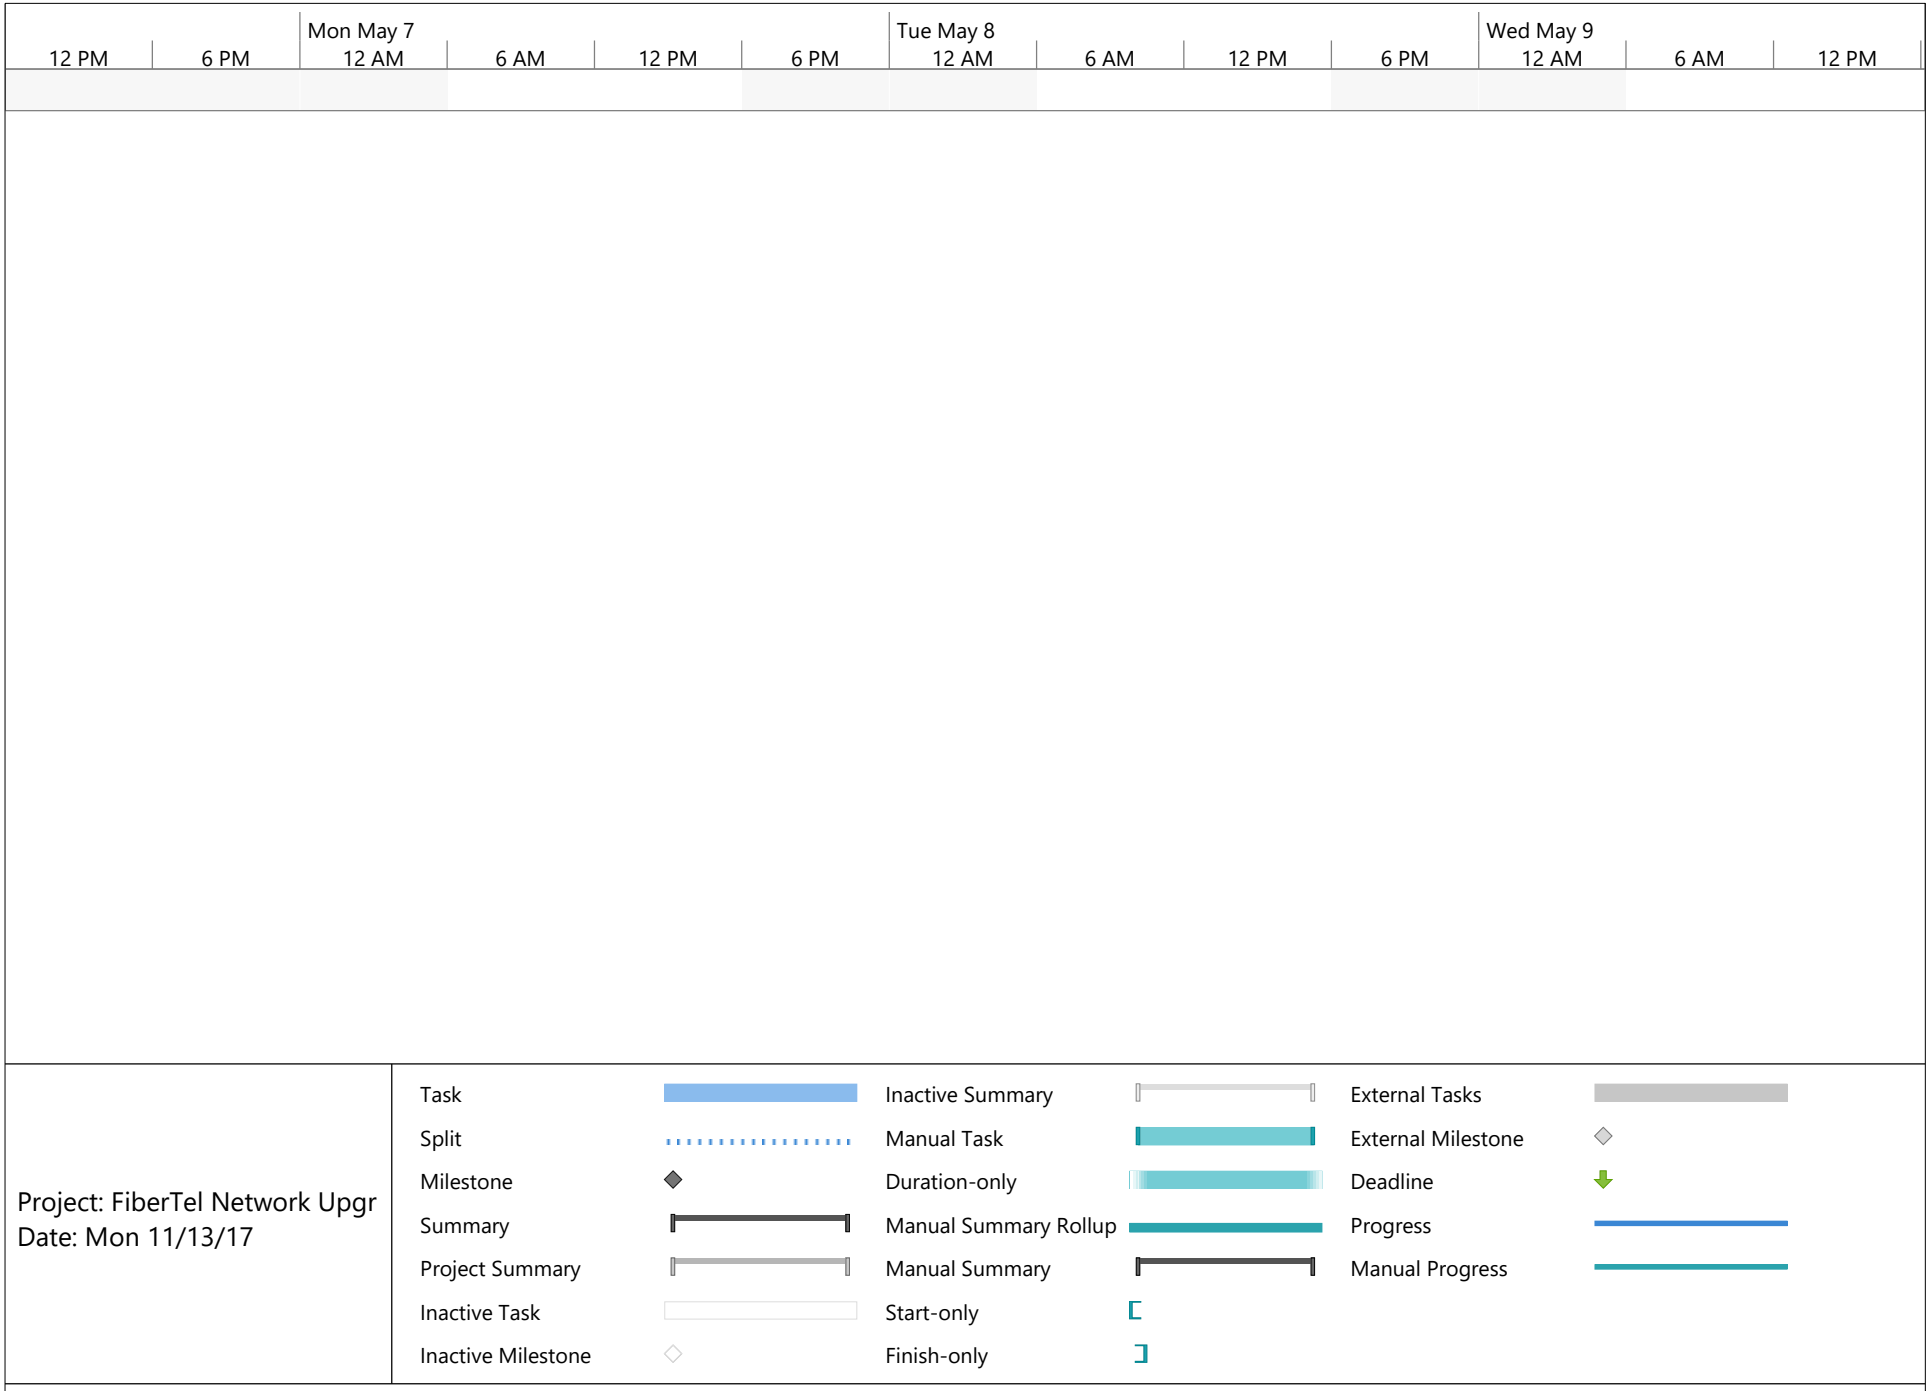
12 PM
6 PM
Mon May 7
12 AM
6 AM
12 PM
6 PM
Tue May 8
12 AM
6 AM
12 PM
6 PM
Wed May 9
12 AM
6 AM
12 PM
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

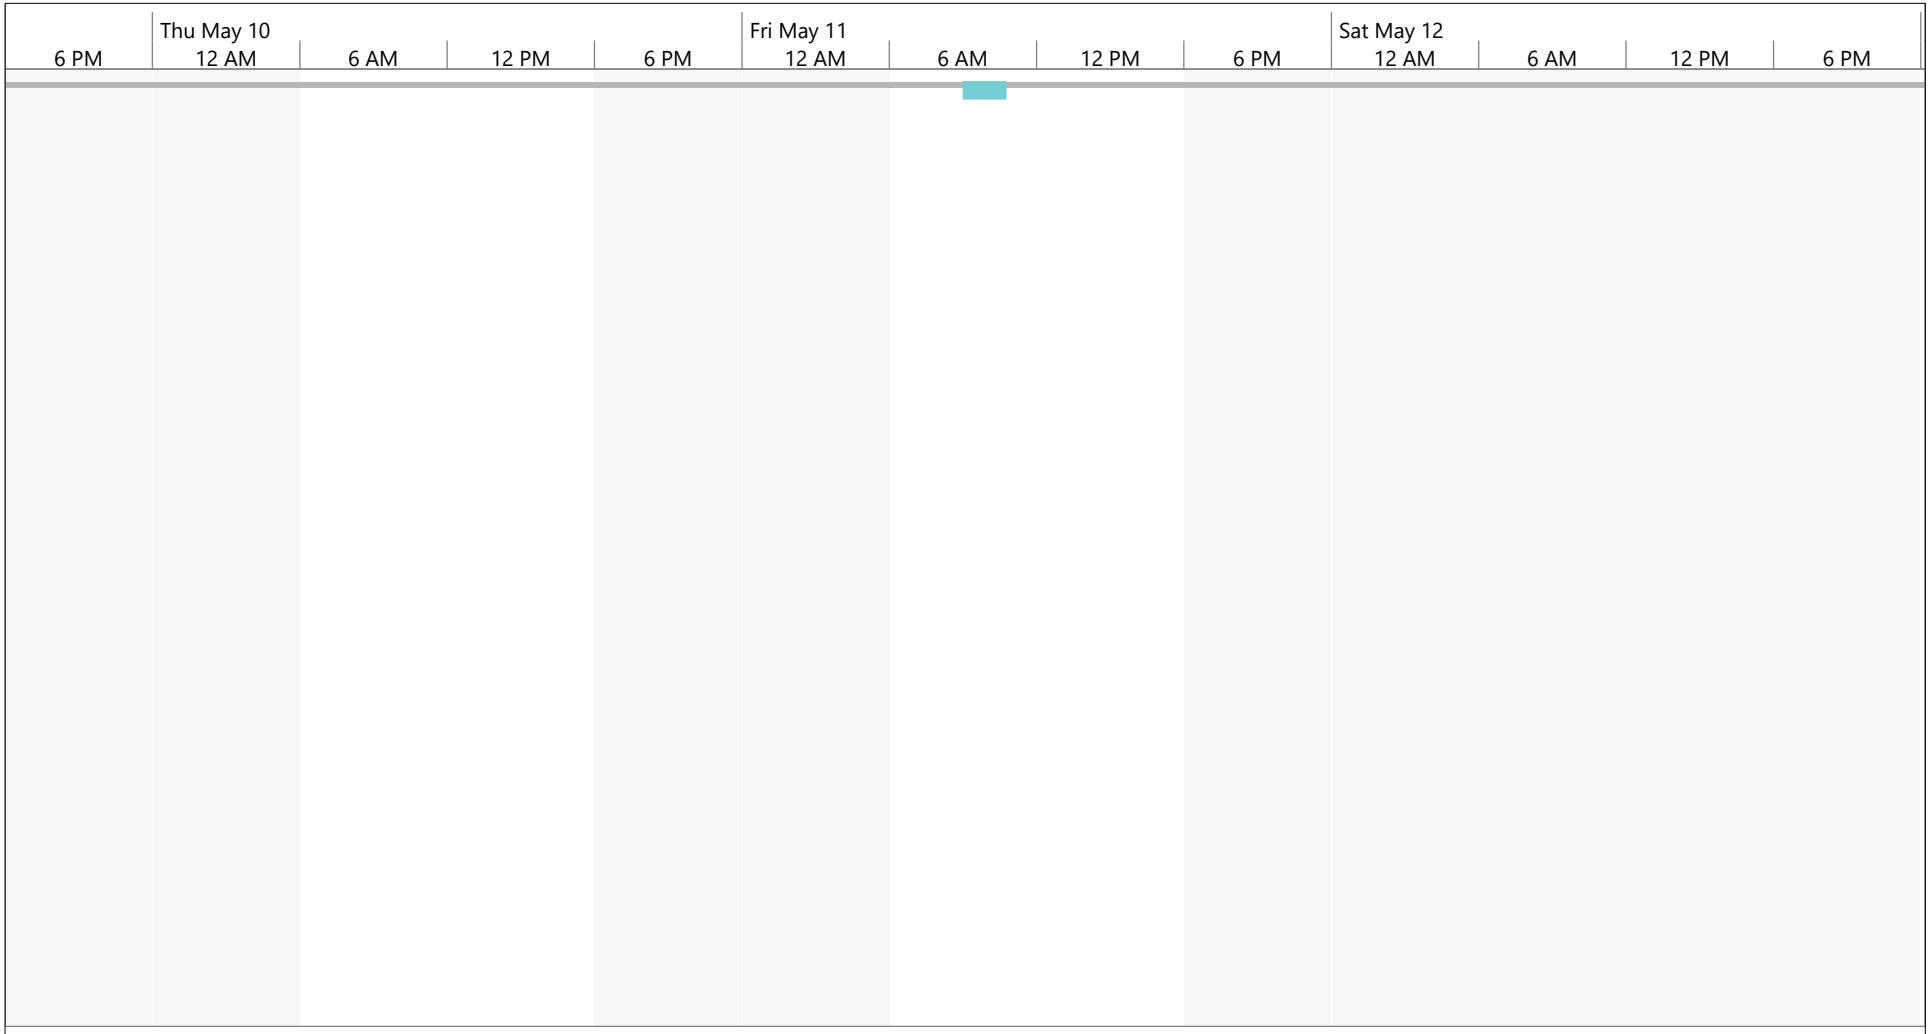

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

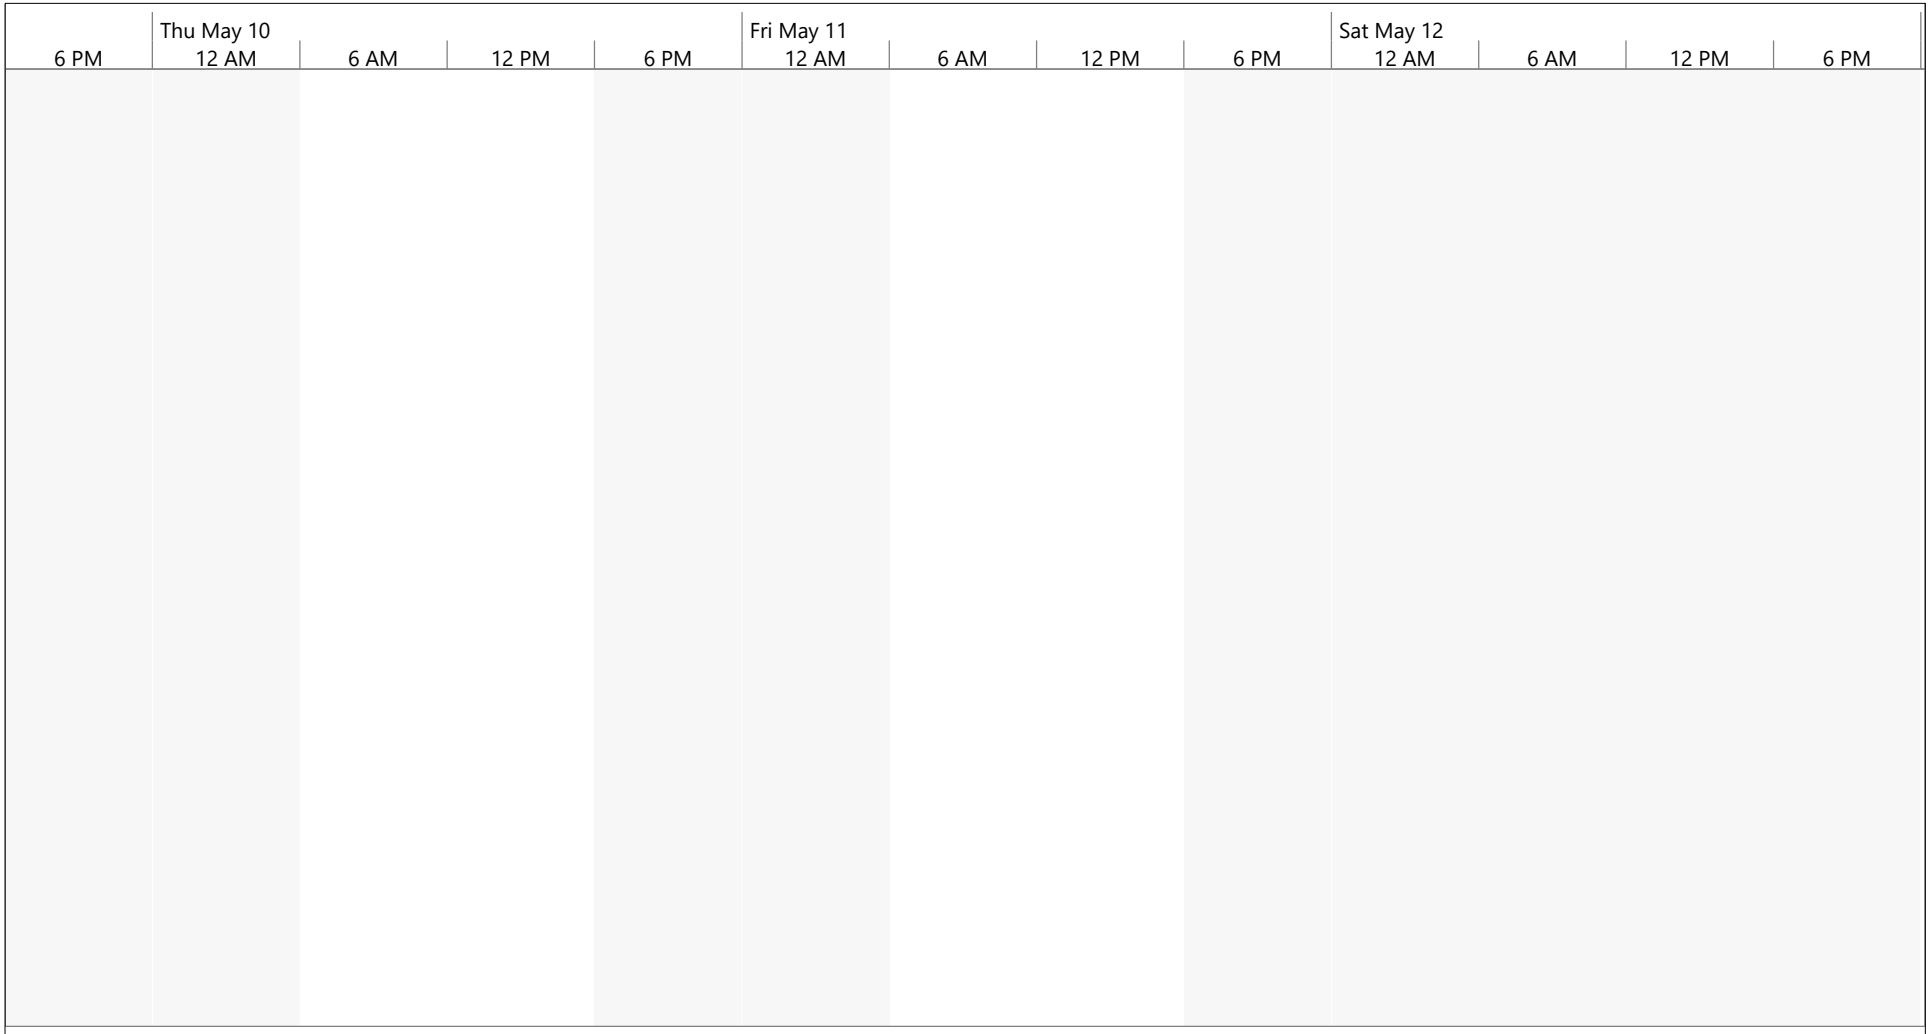

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

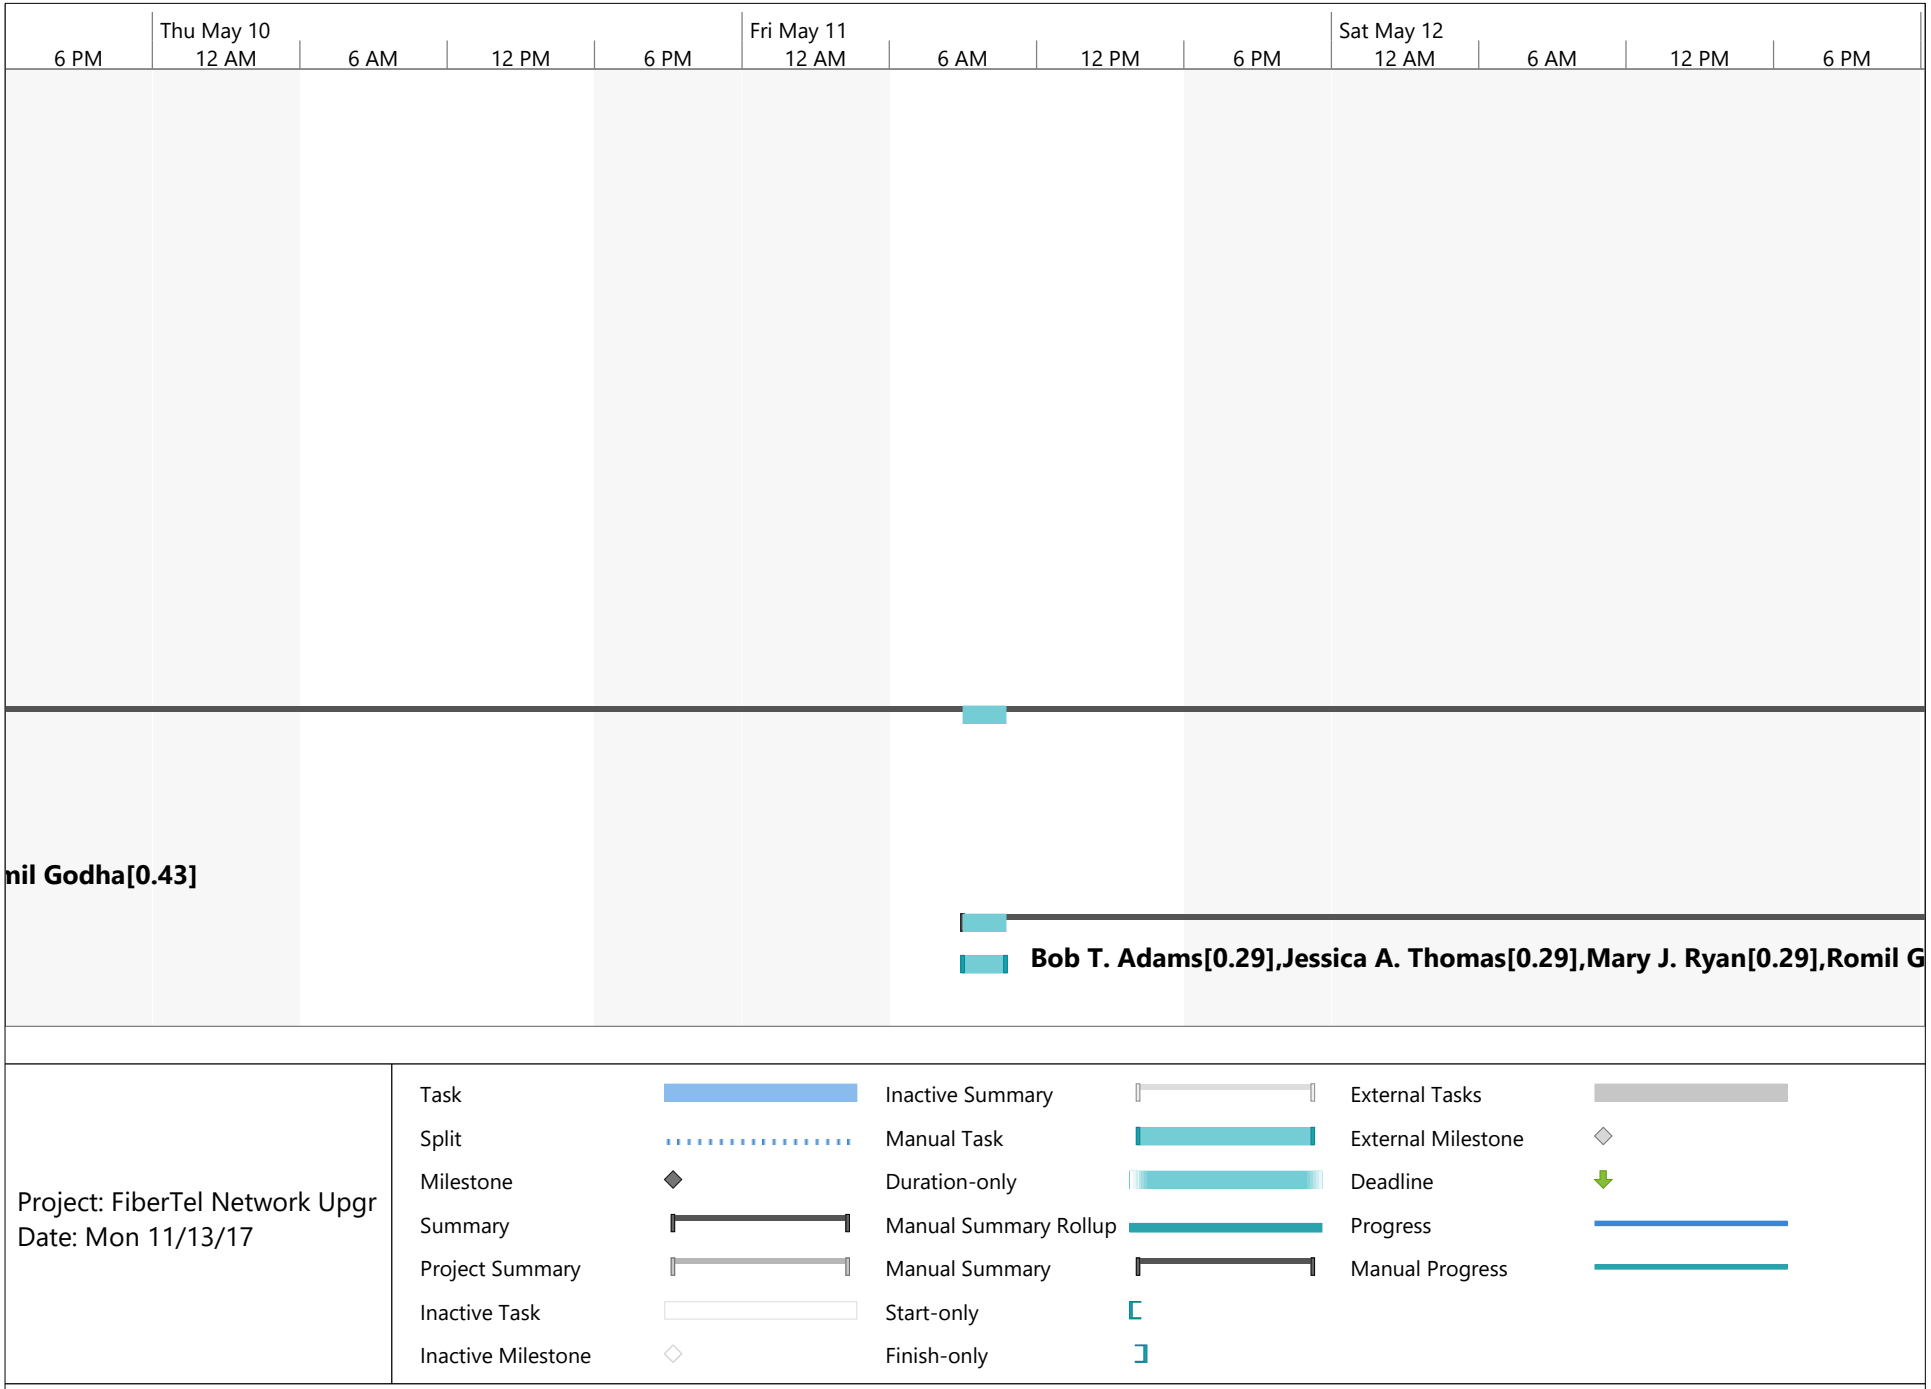
6 PM
Thu May 10
12 AM
6 AM
12 PM
6 PM
Fri May 11
12 AM
6 AM
12 PM
6 PM
Sat May 12
12 AM
6 AM
12 PM
6 PM
nil Godha[0.43]
Bob T. Adams[0.29],Jessica A. Thomas[0.29],Mary J. Ryan[0.29],Romil G
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

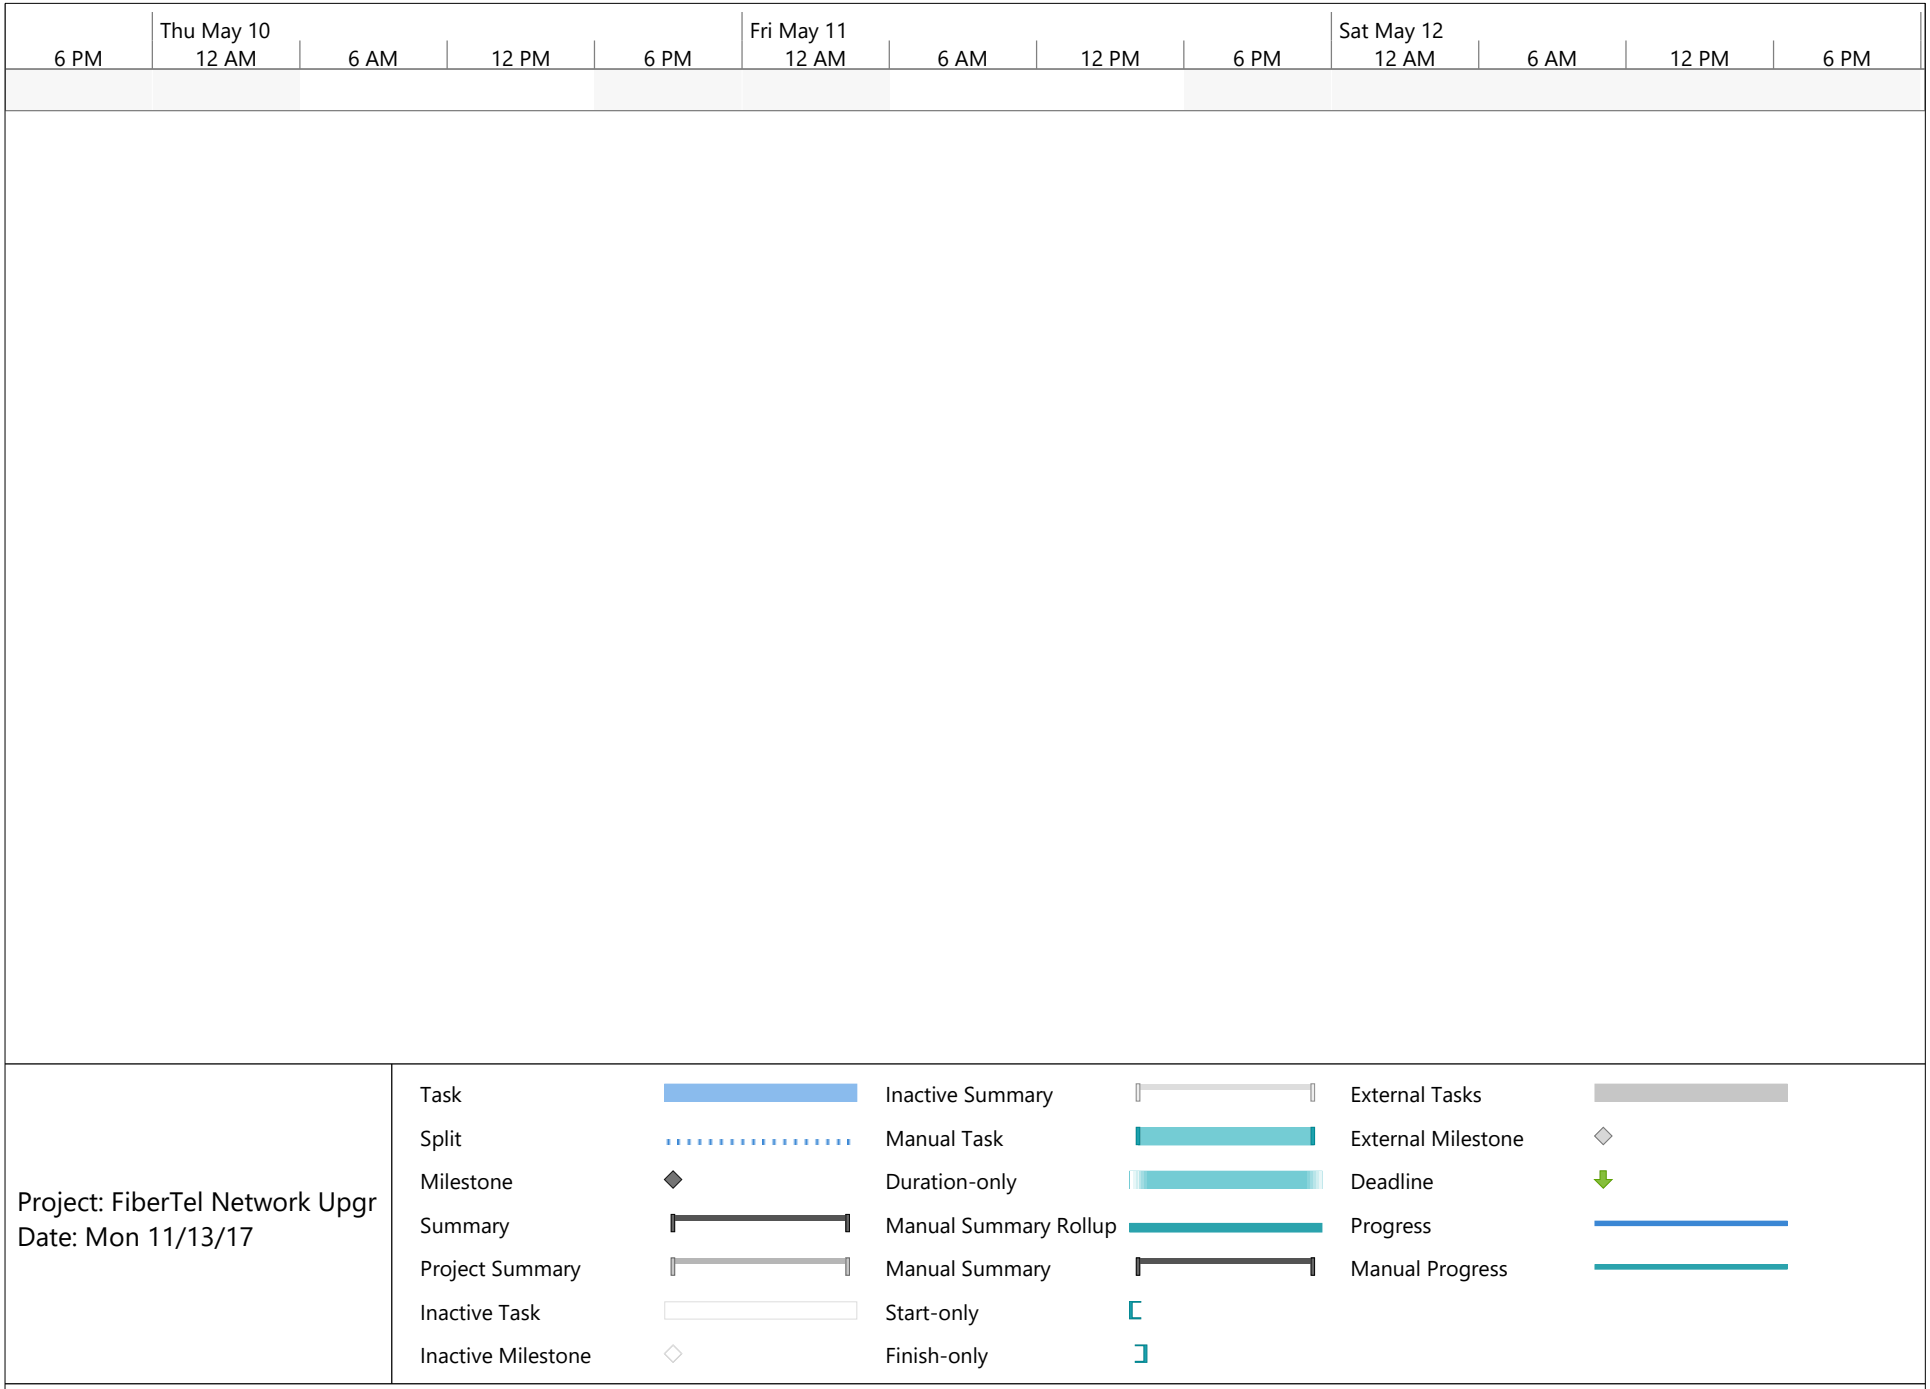
6 PM
Thu May 10
12 AM
6 AM
12 PM
6 PM
Fri May 11
12 AM
6 AM
12 PM
6 PM
Sat May 12
12 AM
6 AM
12 PM
6 PM
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

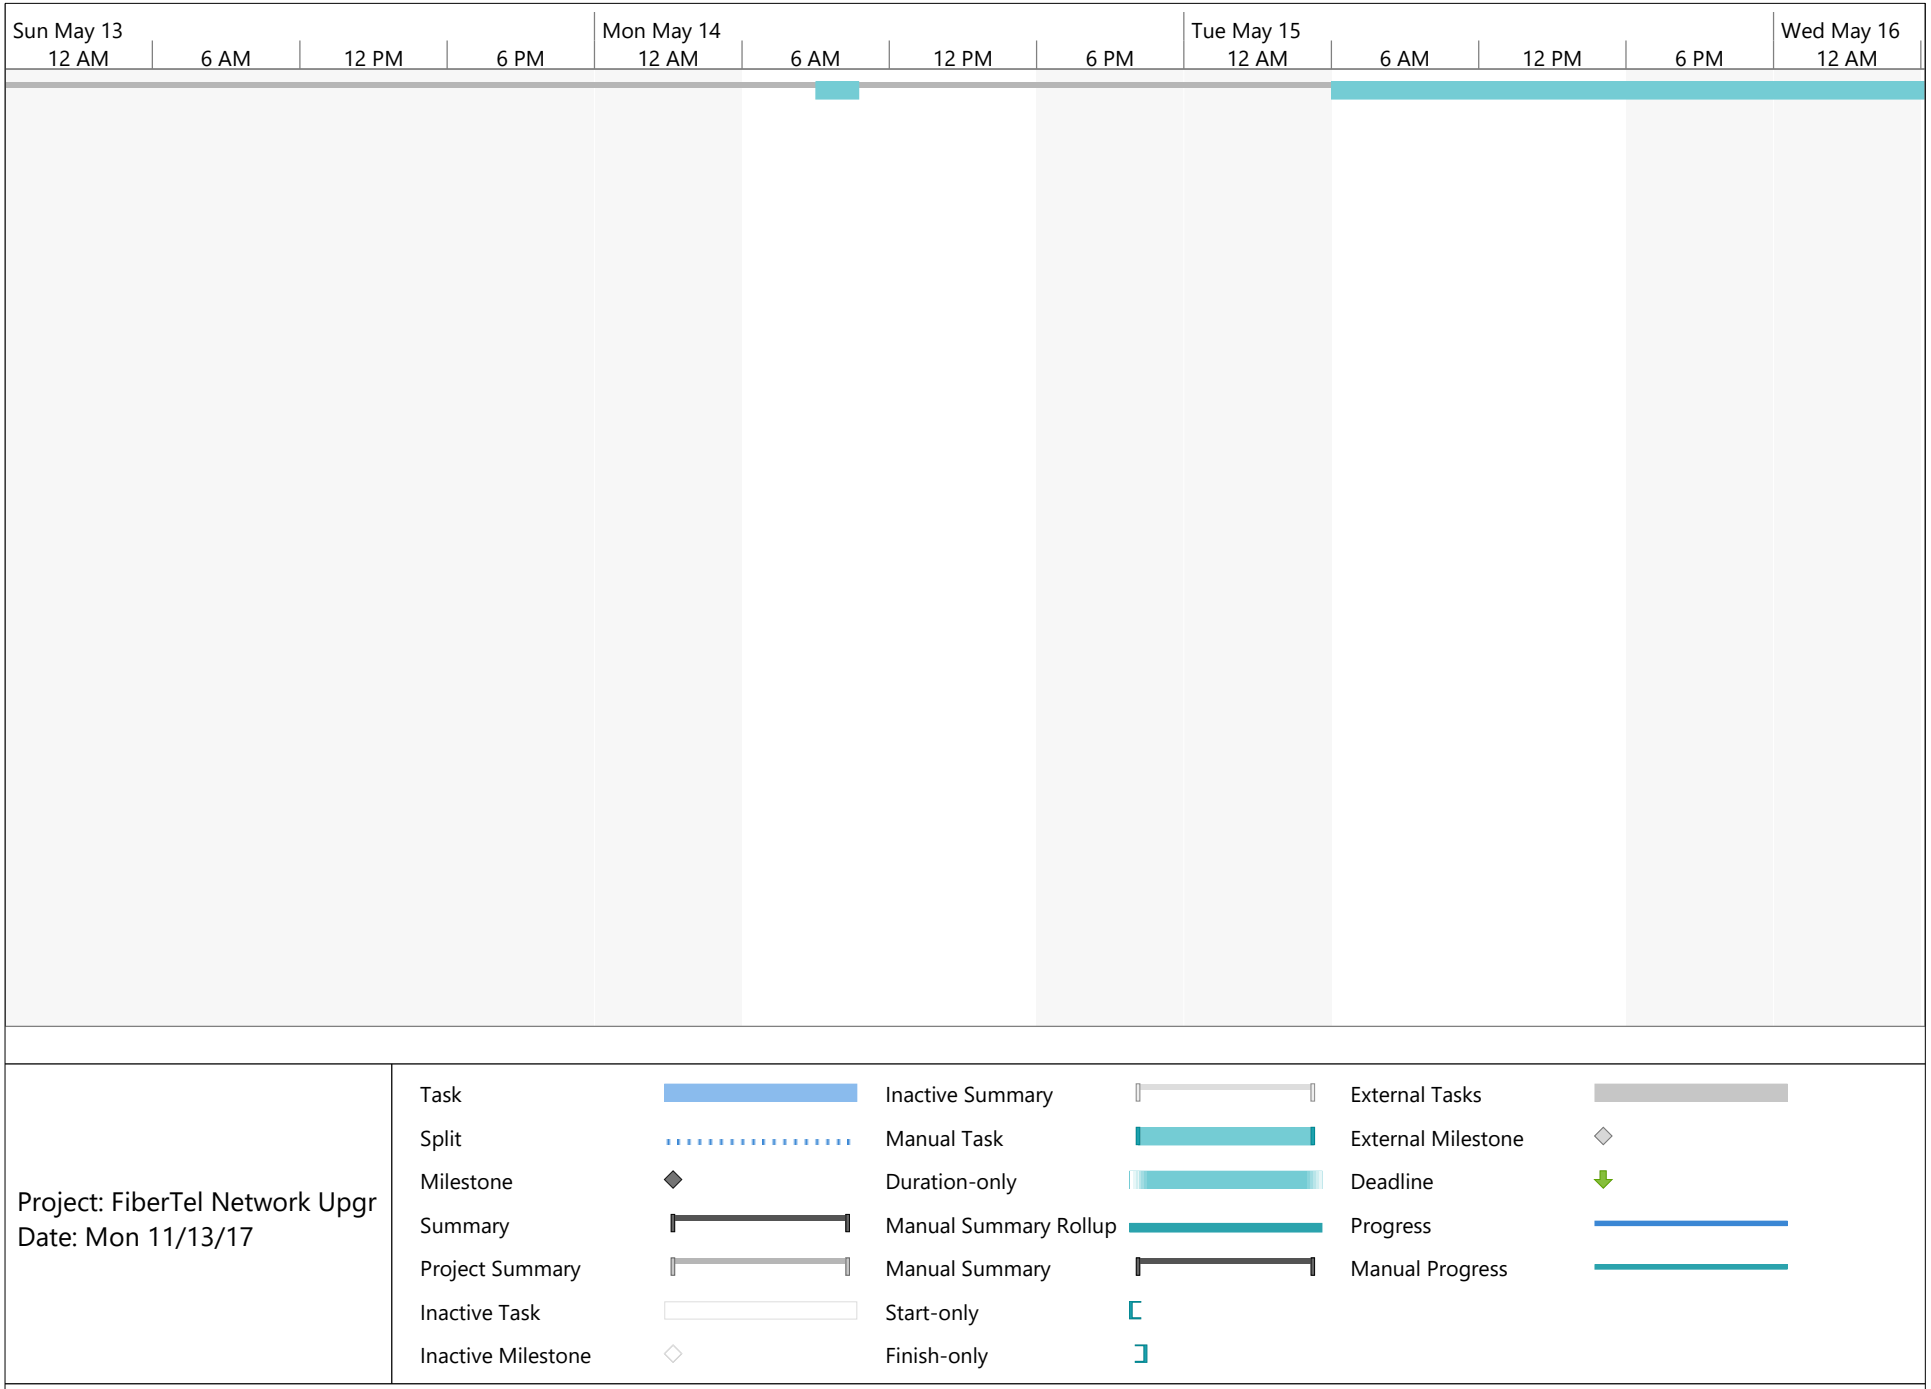

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

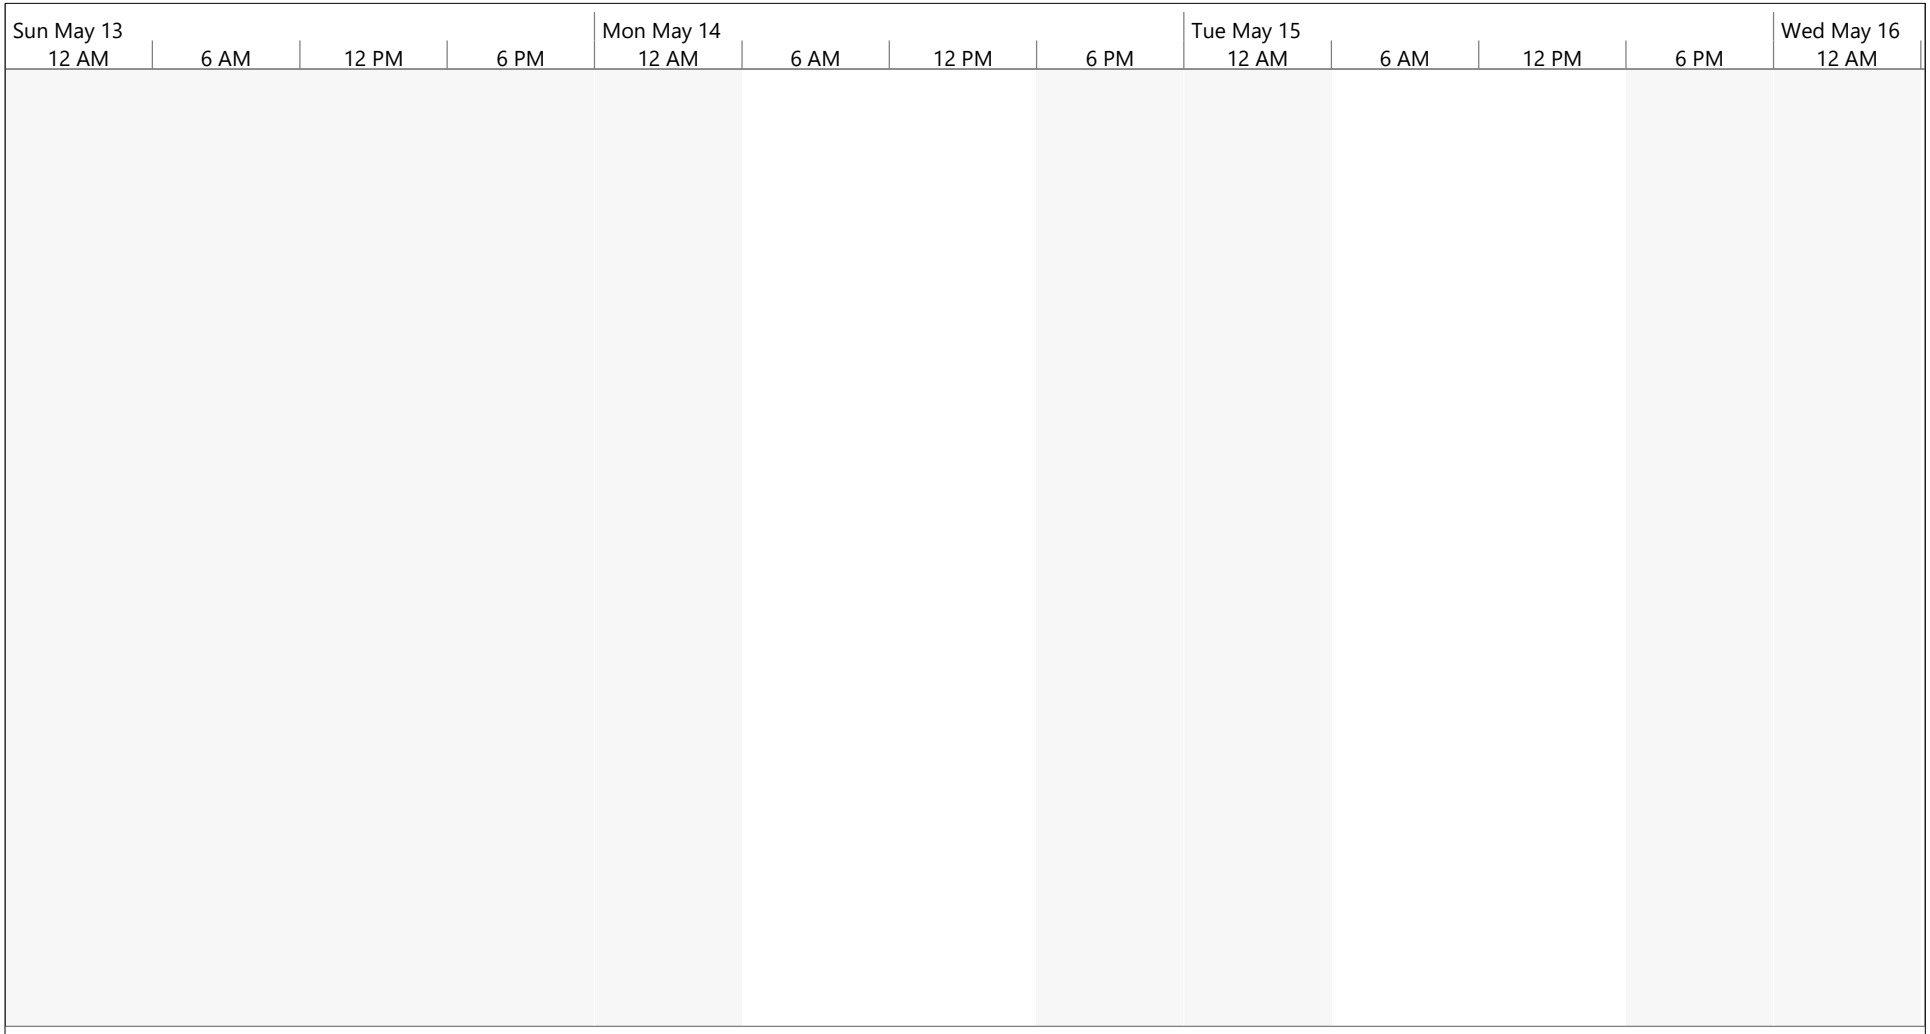

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

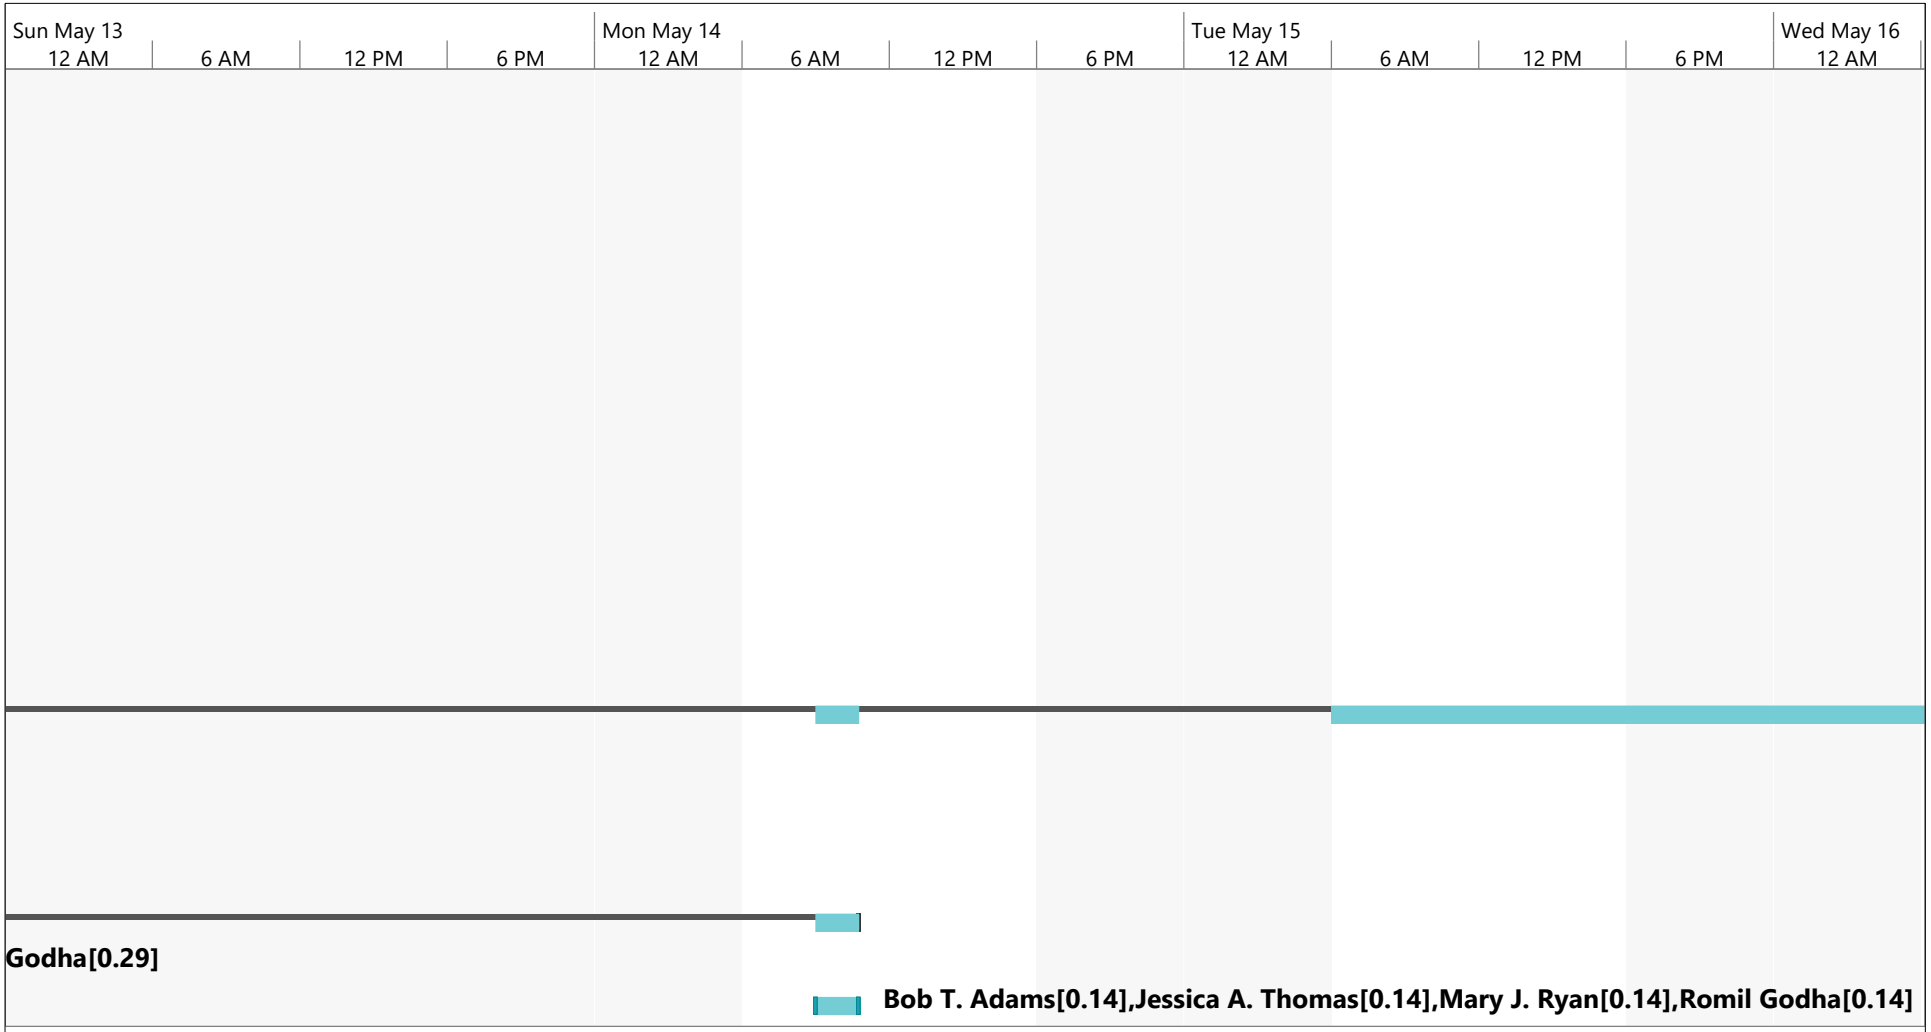

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

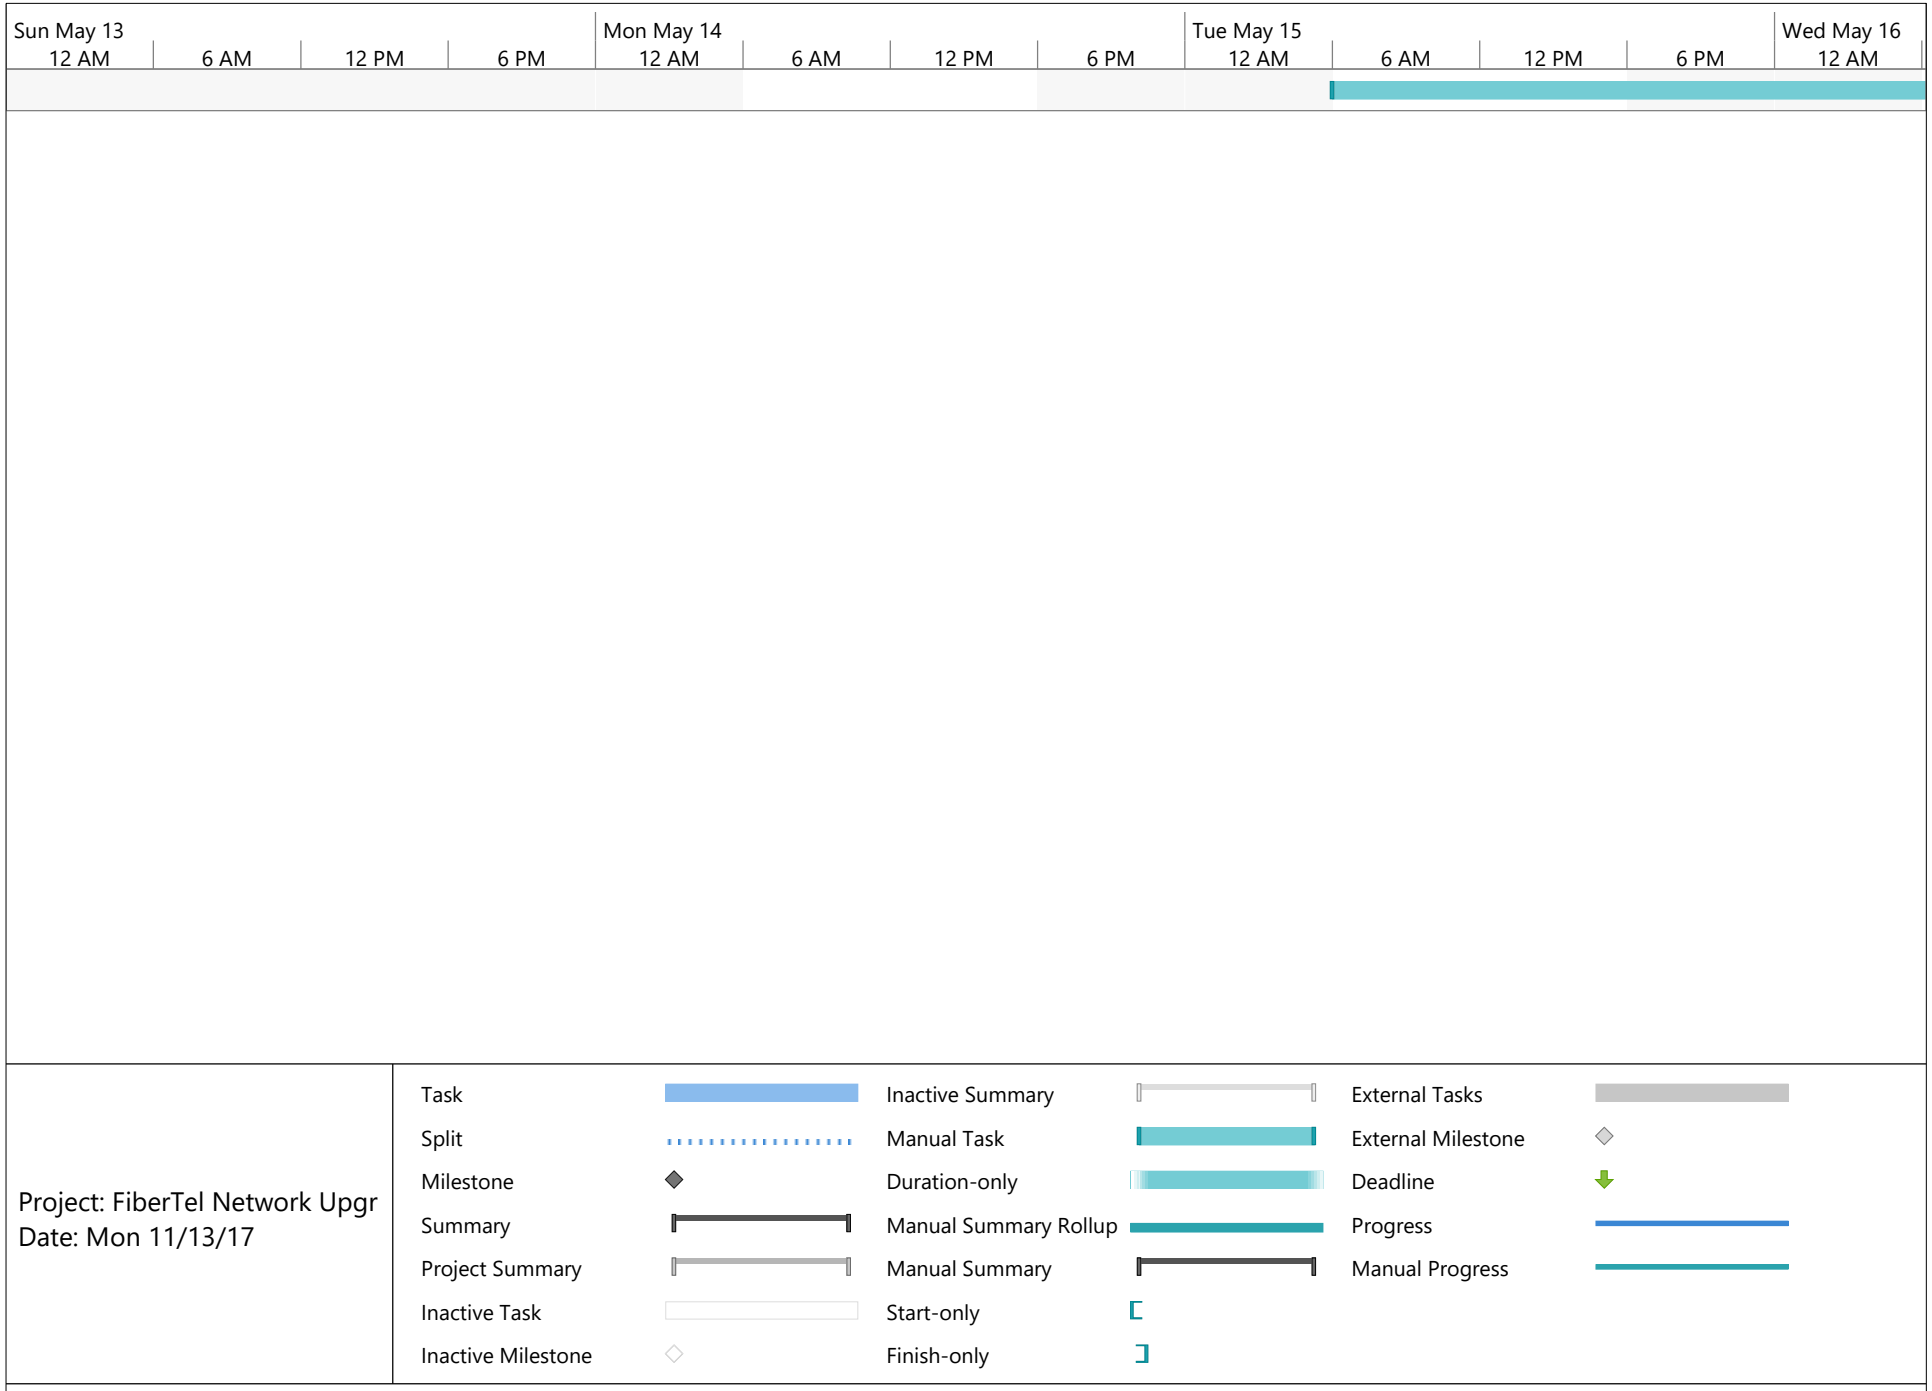
Sun May 13
12 AM
6 AM
12 PM
6 PM
Mon May 14
12 AM
6 AM
12 PM
6 PM
Tue May 15
12 AM
6 AM
12 PM
6 PM
Wed May 16
12 AM
Project: FiberTel Network Upgr
Date: Mon 11/13/17
Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

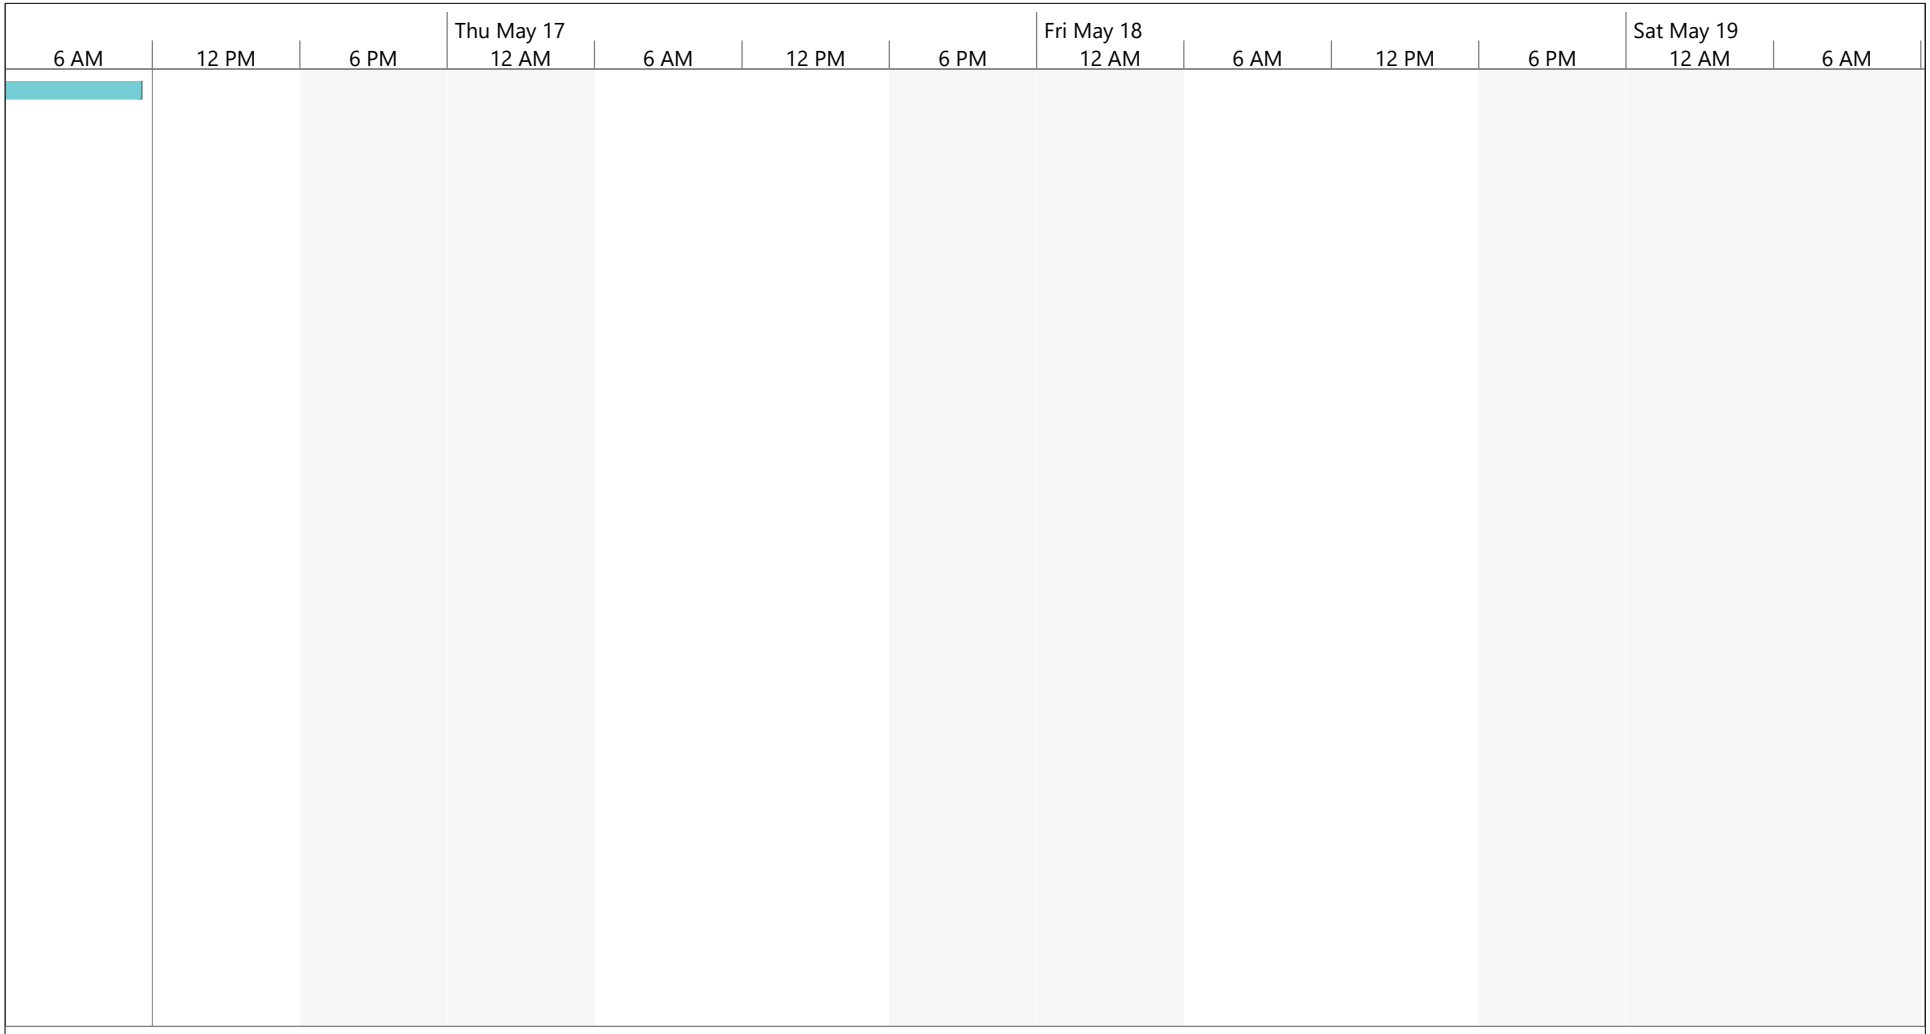

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

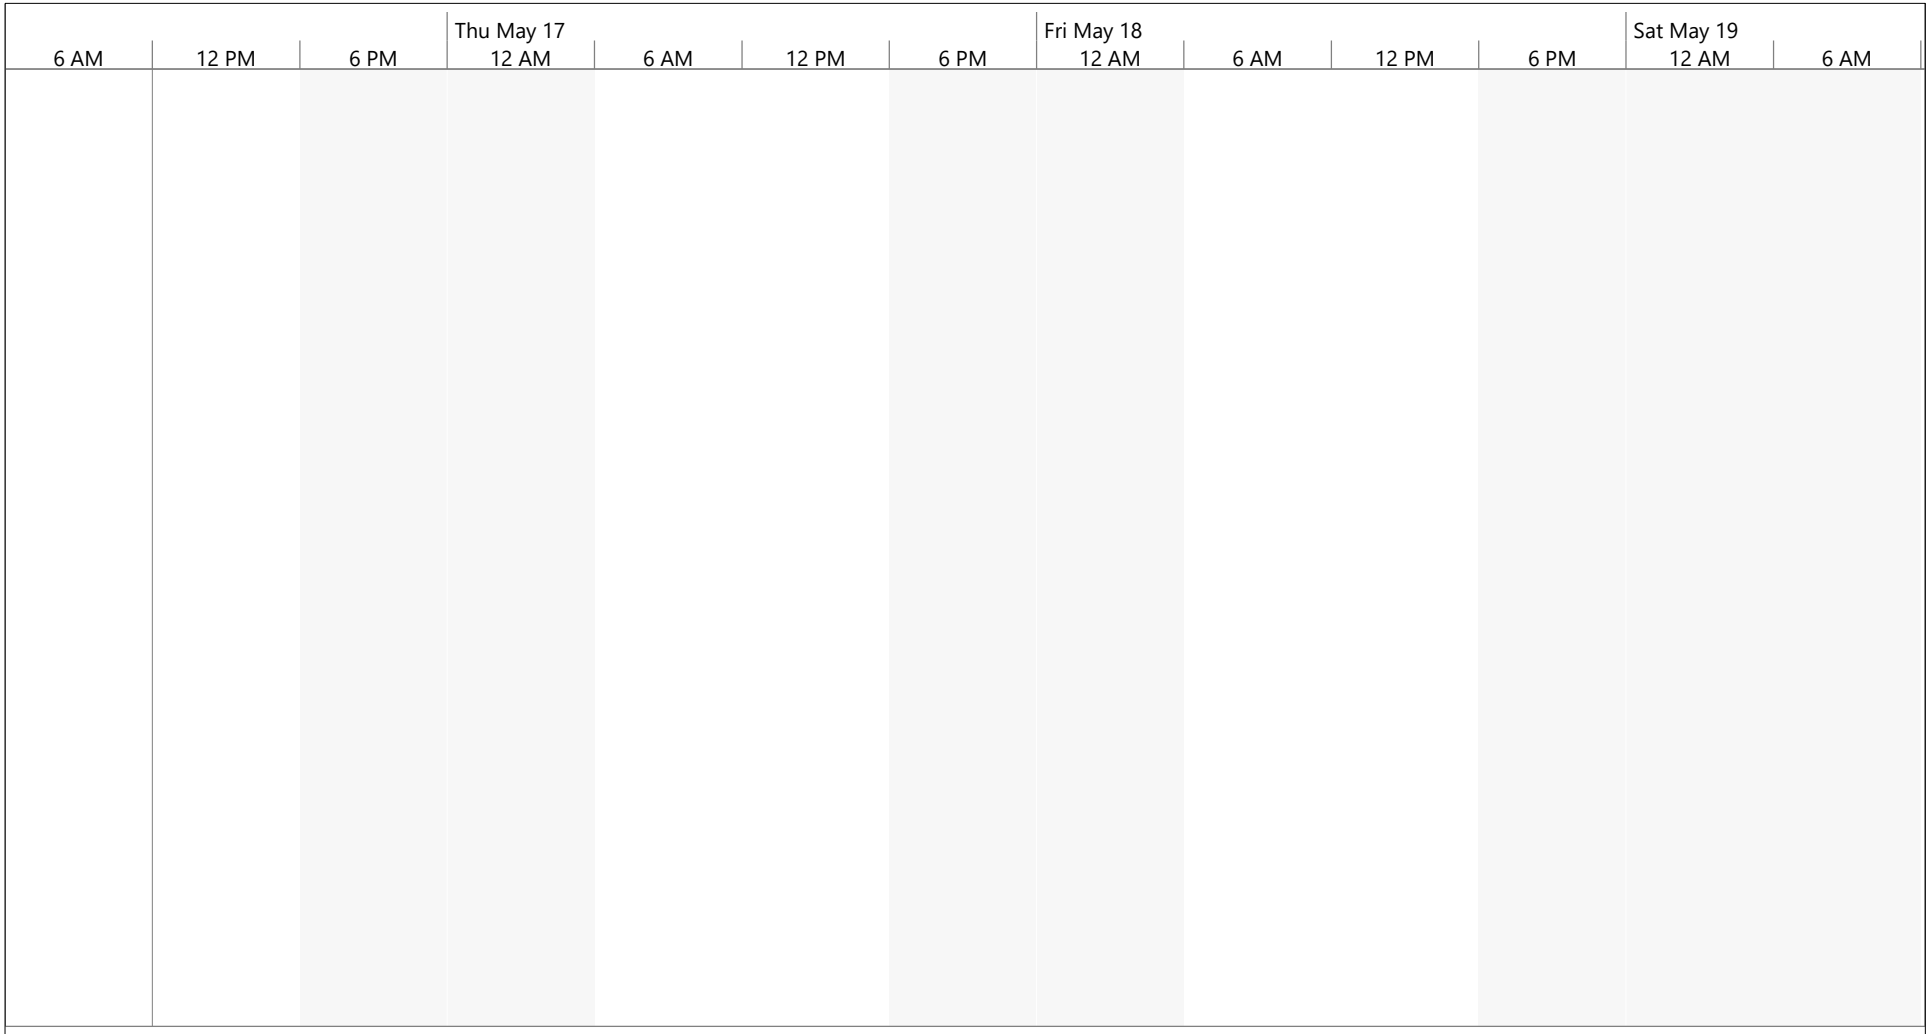

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

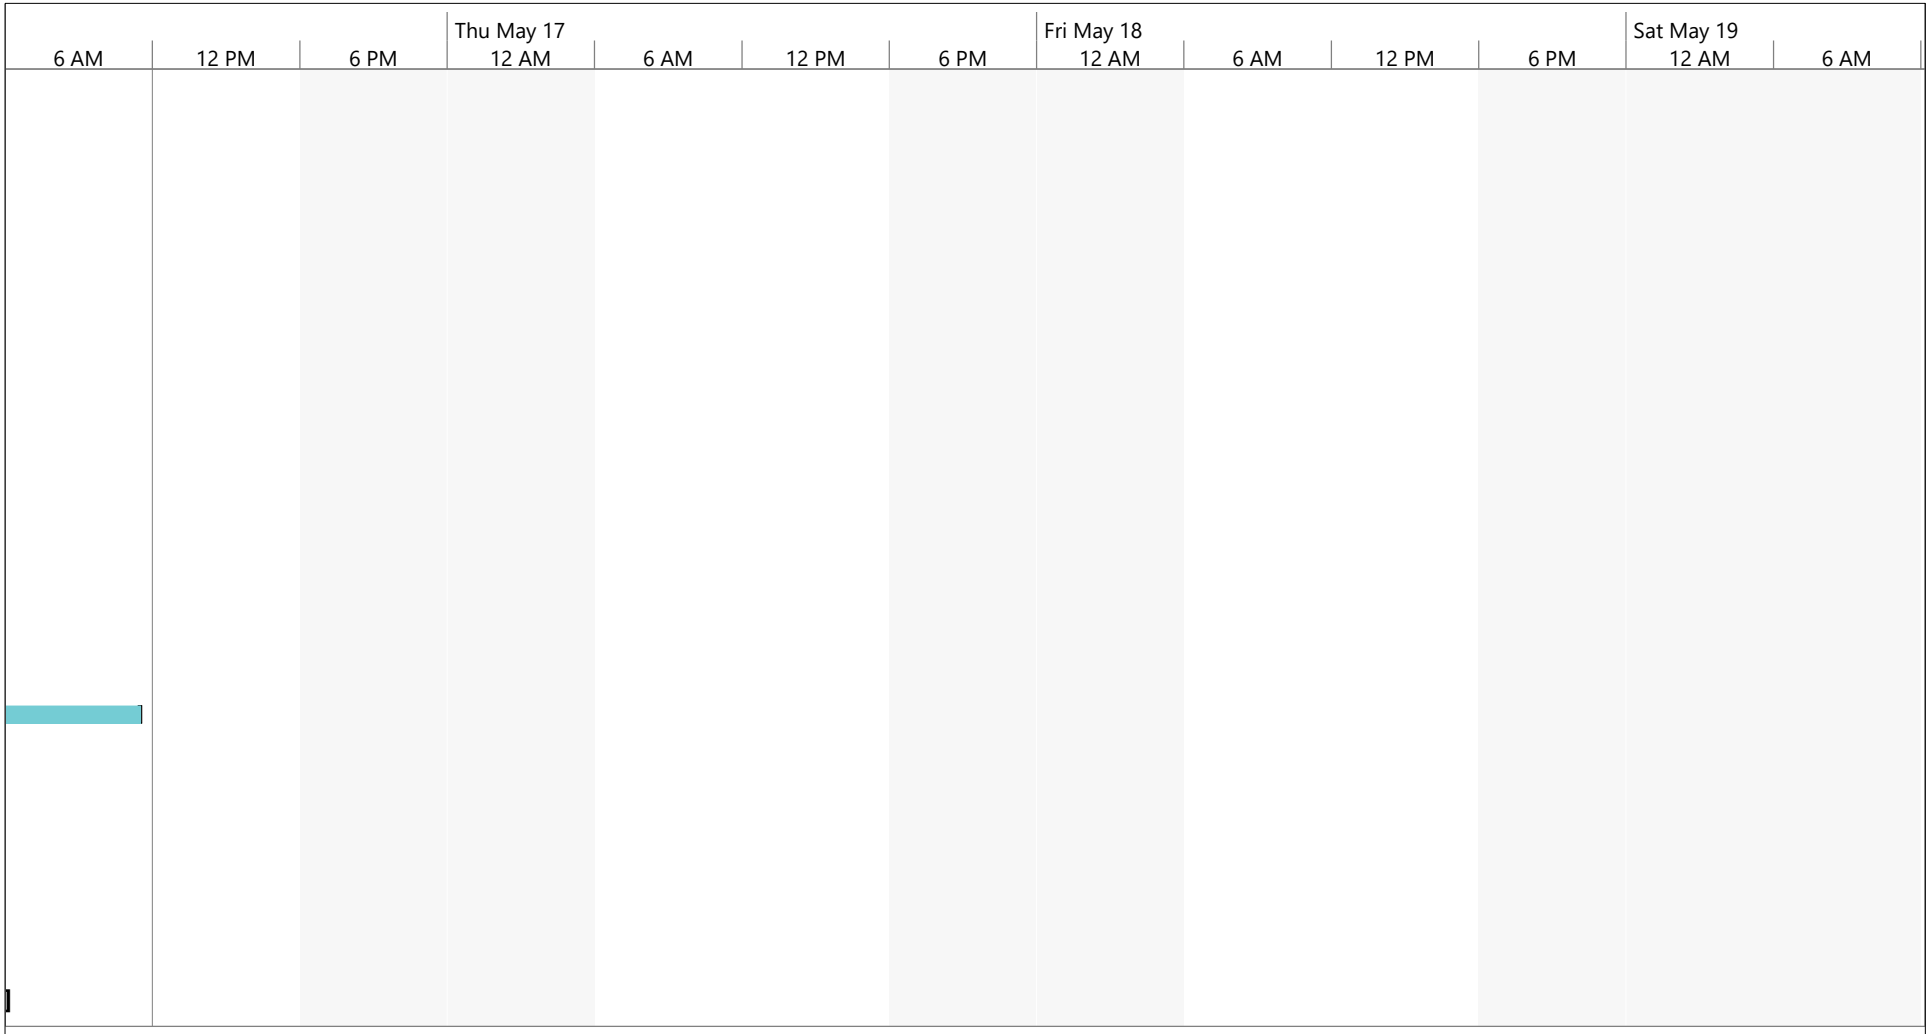

Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: FiberTel Network Upgr
Date: Mon 11/13/17

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
